

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

A28A



FROM: TLMA - Transportation Department


SUBMITTAL DATE:
February 11, 2014

SUBJECT: Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street, and 4th Street in the Unincorporated Community of Mecca, 4th/4th District. [\$1,024,063]; State Funds 13%, Local Funds 87%

RECOMMENDED MOTION: That the Board of Supervisors:

1. Approve three addenda to the plans and specifications issued prior to the December 11, 2013 bid opening; and
2. Accept the low bid of Golden Valley Construction of Palm Springs, CA in the amount of \$1,024,063; and
3. Award the contract to Golden Valley Construction, and authorize the Chairman of the Board to execute the contract documents.

JCP:jjr:sb




Juan C. Perez
Director of Transportation and Land
Management

FORM APPROVED COUNTY COUNSEL
BY:  MARSHAL VICTOR
DATE: 2/11/14
Departmental Concurrence

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost:	POLICY/CONSENT (Per Exec. Office)
COST	\$ 1,024,063	\$ 0	\$ 1,024,063	\$ 0	Consent <input type="checkbox"/> Policy <input checked="" type="checkbox"/>
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0	
SOURCE OF FUNDS: Gas Tax (87%) and State Safe Routes to School Funds (13%). There are no General Funds used in this project.				Budget Adjustment: No	
				For Fiscal Year: 13/14	

C.E.O. RECOMMENDATION:

APPROVE


BY: Tina Grande

County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

- A-30
- Positions Added
- 4/5 Vote
- Change Order

Prev. Agn. Ref.: 11/05/13, Item 3-59

District: 4/4

Agenda Number:

3-34

SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

FORM 11: Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street, and 4th Street in the Unincorporated Community of Mecca, 4th/4th District. [\$1,024,063]; State Funds 13%, Local Funds 87%

DATE: February 11, 2014

PAGE: 2 of 3

BACKGROUND:

Summary

By Minute Order dated November 5, 2013 (Agenda Item 3-59), the Board of Supervisors authorized the Clerk of the Board to advertise for the construction of the Mecca Group 4 Street Improvement Project, including Coahuilla Street, Date Palm Street, and 4th Street in the unincorporated community of Mecca.

During the advertisement period, three addenda were issued to all registered plan holders as a supplement to the plans and specifications. Bidders are required to acknowledge and take into account all issued addenda on their Contractor's Bid in order to be considered for award. The addenda were issued to clarify and modify the approved contract documents. The addenda are attached and designated as Addendum No. 1, Addendum No. 2, and Addendum No. 3.

Seven bids were received on December 11, 2013, ranging from \$1,024,063 to \$1,310,683. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Golden Valley Construction of Palm Springs, CA in the amount of \$1,024,063, which is \$146,698 (13%) less than the Engineer's Estimate.

A letter of bid protest was submitted by the second low bidder for this project. The letter argued that the apparent low bidder did not acknowledge receipt of all addenda and that the bidding documents were not signed by an authorized person; and, therefore, the apparent low bid should be declared as non-responsive. The Transportation Department and County Counsel reviewed the protest and bid documents and determined that the bid documents contained a minor irregularity in form that could be waived, and the documents met the bidding requirements. The bid protester was so notified and stated they would not proceed with their initial protest. Attached is a letter dated December 20, 2013, sent by the Transportation Department, responding to the second low bidder's letter (also included as one of the response attachments).

The bid documents include the following schedules of work:

- Base Bid Schedule A: Coahuilla Street, Stations 20+33 to 30+00
- Base Bid Schedule B: Coahuilla Street, Stations 30+00 to 33+38.26 and Date Palm Street
- Alternate Bid Schedule 1: 4th Street Cul-De-Sac

Award Base Bid Schedule A, Base Bid Schedule B, and Alternate Bid Schedule 1 is recommended.

Between 2010 and 2013, the Transportation Department administered the construction of street improvements throughout downtown Mecca as part of the Redevelopment Agency funded Mecca Street Revitalization Projects – Phases 1, 2, 3, and Roundabout. These projects included the full reconstruction of paved roads and the addition of concrete sidewalks to the streets to eliminate blight and to improve drainage and pedestrian access.

The Mecca Group 4 Street Improvement Project provides a continuation of those improvements in downtown Mecca with the reconstruction of pavement and addition of sidewalks and curb ramps on Coahuilla Street, Date Palm Street, and 4th Street.

The construction duration set for this project is two months, and construction is anticipated to be completed by early summer 2014.

SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

FORM 11: Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street, and 4th Street in the Unincorporated Community of Mecca, 4th/4th District. [\$1,024,063]; State Funds 13%, Local Funds 87%

DATE: February 11, 2014

PAGE: 3 of 3

The contractor is qualified to perform the work as outlined in the bid, has executed the contract, and has provided bonds and insurance documents, which meet the requirements of the contract.

Project No: C1-0654

State Project No: SR2SL-5956(215)

Impact on Residents and Businesses

The project includes the reconstruction of pavement and addition of sidewalks and curbs ramps on Coahuilla Street, Date Palm Street, and 4th Street. These improvements will provide benefits to the community by improving driving surfaces, drainage, and pedestrian access, especially for children who walk to Mecca Elementary School fronting Coahuilla Street and Date Palm Street.

SUPPLEMENTAL:

Additional Fiscal Information

The contract is recommended to be awarded to Golden Valley Construction for the total amount of \$1,024,063. The project will be funded with Gas Tax funds and State Safe Routes to School funds, for which the County of Riverside successfully competed. There are no General Funds used in this project.

The project is expected to be completed within the existing project's budget as shown on Attachment "A."

Contract History and Price Reasonableness



N/A

COUNTY OF RIVERSIDE
DEPARTMENT OF TRANSPORTATION

MECCA GROUP 4 STREET IMPROVEMENT PROJECT

MECCA, CALIFORNIA

PROJECT No. C1-0654

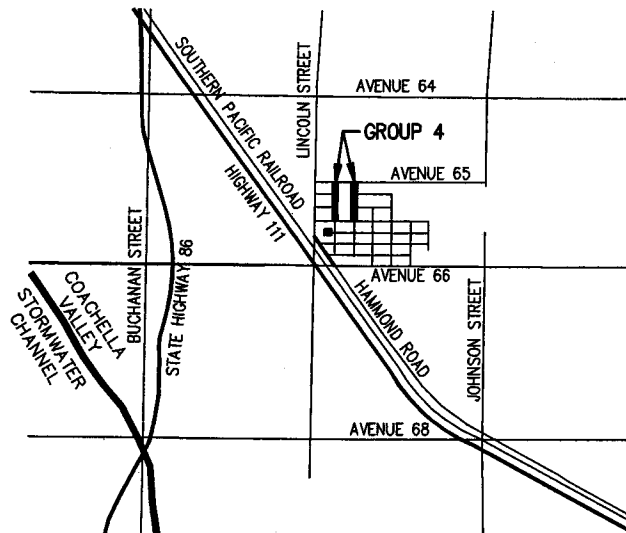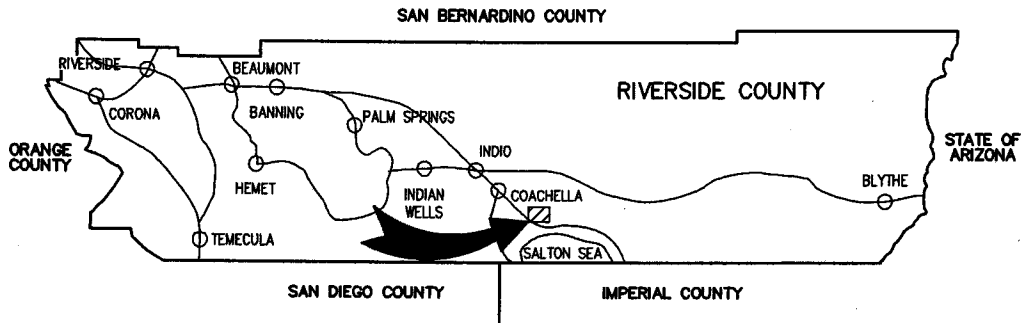

VICINITY MAP

TOWNSHIP 7S RANGE 9E SECTION 8
COUNTY ROAD BOOK PAGE No. 230A

Attachment "A"

Riverside County Transportation Department

1/16/2014

Page 1

Project: **Mecca Group 4 Street Improvement Project**

Project No.(s): **C1-0654**

Project Costs and Budget

Activity	Incurred Costs	Projected Costs	Total Costs	Existing Budget
Preliminary Survey				
Environmental	1,342		1,342	1,000
Design	145,390	20,000	165,390	124,000
Right-of-way				
Utilities				
Construction		1,024,063	1,024,063	1,218,000
Construction Contingency 10%		102,406	102,406	
Construction Engineering & Inspection		150,000	150,000	150,000
Construction Survey	6,100	63,900	70,000	70,000
Totals:	152,832	1,360,369	1,513,201	1,563,000

Project Funding

Code	Name	Existing Budget
221	Gas Tax	1,363,000
258	State Safe Route to Schools	200,000
Totals		1,563,000

Comments

**Riverside County Transportation Department
Summary of Bids**

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

**Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013**

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule A (Coahuilla Street, Sta. 20+33 to 30+00)		COUNTY'S ESTIMATE				Golden Valley Construction Palm Springs, Ca 92262			
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
1	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	29,000.00	29,000.00	10,000.00	10,000.00
2	066102	DUST ABATEMENT	N/A	LS	1	3,500.00	3,500.00	2,500.00	2,500.00
3	170101	DEVELOP WATER SUPPLY	N/A	LS	1	5,000.00	5,000.00	2,000.00	2,000.00
4	074020	WATER POLLUTION CONTROL	N/A	LS	1	3,500.00	3,500.00	1,500.00	1,500.00
5	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	10,000.00	10,000.00	7,000.00	7,000.00
6	000003	TEMPORARY CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	EA	1	1,500.00	1,500.00	1,000.00	1,000.00
7	160101	ROADWAY EXCAVATION	N/A	LS	1	8,000.00	8,000.00	12,000.00	12,000.00
8	190101 (F)	HOT MIX ASPHALT	Like 01	CY	4,100	30.00	123,000.00	9.00	36,900.00
9	390130	CLASS 2 AGGREGATE BASE	Like 02	TON	900	90.00	81,000.00	85.00	76,500.00
10	260201	COLD PLANE EXISTING AC PAVEMENT	Like 03	CY	3,700	35.00	129,500.00	45.00	166,500.00
11	153103	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 04	SQYD	120	15.00	1,800.00	2.00	240.00
12	393001	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 05	SQYD	4,800	8.00	38,400.00	4.50	21,600.00
13	017304	MINOR CONCRETE (TYPE D CURB) (CRS 204)	Like 06	LF	1,610	15.00	24,150.00	25.00	40,250.00
14	017309	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	LF	110	20.00	2,200.00	21.00	2,310.00
15	731521	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 07	SQFT	11,000	4.00	44,000.00	6.75	74,250.00
16	731502	MINOR CONCRETE (DRIVEWAY) (CRS 207)	N/A	SQFT	670	7.00	4,690.00	8.20	5,494.00
17	017315	DRIVEWAY TIE-IN [0.33' PCC]	Like 08	EA	3	3,000.00	9,000.00	1,800.00	5,400.00
18	017315	DRIVEWAY TIE-IN [0.33' PCC]	N/A	EA	1	3,000.00	3,000.00	1,800.00	1,800.00
19	017302	DRIVEWAY TIE-IN [0.33' PCC]	Like 09	SQFT	850	8.00	6,800.00	9.75	8,287.50
20	731516	DRIVEWAY TIE-IN [0.33' PCC]	Like 10	SQFT	5,300	6.00	31,800.00	6.50	34,450.00
21	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	Like 11	SQFT	990	7.00	6,930.00	7.00	6,930.00
22	394002	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	SQFT	110	15.00	1,650.00	4.00	440.00
23	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	20	150.00	3,000.00	140.00	2,800.00
24	000001	ITEM DELETED BY ADDENDUM	---	---	---	---	---	---	---
25	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	860	1.00	860.00	1.15	989.00
26	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	590	4.00	2,360.00	5.00	2,950.00
27	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	3	150.00	450.00	150.00	450.00

**Riverside County Transportation Department
Summary of Bids**

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule A (Continued)		COUNTY'S ESTIMATE				Golden Valley Construction Palm Springs, Ca 92262			
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
28	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	13	250.00	3,250.00	200.00	2,600.00
29	000003	PAINT RED CURB	Like 16	LF	320	6.00	1,920.00	1.00	320.00
30	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	10	100.00	1,000.00	60.00	600.00
Base Bid Sch. A Sub-Total							581,260.00		528,060.50
1									
Base Bid Schedule B		COUNTY'S ESTIMATE				Golden Valley Construction Palm Springs, Ca 92262			
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
31	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	14,000.00	14,000.00	6,000.00	6,000.00
32	066102	DUST ABATEMENT	N/A	LS	1	1,500.00	1,500.00	2,000.00	2,000.00
33	170101	DEVELOP WATER SUPPLY	N/A	LS	1	3,500.00	3,500.00	2,000.00	2,000.00
34	074020	WATER POLLUTION CONTROL	N/A	LS	1	1,500.00	1,500.00	1,500.00	1,500.00
35	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	15,000.00	15,000.00	4,000.00	4,000.00
36	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	3,500.00	3,500.00	8,000.00	8,000.00
37	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	1,000	30.00	30,000.00	9.00	9,000.00
38	390130	HOT MIX ASPHALT	Like 02	TON	850	90.00	76,500.00	85.00	72,250.00
39	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	1,060	35.00	37,100.00	45.00	47,700.00
40	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	5,700	2.50	14,250.00	2.00	11,400.00
41	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	1,400	8.00	11,200.00	4.50	6,300.00
42	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	275	25.00	6,875.00	25.00	6,875.00
43	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	N/A	LF	50	25.00	1,250.00	28.00	1,400.00
44	017304	MINOR CONCRETE (CURB AND GUTTER) (TRANSITION 8" - 6")	N/A	LF	160	25.00	4,000.00	18.00	2,880.00
45	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	2,500	5.00	12,500.00	6.75	16,875.00
46	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	4	3,000.00	12,000.00	1,800.00	7,200.00
47	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B AND PER DETAIL)	N/A	EA	1	3,000.00	3,000.00	1,800.00	1,800.00
48	017315	MINOR CONCRETE (MODIFIED CURB RAMP) (CRS 403 - PER DETAIL)	N/A	EA	1	3,000.00	3,000.00	1,800.00	1,800.00

**Riverside County Transportation Department
Summary of Bids**

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

**Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (1/1/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013**

PROJECT No. C-1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule B (Continued)		COUNTY'S ESTIMATE				Golden Valley Construction Palm Springs, Ca 92262			
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
49	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	1,600	10.00	16,000.00	9.75	15,600.00
50	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	480	10.00	4,800.00	6.50	3,120.00
51	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	100	4.00	400.00	7.00	700.00
52	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC RW	N/A	LF	45	150.00	6,750.00	75.00	3,375.00
53	840856	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	1,050	1.00	1,050.00	1.15	1,207.50
54	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	620	4.00	2,480.00	5.00	3,100.00
55	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	7	150.00	1,050.00	150.00	1,050.00
56	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	9	250.00	2,250.00	200.00	1,800.00
57	000003	PAINT RED CURB	Like 16	LF	640	6.00	3,840.00	1.00	640.00
58	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	6	100.00	600.00	60.00	360.00
59	000003	MISCELLANEOUS DIRECTED WORK	N/A	FA	1	95,000.00	95,000.00	95,000.00	95,000.00
Base Bid Sch. B Sub-Total							384,895.00		334,932.50
Alternate Bid Schedule 1 (4th Street Cul De Sac)		COUNTY'S ESTIMATE				Golden Valley Construction Palm Springs, Ca 92262			
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
60	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	9,800.00	9,800.00	8,000.00	8,000.00
61	066102	DUST ABATEMENT	N/A	LS	1	1,500.00	1,500.00	4,000.00	4,000.00
62	170101	DEVELOP WATER SUPPLY	N/A	LS	1	2,500.00	2,500.00	2,000.00	2,000.00
63	074020	WATER POLLUTION CONTROL	N/A	LS	1	1,500.00	1,500.00	1,500.00	1,500.00
64	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	1,500.00	1,500.00	4,000.00	4,000.00
65	160101	CLEARING AND GRUBBING (INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS)	N/A	LS	1	5,000.00	5,000.00	6,000.00	6,000.00
66	190101 (F)	ROADWAY EXCAVATION	N/A	CY	840	30.00	25,200.00	9.00	7,560.00
67	390130	HOT MIX ASPHALT	N/A	TON	200	90.00	18,000.00	100.00	20,000.00
68	260201	CLASS 2 AGGREGATE BASE	N/A	CY	700	35.00	24,500.00	45.00	31,500.00
69	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	N/A	SQYD	1,100	8.00	8,800.00	6.50	7,150.00

**Riverside County Transportation Department
Summary of Bids**

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

**Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013**

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Alternate Bid Schedule 1 (Continued)		COUNTY'S ESTIMATE					Golden Valley Construction Palm Springs, Ca 92262		
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
70	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	N/A	LF	450	15.00	6,750.00	30.00	13,500.00
71	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	SQFT	2,500	5.00	12,500.00	6.75	16,875.00
72	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	N/A	SQFT	1,275	10.00	12,750.00	8.00	10,200.00
73	000003	DRIVEWAY TIE-IN [0.33' PCC]	N/A	SQFT	390	4.00	1,560.00	8.00	3,120.00
74	510502	MINOR CONCRETE (MINOR STRUCTURE) (CONCRETE U-DRAIN PER DETAIL AND MODIFIED UNDER SIDEWALK DRAIN PER CRS 309)	N/A	LS	1	4,000.00	4,000.00	2,500.00	2,500.00
75	510502	MINOR CONCRETE (MINOR STRUCTURE) (UNDER SIDEWALK DRAIN (24" WIDE) PER CRS 309)	N/A	EA	2	1,200.00	2,400.00	1,500.00	3,000.00
76	000003	CONTAMINATED SOIL MANAGEMENT	N/A	LS	1	5,000.00	5,000.00	5,000.00	5,000.00
77	000003 (F)	CONTAMINATED SOIL MITIGATION/EXPORT	N/A	CY	235	150.00	35,250.00	25.00	5,875.00
78	151281	SALVAGE ROADSIDE SIGN	N/A	EA	3	100.00	300.00	60.00	180.00
79	000003	CHAIN LINK FENCE (6' HIGH)	N/A	LF	94	59.00	5,546.00	40.00	3,760.00
80	000003	REMOVE EXISTING (MISCELLANEOUS)	N/A	LS	1	15,000.00	15,000.00	5,000.00	5,000.00
81	198005	IMPORTED GRANULAR MATERIAL (DECOMPOSED GRANITE)	N/A	CY	7	750.00	5,250.00	50.00	350.00
Alt Bid Sch. 1 Sub-Total							204,606.00		161,070.00
Items 60-81									

Project Total	1,170,761.00	1,024,063.00
Items 1-81		

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule A (Coahuilla Street, Sta. 20+33 to 30+00)		2			3				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
1	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	29,000.00	29,000.00	29,000.00	29,000.00
2	066102	DUST ABATEMENT	N/A	LS	1	30,000.00	30,000.00	2,000.00	2,000.00
3	170101	DEVELOP WATER SUPPLY	N/A	LS	1	5,000.00	5,000.00	5,000.00	5,000.00
4	074020	WATER POLLUTION CONTROL	N/A	LS	1	20,000.00	20,000.00	9,500.00	9,500.00
5	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	82,500.00	82,500.00	8,500.00	8,500.00
6	000003	TEMPORARY CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN CLEARING AND GRUBBING (INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS)	N/A	EA	1	1,000.00	1,000.00	800.00	800.00
7	160101	ROADWAY EXCAVATION	N/A	LS	1	8,000.00	8,000.00	8,000.00	8,000.00
8	190101 (F)	HOT MIX ASPHALT	Like 01	CY	4,100	30.00	123,000.00	21.00	86,100.00
9	390130	CLASS 2 AGGREGATE BASE	Like 02	TON	900	77.00	69,300.00	97.00	87,300.00
10	260201	COLD PLANE EXISTING AC PAVEMENT	Like 03	CY	3,700	30.00	111,000.00	45.00	168,500.00
11	153103	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 04	SQYD	120	2.50	300.00	3.00	360.00
12	393001	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 05	SQYD	4,800	3.00	14,400.00	5.00	24,000.00
13	017304	MINOR CONCRETE (TYPE D CURB) (CRS 204)	Like 06	LF	1,610	17.00	27,370.00	18.00	28,980.00
14	017309	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	LF	110	15.00	1,650.00	30.00	3,300.00
15	731521	MINOR CONCRETE (8" PAVEMENT)	Like 07	SQFT	11,000	3.00	33,000.00	3.25	35,750.00
16	731502	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	N/A	SQFT	670	7.00	4,690.00	10.00	6,700.00
17	017315	MINOR CONCRETE (ADA ACCESSIBLE RAMP) (CRS 403 - CASE A PER DETAIL)	Like 08	EA	3	1,200.00	3,600.00	1,000.00	3,000.00
18	017315	MINOR CONCRETE (GROSS-GUTTER) (CRS 209)	N/A	EA	1	700.00	700.00	1,100.00	1,100.00
19	017302	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 09	SQFT	850	6.00	5,100.00	9.00	7,650.00
20	731516	DRIVEWAY TIE-IN [0.33' PCC]	Like 10	SQFT	5,300	3.50	18,550.00	7.00	37,100.00
21	000003	PLACE ASPHALT CONCRETE (DRIVEWAY TIE-IN)	Like 11	SQFT	990	3.50	3,465.00	5.00	4,950.00
22	394002	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	SQFT	110	5.00	550.00	22.00	2,420.00
23	000003	ITEM DELETED BY ADDENDUM	N/A	LF	20	150.00	3,000.00	27.00	540.00
24	000001	PAINT TRAFFIC STRIPE (2 COAT)	---	---	---	---	---	---	---
25	840656	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 12	LF	860	1.00	860.00	3.00	2,580.00
26	840519	RELOCATE ROADSIDE SIGN	Like 13	SQFT	590	3.80	2,242.00	8.00	4,720.00
27	152390		Like 14	EA	3	100.00	300.00	170.00	510.00

**Riverside County Transportation Department
Summary of Bids**

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

PROJECT No. C1-0654, State Project No. SR25L-5956(215)

Base Bid Schedule A (Continued)		2			3				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
28	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	13	150.00	1,950.00	90.00	1,170.00
29	000003	PAINT RED CURB	Like 16	LF	320	1.00	320.00	5.00	1,600.00
30	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	10	100.00	1,000.00	50.00	500.00
Base Bid Sch. A Sub-Total							601,847.00		569,630.00
Base Bid Schedule B (Coahuilla Street 30+00 to 33+38.26, Date Palm Street 23+38 to 36+40.08)		2			3				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
31	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	14,000.00	14,000.00	14,000.00	14,000.00
32	066102	DUST ABATEMENT	N/A	LS	1	15,000.00	15,000.00	2,000.00	2,000.00
33	170101	DEVELOP WATER SUPPLY	N/A	LS	1	3,500.00	3,500.00	3,500.00	3,500.00
34	074020	WATER POLLUTION CONTROL	N/A	LS	1	7,500.00	7,500.00	3,000.00	3,000.00
35	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	17,500.00	17,500.00	5,500.00	5,500.00
36	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	3,500.00	3,500.00	3,500.00	3,500.00
37	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	1,000	30.00	30,000.00	21.00	21,000.00
38	390130	HOT MIX ASPHALT	Like 02	TON	850	77.00	65,450.00	97.00	82,450.00
39	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	1,060	30.00	31,800.00	45.00	47,700.00
40	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	5,700	2.50	14,250.00	3.00	17,100.00
41	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	1,400	3.00	4,200.00	5.00	7,000.00
42	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	275	17.00	4,675.00	18.00	4,950.00
43	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	N/A	LF	50	15.00	750.00	28.00	1,400.00
44	017304	MINOR CONCRETE (CURB AND GUTTER) (TRANSITION 8" - 6")	N/A	LF	160	20.00	3,200.00	35.00	5,600.00
45	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	2,500	3.00	7,500.00	3.25	8,125.00
46	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	4	1,200.00	4,800.00	1,000.00	4,000.00
47	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B AND PER DETAIL)	N/A	EA	1	750.00	750.00	1,100.00	1,100.00
48	017315	MINOR CONCRETE (MODIFIED CURB RAMP) (CRS 403 - PER DETAIL)	N/A	EA	1	800.00	800.00	1,750.00	1,750.00

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (1/1/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule B (Continued)		2		3					
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
49	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	1,600	6.00	9,600.00	9.00	14,400.00
50	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	480	3.50	1,680.00	7.00	3,360.00
51	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	100	3.50	350.00	5.00	500.00
52	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	45	100.00	4,500.00	65.00	2,925.00
53	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	1,050	1.00	1,050.00	3.00	3,150.00
54	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	620	3.80	2,356.00	8.00	4,960.00
55	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	7	100.00	700.00	170.00	1,190.00
56	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	9	150.00	1,350.00	90.00	810.00
57	000003	PAINT RED CURB	Like 16	LF	640	1.00	640.00	5.00	3,200.00
58	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	6	100.00	600.00	50.00	300.00
59	000003	MISCELLANEOUS DIRECTED WORK	N/A	FA	1	95,000.00	95,000.00	95,000.00	95,000.00
Base Bid Sch.B Sub-Total							347,001.00		363,470.00
Alternate Bid Schedule 1 (4th Street Cul De Sac)		2		3					
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
60	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	9,800.00	9,800.00	9,800.00	9,800.00
61	066102	DUST ABATEMENT	N/A	LS	1	1,000.00	1,000.00	5,500.00	5,500.00
62	170101	DEVELOP WATER SUPPLY	N/A	LS	1	2,500.00	2,500.00	2,500.00	2,500.00
63	074020	WATER POLLUTION CONTROL	N/A	LS	1	500.00	500.00	1,500.00	1,500.00
64	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	2,500.00	2,500.00	800.00	800.00
65	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	5,000.00	5,000.00	5,000.00	5,000.00
66	190101 (F)	ROADWAY EXCAVATION	N/A	CY	840	25.00	21,000.00	21.00	17,640.00
67	390130	HOT MIX ASPHALT	N/A	TON	200	80.00	16,000.00	97.00	19,400.00
68	260201	CLASS 2 AGGREGATE BASE	N/A	CY	700	30.00	21,000.00	45.00	31,500.00
69	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	N/A	SQYD	1,100	3.00	3,300.00	8.00	8,800.00

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (1/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Alternate Bid Schedule 1 (Continued)		2		3						
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE	
70	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	N/A	LF	450	20.00	9,000.00	18.00	8,100.00	
71	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	SQFT	2,500	3.00	7,500.00	3.25	8,125.00	
72	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	N/A	SQFT	1,275	3.50	4,462.50	7.00	8,925.00	
73	000003	DRIVEWAY TIE-IN [0.33' PCC]	N/A	SQFT	390	3.50	1,365.00	5.00	1,950.00	
74	510502	MINOR CONCRETE (MINOR STRUCTURE) (CONCRETE U-DRAIN PER DETAIL AND MODIFIED UNDER SIDEWALK DRAIN PER CRS 309)	N/A	LS	1	3,000.00	3,000.00	2,000.00	2,000.00	
75	510502	MINOR CONCRETE (MINOR STRUCTURE) (UNDER SIDEWALK DRAIN (24" WIDE) PER CRS 309)	N/A	EA	2	3,000.00	6,000.00	1,200.00	2,400.00	
76	000003	CONTAMINATED SOIL MANAGEMENT	N/A	LS	1	10,000.00	10,000.00	6,438.00	6,438.00	
77	000003 (F)	CONTAMINATED SOIL MITIGATION/EXPORT	N/A	CY	235	25.00	5,875.00	98.00	23,030.00	
78	151281	SALVAGE ROADSIDE SIGN	N/A	EA	3	100.00	300.00	60.00	180.00	
79	000003	CHAIN LINK FENCE (6' HIGH)	N/A	LF	94	35.00	3,290.00	23.00	2,162.00	
80	000003	REMOVE EXISTING (MISCELLANEOUS)	N/A	LS	1	1,000.00	1,000.00	10,000.00	10,000.00	
81	198005	IMPORTED GRANULAR MATERIAL (DECOMPSED GRANITE)	N/A	CY	7	200.00	1,400.00	180.00	1,260.00	
Alt Bid Sch. 1 Sub-Total								135,792.50		177,010.00
Items 60-81										

Project Total	1,084,640.50	1,110,110.00
Items 1-81		

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule A (Coahuilla Street, Sta. 20+33 to 30+00)		4			5				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
1	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	20,000.00	20,000.00	37,007.00	37,007.00
2	066102	DUST ABATEMENT	N/A	LS	1	3,500.00	3,500.00	3,300.00	3,300.00
3	170101	DEVELOP WATER SUPPLY	N/A	LS	1	0.00	0.00	580.00	580.00
4	074020	WATER POLLUTION CONTROL	N/A	LS	1	2,800.00	2,800.00	8,900.00	8,900.00
5	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	5,000.00	5,000.00	11,000.00	11,000.00
6	000003	TEMPORARY CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN	N/A	EA	1	1,200.00	1,200.00	920.00	920.00
7	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	7,800.00	7,800.00	7,500.00	7,500.00
8	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	4,100	28.00	114,800.00	44.00	180,400.00
9	390130	HOT MIX ASPHALT	Like 02	TON	900	103.00	92,700.00	105.00	94,500.00
10	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	3,700	45.00	166,500.00	42.00	155,400.00
11	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	120	2.00	240.00	2.00	240.00
12	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	4,800	2.75	13,200.00	3.00	14,400.00
13	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	1,610	28.75	46,287.50	18.00	28,980.00
14	017309	MINOR CONCRETE (TYPE D CURB) (CRS 204)	N/A	LF	110	30.00	3,300.00	14.00	1,540.00
15	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	11,000	3.90	42,900.00	4.50	49,500.00
16	731502	MINOR CONCRETE (8" PAVEMENT)	N/A	SQFT	670	18.75	12,562.50	6.50	4,355.00
17	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	3	2,880.00	8,640.00	1,800.00	5,400.00
18	017315	MINOR CONCRETE (ADA ACCESSIBLE RAMP) (CRS 403 - CASE A PER DETAIL)	N/A	EA	1	3,800.00	3,800.00	1,800.00	1,800.00
19	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	850	10.20	8,670.00	9.50	8,075.00
20	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	5,300	6.01	31,853.00	6.20	32,860.00
21	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	990	6.50	6,435.00	4.50	4,455.00
22	394002	PLACE ASPHALT CONCRETE (DRIVEWAY TIE-IN)	N/A	SQFT	110	8.50	935.00	23.00	2,530.00
23	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	20	50.00	1,000.00	75.00	1,500.00
24	000001	ITEM DELETED BY ADDENDUM	---	---	---	---	---	---	---
25	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	860	2.50	2,150.00	1.50	1,290.00
26	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	590	10.00	5,900.00	4.50	2,655.00
27	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	3	200.00	600.00	205.00	615.00

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule A (Continued)		4			5				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
28	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	13	200.00	2,600.00	305.00	3,965.00
29	000003	PAINT RED CURB	Like 16	LF	320	3.00	960.00	1.25	400.00
30	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	10	100.00	1,000.00	60.00	600.00
Base Bid Sch. A Sub-Total							607,333.00		664,667.00
Base Bid Schedule B		4			5				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
31	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	12,000.00	12,000.00	33,000.00	33,000.00
32	066102	DUST ABATEMENT	N/A	LS	1	3,500.00	3,500.00	3,300.00	3,300.00
33	170101	DEVELOP WATER SUPPLY	N/A	LS	1	3,400.00	3,400.00	285.00	285.00
34	074020	WATER POLLUTION CONTROL	N/A	LS	1	4,900.00	4,900.00	8,500.00	8,500.00
35	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	2,800.00	2,800.00	5,500.00	5,500.00
36	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	3,499.00	3,499.00	2,300.00	2,300.00
37	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	1,000	28.00	28,000.00	44.00	44,000.00
38	390130	HOT MIX ASPHALT	Like 02	TON	850	103.00	87,550.00	105.00	89,250.00
39	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	1,060	45.00	47,700.00	42.00	44,520.00
40	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	5,700	2.00	11,400.00	2.00	11,400.00
41	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	1,400	2.75	3,850.00	3.00	4,200.00
42	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	275	28.75	7,906.25	18.00	4,950.00
43	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	N/A	LF	50	30.00	1,500.00	21.00	1,050.00
44	017304	MINOR CONCRETE (CURB AND GUTTER) (TRANSITION 8" - 6")	N/A	LF	160	28.75	4,600.00	23.00	3,680.00
45	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	2,500	3.90	9,750.00	4.50	11,250.00
46	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	4	2,880.00	11,520.00	1,800.00	7,200.00
47	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B AND PER DETAIL)	N/A	EA	1	3,200.00	3,200.00	1,400.00	1,400.00
48	017315	MINOR CONCRETE (MODIFIED CURB RAMP) (CRS 403 - PER DETAIL)	N/A	EA	1	3,500.00	3,500.00	1,500.00	1,500.00

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule B (Continued)		4			5				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
49	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	1,600	10.20	16,320.00	9.50	15,200.00
50	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	480	6.01	2,884.80	6.20	2,976.00
51	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	100	6.50	650.00	4.50	450.00
52	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	45	35.00	1,575.00	75.00	3,375.00
53	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	1,050	2.50	2,625.00	1.50	1,575.00
54	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	620	10.00	6,200.00	4.50	2,790.00
55	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	7	200.00	1,400.00	205.00	1,435.00
56	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	9	200.00	1,800.00	305.00	2,745.00
57	000003	PAINT RED CURB	Like 16	LF	640	3.00	1,920.00	1.25	800.00
58	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	6	100.00	600.00	60.00	360.00
59	000003	MISCELLANEOUS DIRECTED WORK	N/A	FA	1	95,000.00	95,000.00	95,000.00	95,000.00
Base Bid Sch.B Sub-Total							381,550.05		403,991.00
Alternate Bid Schedule 1 (4th Street Cul De Sac)		4			5				
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
60	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	5,000.00	5,000.00	2,000.00	2,000.00
61	066102	DUST ABATEMENT	N/A	LS	1	3,500.00	3,500.00	1,750.00	1,750.00
62	170101	DEVELOP WATER SUPPLY	N/A	LS	1	2,100.00	2,100.00	115.00	115.00
63	074020	WATER POLLUTION CONTROL	N/A	LS	1	2,800.00	2,800.00	500.00	500.00
64	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	2,100.00	2,100.00	2,800.00	2,800.00
65	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	4,850.00	4,850.00	2,800.00	2,800.00
66	190101 (F)	ROADWAY EXCAVATION	N/A	CY	840	31.00	26,040.00	35.00	29,400.00
67	390130	HOT MIX ASPHALT	N/A	TON	200	120.00	24,000.00	105.00	21,000.00
68	260201	CLASS 2 AGGREGATE BASE	N/A	CY	700	45.00	31,500.00	40.00	28,000.00
69	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	N/A	SQYD	1,100	2.75	3,025.00	3.00	3,300.00

**Riverside County Transportation Department
Summary of Bids**

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Alternate Bid Schedule 1 (Continued)		4		5					
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
70	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	N/A	LF	450	30.50	13,725.00	18.00	8,100.00
71	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	SQFT	2,500	4.50	11,250.00	5.00	12,500.00
72	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	N/A	SQFT	1,275	6.50	8,287.50	7.00	8,925.00
73	000003	DRIVEWAY TIE-IN [0.33' PCC]	N/A	SQFT	390	6.50	2,535.00	5.00	1,950.00
74	510502	MINOR CONCRETE (MINOR STRUCTURE) (CONCRETE U-DRAIN PER DETAIL AND MODIFIED UNDER SIDEWALK DRAIN PER CRS 309)	N/A	LS	1	3,700.00	3,700.00	4,100.00	4,100.00
75	510502	MINOR CONCRETE (MINOR STRUCTURE) (UNDER SIDEWALK DRAIN (24" WIDE) PER CRS 309)	N/A	EA	2	3,500.00	7,000.00	2,300.00	4,600.00
76	000003	CONTAMINATED SOIL MANAGEMENT	N/A	LS	1	1,800.00	1,800.00	4,000.00	4,000.00
77	000003 (F)	CONTAMINATED SOIL MITIGATION/EXPORT	N/A	CY	235	60.00	14,100.00	70.00	16,450.00
78	151281	SALVAGE ROADSIDE SIGN	N/A	EA	3	100.00	300.00	86.00	258.00
79	000003	CHAIN LINK FENCE (6' HIGH)	N/A	LF	94	35.00	3,290.00	51.00	4,794.00
80	000003	REMOVE EXISTING (MISCELLANEOUS)	N/A	LS	1	2,000.00	2,000.00	8,200.00	8,200.00
81	198005	IMPORTED GRANULAR MATERIAL (DECOMPOSED GRANITE)	N/A	CY	7	100.00	700.00	97.00	679.00
Alt Bid Sch. 1 Sub-Total							173,602.50		166,221.00

Items 60-81

Project Total	1,162,485.55	1,234,879.00
Items 1-81		

**Riverside County Transportation Department
Summary of Bids**

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

**Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013**

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule A (Coahuilla Street, Sta. 20+33 to 30+00)		6				7			
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
1	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	29,000.00	29,000.00	18,826.00	18,826.00
2	066102	DUST ABATEMENT	N/A	LS	1	12,600.00	12,600.00	12,181.00	12,181.00
3	170101	DEVELOP WATER SUPPLY	N/A	LS	1	5,000.00	5,000.00	884.00	884.00
4	074020	WATER POLLUTION CONTROL	N/A	LS	1	9,900.00	9,900.00	2,395.00	2,395.00
5	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	30,000.00	30,000.00	10,607.00	10,607.00
6	000003	TEMPORARY CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN	N/A	EA	1	1,720.00	1,720.00	1,264.00	1,264.00
7	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	8,000.00	8,000.00	7,033.00	7,033.00
8	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	4,100	40.00	164,000.00	29.00	118,900.00
9	390130	HOT MIX ASPHALT	Like 02	TON	900	87.00	78,300.00	132.00	118,800.00
10	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	3,700	29.30	108,410.00	38.70	143,190.00
11	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	120	2.56	307.20	2.61	313.20
12	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	4,800	7.40	35,520.00	6.62	31,776.00
13	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	1,610	24.40	39,284.00	23.50	37,835.00
14	017309	MINOR CONCRETE (TYPE D CURB) (CRS 204)	N/A	LF	110	20.50	2,255.00	21.40	2,354.00
15	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	11,000	5.00	55,000.00	5.19	57,090.00
16	731502	MINOR CONCRETE (8" PAVEMENT)	N/A	SQFT	670	9.70	6,499.00	13.80	9,246.00
17	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	3	1,900.00	5,700.00	2,126.00	6,378.00
18	017315	MINOR CONCRETE (ADA ACCESSIBLE RAMP) (CRS 403 - CASE A PER DETAIL)	N/A	EA	1	1,470.00	1,470.00	2,533.00	2,533.00
19	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	860	13.70	11,645.00	10.04	8,534.00
20	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	5,300	4.30	22,790.00	7.78	41,234.00
21	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	990	4.46	4,415.40	7.30	7,227.00
22	394002	PLACE ASPHALT CONCRETE (DRIVEWAY TIE-IN)	N/A	SQFT	110	14.00	1,540.00	24.00	2,640.00
23	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	20	190.00	3,800.00	77.00	1,540.00
24	000001	ITEM DELETED BY ADDENDUM	---	---	---	---	---	---	---
25	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	860	2.20	1,892.00	1.50	1,290.00
26	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	590	5.00	2,950.00	6.00	3,540.00
27	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	3	176.00	528.00	148.00	444.00

**Riverside County Transportation Department
Summary of Bids**

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule A (Continued)		6			7					
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE	
28	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	13	360.00	4,680.00	184.00	2,392.00	
29	000003	PAINT RED CURB	Like 16	LF	320	2.20	704.00	1.50	480.00	
30	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	10	27.50	275.00	71.00	710.00	
Base Bid Sch. A Sub-Total							648,184.60		651,636.20	
Items 1-30					6			7		
Base Bid Schedule B (Coahuilla Street 30+00 to 33+38.26, Date Palm Street 23+38 to 36+40.08)		6			7					
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE	
31	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	14,000.00	14,000.00	18,826.00	18,826.00	
32	066102	DUST ABATEMENT	N/A	LS	1	12,600.00	12,600.00	12,181.00	12,181.00	
33	170101	DEVELOP WATER SUPPLY	N/A	LS	1	3,500.00	3,500.00	884.00	884.00	
34	074020	WATER POLLUTION CONTROL	N/A	LS	1	9,900.00	9,900.00	2,394.00	2,394.00	
35	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	26,500.00	26,500.00	10,607.00	10,607.00	
36	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	3,500.00	3,500.00	7,033.00	7,033.00	
37	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	1,000	40.00	40,000.00	29.00	29,000.00	
38	390130	HOT MIX ASPHALT	Like 02	TON	850	87.00	73,950.00	132.00	112,200.00	
39	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	1,060	29.30	31,058.00	38.70	41,022.00	
40	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	5,700	2.56	14,592.00	2.61	14,877.00	
41	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	1,400	7.40	10,360.00	6.62	9,268.00	
42	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	275	24.40	6,710.00	23.50	6,462.50	
43	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	N/A	LF	50	19.00	950.00	24.02	1,201.00	
44	017304	MINOR CONCRETE (CURB AND GUTTER) (TRANSITION 8" - 6")	N/A	LF	160	24.00	3,840.00	24.45	3,912.00	
45	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	2,500	5.00	12,500.00	5.19	12,975.00	
46	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	4	1,900.00	7,600.00	2,126.00	8,504.00	
47	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B AND PER DETAIL)	N/A	EA	1	1,470.00	1,470.00	2,523.00	2,523.00	
48	017315	MINOR CONCRETE (MODIFIED CURB RAMP) (CRS 403 - PER DETAIL)	N/A	EA	1	1,540.00	1,540.00	2,533.00	2,533.00	

**Riverside County Transportation Department
Summary of Bids**

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Base Bid Schedule B (Continued)				6			7		
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
49	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	1,600	13.70	21,920.00	10.04	16,064.00
50	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	480	4.30	2,064.00	7.78	3,734.40
51	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	100	4.46	446.00	7.30	730.00
52	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC RW	N/A	LF	45	114.00	5,130.00	77.00	3,465.00
53	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	1,050	2.20	2,310.00	1.50	1,575.00
54	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	620	5.00	3,100.00	6.00	3,720.00
55	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	7	176.00	1,232.00	148.00	1,036.00
56	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	9	360.00	3,240.00	184.00	1,656.00
57	000003	PAINT RED CURB	Like 16	LF	640	2.20	1,408.00	1.50	960.00
58	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	6	27.50	165.00	71.00	426.00
59	000003	MISCELLANEOUS DIRECTED WORK	N/A	FA	1	95,000.00	95,000.00	95,000.00	95,000.00
Base Bid Sch. B Sub-Total							410,585.00		424,768.90
Alternate Bid Schedule 1 (4th Street Cul De Sac)				6			7		
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
60	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	9,800.00	9,800.00	15,055.00	15,055.00
61	066102	DUST ABATEMENT	N/A	LS	1	2,160.00	2,160.00	12,181.00	12,181.00
62	170101	DEVELOP WATER SUPPLY	N/A	LS	1	2,500.00	2,500.00	884.00	884.00
63	074020	WATER POLLUTION CONTROL	N/A	LS	1	4,100.00	4,100.00	2,394.00	2,394.00
64	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	2,550.00	2,550.00	3,210.00	3,210.00
65	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	5,000.00	5,000.00	4,514.00	4,514.00
66	190101 (F)	ROADWAY EXCAVATION	N/A	CY	840	65.00	54,600.00	29.00	24,360.00
67	390130	HOT MIX ASPHALT	N/A	TON	200	90.00	18,000.00	157.50	31,500.00
68	260201	CLASS 2 AGGREGATE BASE	N/A	CY	700	31.00	21,700.00	39.19	27,433.00
69	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	N/A	SQYD	1,100	9.30	10,230.00	6.42	7,062.00

**Riverside County Transportation Department
Summary of Bids**

Advertised: November 5, 2013 (Agenda Item: 3-59)
Addenda: 1 (11/20/2013), 2 (12/4/2013), 3 (12/5/2013)
Bids Open: 2 pm Date: Wednesday, December 11, 2013

PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

PROJECT No. C1-0654, State Project No. SR2SL-5956(215)

Alternate Bid Schedule 1 (Continued)		6			7					
ITEM NO.	ITEM CODE	CONTRACT ITEM	LIKE BID ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE	
70	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	N/A	LF	450	26.30	11,835.00	25.54	11,493.00	
71	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	SQFT	2,500	7.30	18,250.00	5.19	12,975.00	
72	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	N/A	SQFT	1,275	5.30	6,757.50	8.20	10,455.00	
73	000003	DRIVEWAY TIE-IN [0.33' PCC]	N/A	SQFT	390	5.20	2,028.00	9.00	3,510.00	
74	510502	MINOR CONCRETE (MINOR STRUCTURE) (CONCRETE U-DRAIN PER DETAIL AND MODIFIED UNDER SIDEWALK DRAIN PER CRS 309)	N/A	LS	1	3,800.00	3,800.00	3,698.00	3,698.00	
75	510502	MINOR CONCRETE (MINOR STRUCTURE) (UNDER SIDEWALK DRAIN (24" WIDE) PER CRS 309)	N/A	EA	2	3,800.00	7,600.00	4,202.00	8,404.00	
76	000003	CONTAMINATED SOIL MANAGEMENT	N/A	LS	1	5,500.00	5,500.00	6,081.00	6,081.00	
77	000003 (F)	CONTAMINATED SOIL MITIGATION/EXPORT	N/A	CY	235	110.00	25,850.00	137.00	32,195.00	
78	151281	SALVAGE ROADSIDE SIGN	N/A	EA	3	38.50	115.50	59.00	177.00	
79	000003	CHAIN LINK FENCE (6' HIGH)	N/A	LF	94	53.00	4,982.00	59.00	5,546.00	
80	000003	REMOVE EXISTING (MISCELLANEOUS)	N/A	LS	1	12,700.00	12,700.00	9,611.00	9,611.00	
81	198005	IMPORTED GRANULAR MATERIAL (DECOMPOSED GRANITE)	N/A	CY	7	660.00	4,620.00	220.00	1,540.00	
Alt Bid Sch. 1 Sub-Total							234,678.00		234,278.00	
Items 60-81								1,293,447.60		1,310,683.10

Project Total	1,293,447.60	1,310,683.10
Items 1-81		

For Internal Use Only

**Riverside County Transportation Department
Bid Evaluation**

**PROJECT: Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
PROJECT No. C1-0654, State Project No. SR2SL-6956(215)**

Advertised: November 5, 2013 Agenda Item No. 3-59
Bids Opened: 2:00 pm Date: December 11, 2013
Estimated Award: February 11, 2014

Project Manager: Cathy Wampler

County's Estimate: Base Bid Sch. A: \$ 581,260.00
 Base Bid Sch. B: \$ 384,895.00
 Alt Bid Sch. 1: \$ 204,606.00
 Total (BaseA+BaseB+Alt1): \$ 1,170,761.00

BIDDING CONTRACTORS	BIDS	DIFFERENCE	
		AMOUNT	%
1 Golden Valley Construction Palm Springs, Ca 92262	Base Bid Sch. A: \$ 528,060.50	\$ (53,199.50)	-9.15%
	Base Bid Sch. B: \$ 334,932.50	\$ (49,962.50)	-12.98%
	Alt Bid Sch. 1: \$ 161,070.00	\$ (43,536.00)	-21.28%
	Total (BaseA+BaseB+Alt1): \$ 1,024,063.00	\$ (146,698.00)	-12.53%
2 Hazard Construction Co. San Diego, Ca 92121	Base Bid Sch. A: \$ 601,847.00	\$ 20,587.00	3.54%
	Base Bid Sch. B: \$ 347,001.00	\$ (37,894.00)	-9.85%
	Alt Bid Sch. 1: \$ 135,792.50	\$ (68,813.50)	-33.63%
	Total (BaseA+BaseB+Alt1): \$ 1,084,640.50	\$ (86,120.50)	-7.36%
3 Granite Construction Co. Indio, Ca 92203	Base Bid Sch. A: \$ 569,630.00	\$ (11,630.00)	-2.00%
	Base Bid Sch. B: \$ 363,470.00	\$ (21,425.00)	-5.57%
	Alt Bid Sch. 1: \$ 177,010.00	\$ (27,596.00)	-13.49%
	Total (BaseA+BaseB+Alt1): \$ 1,110,110.00	\$ (60,651.00)	-5.18%
4 Kad Paving Co. Yucaipa, Ca 92399	Base Bid Sch. A: \$ 607,333.00	\$ 26,073.00	4.49%
	Base Bid Sch. B: \$ 381,550.05	\$ (3,344.95)	-0.87%
	Alt Bid Sch. 1: \$ 173,602.50	\$ (31,003.50)	-15.15%
	Total (BaseA+BaseB+Alt1): \$ 1,162,485.55	\$ (8,275.45)	-0.71%
5 Mamco Inc. dba Alabbasi Riverside, CA 92504	Base Bid Sch. A: \$ 664,667.00	\$ 83,407.00	14.35%
	Base Bid Sch. B: \$ 403,991.00	\$ 19,096.00	4.96%
	Alt Bid Sch. 1: \$ 166,221.00	\$ (38,385.00)	-18.76%
	Total (BaseA+BaseB+Alt1): \$ 1,234,879.00	\$ 64,118.00	5.48%
6 Cooley Construction Hesperia, Ca 92340	Base Bid Sch. A: \$ 648,184.60	\$ 66,924.60	11.51%
	Base Bid Sch. B: \$ 410,585.00	\$ 25,690.00	6.67%
	Alt Bid Sch. 1: \$ 234,678.00	\$ 30,072.00	14.70%
	Total (BaseA+BaseB+Alt1): \$ 1,293,447.60	\$ 122,686.60	10.48%
7 C. S. Legacy Construction Chino, Ca 91710	Base Bid Sch. A: \$ 651,636.20	\$ 70,376.20	12.11%
	Base Bid Sch. B: \$ 424,768.90	\$ 39,873.90	10.36%
	Alt Bid Sch. 1: \$ 234,278.00	\$ 29,672.00	14.50%
	Total (BaseA+BaseB+Alt1): \$ 1,310,683.10	\$ 139,922.10	11.95%
Average Bid	Base Bid Sch. A: \$ 610,194.04	\$ 28,934.04	4.98%
	Base Bid Sch. B: \$ 380,899.78	\$ (3,995.22)	-1.04%
	Alt Bid Sch. 1: \$ 183,236.00	\$ (21,370.00)	-10.44%
	Total (BaseA+BaseB+Alt1): \$ 1,174,329.82	\$ 3,568.82	0.30%

LOW BID / AVERAGE BID VS. ENGINEER ESTIMATE COMPARISONS (Total Base Bid)

Low Bidder Comparison:	\$ (146,698.00)	-12.5%	BELOW
Average Bid Comparison:	\$ 3,568.82	0.30%	ABOVE

LOW BID VS. ENGINEER ESTIMATE EVALUATION

It is desired that the lowest responsible bid be as close as possible to the engineer's estimate. The target range for the low responsive and responsible bid is between 10% below the engineer's estimate and 5% over the engineer's estimate. Bids outside this range should be evaluated.

5% Above:	\$ 1,229,299.05		
10% Below:	\$ 1,053,684.90		Low Bid: \$ 1,024,063.00
Within Standard Range:			NO

EVALUATION COMMENTS

A total of 7 bids were submitted. The bids received range from \$1,024,063 to \$1,310,683.10

Golden Valley Construction, Inc. (Golden Valley) of Palm Springs, CA is the apparent low bidder. Their bid is \$146,698 (12.53%) below the Engineer's Estimate. During the bid review, no major errors were discovered. However their bid has few Like Bid Items corrections. The total amount written on their bid was \$1,029,049, and after making corrections the total went down to \$1,024,063. Golden Valley Construction will be notified about the change in Intent to Award Letter.

Golden Valley has not worked on any County's public works projects in the past, therefore their references will be checked upon receipt. They are requested to provide minimum 5 references of similar nature public works project. Their reference provided a mixed response.

Golden Valley has a combination of bid items above and below Engineer's Estimate. In comparison with Engineer's Estimate, Golden Valley did not bid any item to be considered as significantly BELOW or ABOVE the engineer's estimate. Golden Valley bid the following fifteen items which are more than 50% under the Engineer's Estimate prices: Item# 1, 3, 4, 8, 11, 22, 29, 31, 35, 37, 52, 57, 77, 80, and 81. On the other hand Golden Valley bid the following nine items which are more than 50% above the Engineer's Estimate prices: Item# 7, 13, 15, 36, 51, 61, 64, 70, and 100. Resident Inspector and Project Manager are advised to be extra vigilant when change order is required for these items. Following bid items are major contributors in this contract.

Following 10 items contribute 59% of the total cost of the project.

Bid Item No.	Contract Item	Eng'r Estimate	Avg. Bid	Low Bidder	Eng. Est Vs. Low Bidder % Difference
8	ROADWAY EXCAVATION	123,000.00	117,728.57	36,900.00	70% Below Engr. Estimate, & contribute 3.6%
9	HOT MIX ASPHALT	81,000.00	88,200.00	76,500.00	5.6% Below Engr. Estimate, & contribute 7.47%
10	CLASS 2 AGGREGATE BASE	129,500.00	145,357.14	166,500.00	28% Above Engr. Estimate, & contribute 16.26%
12	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	38,400.00	22,128.00	21,600.00	43.8% Below Engr. Estimate, & contribute 3.1%
13	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	24,150.00	35,569.50	40,250.00	66.7% Above Engr. Estimate, & contribute 3.9%
15	MINOR CONCRETE (SIDEWALK) (CRS 401)	44,000.00	49,641.43	74,250.00	68.8% Below Engr. Estimate, & contribute 7.3%
20	MINOR CONCRETE (DRIVEWAY) (CRS 207)	31,800.00	31,262.43	34,450.00	8.3% above Engr. Estimate, & contribute 3.36%
38	HOT MIX ASPHALT	7,650.00	83,300.00	72,250.00	5.6% Below Engr. Estimate, & contribute 7.1%
39	CLASS 2 AGGREGATE BASE	37,100.00	41,642.86	47,700.00	28.6% above Engr. Estimate, & contribute 4.7%
68	CLASS 2 AGGREGATE BASE	24,500.00	27,519.00	31,500.00	28.6% above Engr. Estimate, & contribute 3.1%
				601,900.00	

PROJECT TOTAL:

1,024,063.00

58.78%

Alternate Bids:

This project has 2 base bid schedules and 1 alternate bid. The items of work listed in alternate bid schedule was also for the County. It was separated due to funding reasons. Alternate bid will be included in the contract for award.

Un Balance Bid Review:

Each bid item was looked at carefully, their bid has several bid items which are below and above the Engineer's estimate pricing. However the overall bid is 5% below the Engineer's estimate, therefore minor irregularities are waivable. Even though the costs of some bid items are considerably higher than the Engr's Estimate the overall effect on the total project cost is minimal. The overall bid is 5% below the Engr's Estimate and there are no bid items where the contractor can take advantage of front loading. Therefore the bid is seems acceptable to the County. Project Manager and Resident Engineer are advised to be extra vigilant about the bid items which are significantly higher than the Engineer's Estimate when construction change orders are required.

Bid Irregularities:

There were no bid major bid Irregularities found on any of the received bids, however there were some minor irregularities which can be waived per contract documents.

Iran Contracting Act:

Golden Valley and all subs were checked on the Department of General Services Procurement Division list and none of the name found in that list.

Partial Payment Restrictions:

The "Partial Payments" special provision was included for this project. Since Golden Valley Construction bid "Clearing and Grubbing" bid item in all three schedules of work above the maximum listed price on page 3 of Special Provisions, therefore partial payment restriction is applicable to "Clearing and Grubbing" bid item.

Golden Valley is responsive and responsible. This contract will be awarded to Golden Valley Construction in the total amount of \$1,024,063. This is a total for the All bid schedules.

-SB

Additional Project Information

**Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

**Project No. C1-0654
State Project No. – SR2SL-5956(215)**

Working Days

30

Liquidated Damages

\$ 3,000 per calendar day*

Project Manager:

Catherine M. Wampler


Project Engineers:

The Altum Group

Assistant Project Engineer:

Mike Heath

* In addition to the liquidated damages set forth above, the first lift of asphalt concrete paving shall be placed within seven (7) calendar days of the removal of existing asphalt concrete for each street segment. A street segment is hereby defined as that area of road removed in one (1) day. Contractor shall pay to the County of Riverside the sum of **\$800.00 per day**, for each and every calendar day's delay in completing paving within the number of calendar days prescribed above, for each street segment subjected to delay, and shall apply separately to each street segment within the scope of work.



COUNTY OF RIVERSIDE TRANSPORTATION AND LAND MANAGEMENT AGENCY



Juan C. Perez, P.E., T.E.
Director of Transportation

Transportation Department

ADDENDUM NUMBER 1

Dated November 20, 2013

to the
Specifications and Contract Documents
for the construction of

Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Project No. C1-0654
State Project No. SR2SL-5956(215)

Bids Due: Wednesday, December 4, 2013; 2:00 PM
14th Street Transportation Annex
3525 14th Street; Riverside, CA 92501
(951) 955-6780

This Addendum is issued pursuant to the Instructions to Bidders, Item No. 8, of the Contract Documents for the reference project. This Addendum is issued as a supplement to the specification and special provisions for the referenced project. The revisions to the specifications shall become a part of the Contract Documents, and each bidder shall acknowledge receipt thereof on the Contractor's Bid. Bidders are directed to sign this addendum as acknowledged, and attach the signed addendum to the contractor's submitted Bid.

Note: During the advertisement period of this project, this document and attachments (if any) are available upon request at the office of the Transportation Department, and are available as a free download at the Transportation Department's website:

http://www.rctlma.org/trans/con_bid_advertisements.html

MODIFICATIONS / CLARIFICATIONS TO SPECIAL PROVISIONS:

Item 1: Revised Proposal.

Refer to "Proposal" pages B2-B5. Proposal pages B2 through B5 are deleted and replaced with revised Proposal issued with this addendum as **Attachment "A"**. The following changes have been made to the Proposal:

- a. The following bid item has been deleted from Base Bid Schedule A:
 - Item 24, "IMPORTED GRANULAR MATERIAL (DECOMPOSED GRANITE)"
- b. The following bid item has been added to Alternate Bid Schedule 1:
 - Item 81, "IMPORTED GRANULAR MATERIAL (DECOMPOSED GRANITE)"

See Attachment "A" Revised Proposal

Item 2: Liquidated Damages.

Refer to Section, "Liquidated Damages" on page 2 of the Special Provisions. Following additional Liquidated Damages are added to this provision and made part thereof.

Additional Liquidated Damages for Coahuilla Street Improvements between 5th Street and 65th Street:

In addition to the Liquidated damages set forth in Special Provision as referenced above, refer to Special Provisions section entitled "Traffic Requirements" included in this addendum for additional Liquidated Damages.

Item 3: Modified hours of Work.

The following Special Provisions are added and made part hereof:

MODIFIED HOURS OF WORK:

Hours of work as stated elsewhere in the Special Provisions are modified below and applied to this project. These hours of work shall be considered as regular working hours as described below:

Working hours shall be between 7:00 a.m. and 7:00 p.m. from Monday through Friday. Additionally, Working hours shall be between 7:00 a.m. and 7:00 p.m., including Saturdays and Sundays, during the week of **Saturday March 22, 2014 through Sunday, March 30, 2014**. This provision for extended hours applies to Coahuilla Street only and does not supersede the other provisions of the contract.

Item 4: Traffic Requirements.

The following Special Provisions are added and made part hereof:

TRAFFIC REQUIREMENTS:

The project is adjacent to Mecca Elementary School, which is located in the block bounded by Coahuilla Street to the west, Date Palm Street to the east, 5th Street to the south, and 65th Avenue to the north.

In order to minimize disturbance to the school, the Contractor is encouraged to complete the improvements in front of the school on Coahuilla Street as quickly as possible. The Contractor is permitted to work 7:00 a.m. to 7:00 p.m. The Contractor may be permitted to work Saturdays and/or Sundays if approved by the Engineer. No night construction will be allowed due to the impact of noise on the adjacent residential neighborhood. This provision for extended hours applies to Coahuilla Street only and does not supersede the other provisions of the contract.

The school's spring break is the week of March 24, 2014. **The Contractor is directed to use the days between Saturday March 22, 2014 and Sunday, March 30, 2014 to perform all road excavation, aggregate base installation, and concrete curb,**

gutter, and sidewalk construction on Coahuilla Street between 5th Street and 65th Avenue before school resumes on Monday, March 31, 2014. No road excavation on Coahuilla Street will begin prior to March 22, 2014. The Contractor will pay to the County of Riverside **liquidated damages in the amount of \$5,000.00 per calendar day** for each and every calendar day delay in completing the work as described herein. (Easter is April 20, 2014.)

To avoid impacts from construction of both the school's frontage streets, the Contractor shall not perform construction on Coahuilla Street and Date Palm Street at the same time.

School hours are 8:06 a.m. to 2:36 p.m. on Mondays, Tuesdays, Thursdays and Fridays, and 8:06 a.m. to 1:36 p.m. Wednesdays.

The Contractor will cease activities and will provide two crossing guards (one for Coahuilla Street and one for Date Palm Street) during the following peak traffic times listed below. The crossing guards will be persons with a basic understanding of traffic safety and with the ability to direct children to cross the street. Crossing guards will wear safety vests and use "stop" paddles. Crossing guards are required for following times and days:

7:40 a.m. to 8:10 a.m. Mondays through Fridays

2:20 p.m. to 2:50 p.m. Mondays, Tuesdays, Thursdays, and Fridays

1:20 p.m. to 1:50 p.m. Wednesdays

The Contractor will maintain accessible pedestrian paths to the school at all times.

The school operates a bus loading and unloading zone off Date Palm Street near 7th Street. The Contractor will maintain unobstructed access for buses during bus drop-off and pick-up times.

The Contractor, its subcontractors and material suppliers will not park their trucks, equipment or employee personal vehicles adjacent to the school in locations where parents need to park to pick-up/drop-off their school children.

As a point of information, the church at the corner of Coahuilla Street and 6th Street distributes food to the needy on Fridays and generates significant traffic between the approximate hours of 6:00 a.m. and 11:00 a.m.


The Contractor, its subcontractors and suppliers will access the project site from 62nd Avenue along the route of Lincoln Street between 5th Street and 62nd Avenue. Heavy equipment trucks will not access the project site through the roundabout located at Hammond Road and 4th Street.


Payment:

Full compensation for complying with the Traffic Control requirements stated herein shall be considered as included in the contract lump sum price paid for Traffic Control System and no additional compensation will be allowed therefor.

Addendum No. 1
Mecca Group 4 Street Improvement Project
Project No. C1-0654, State Project No. CML-5956(215)
November 20, 2013
Page 4 of 5

This addendum has been prepared under the direction of the following registered Civil Engineer(s):


James Ron Bazua, PE



Recommended by:



Catherine M. Wampler, PE
County Project Manager

Concurrence:



11/20/13

Khalid Nasim, PE
Engineering Division Manager

Acknowledged: _____ **Date:** _____

(Contractor)

JRJ:jrj:sb

Note: Refer to Instruction to Bidders Item No. 8, "Addenda". Submission of all addendum pages and non-bidding document attachments of addendum are not necessary for Bid submittal. Submittal of this acknowledgement page is adequate for Bid reception. Bidders are reminded to list addendum number(s) received on the first page of the Bid form (Proposal).

**Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca
Project No. C1-0654
State Project No. SR2SL-5956(215)**

PROPOSAL (Revised)**Base Bid Schedule A (Coahuilla Street 20+33 to 30+00)**

ITEM No.	ITEM CODE	ITEM	Like Bid Item*	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
1	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1		
2	066102	DUST ABATEMENT	N/A	LS	1		
3	170101	DEVELOP WATER SUPPLY	N/A	LS	1		
4	074020	WATER POLLUTION CONTROL	N/A	LS	1		
5	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1		
6	000003	TEMPORARY CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN	N/A	EA	1		
7	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1		
8	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	4,100		
9	390130	HOT MIX ASPHALT	Like 02	TON	900		
10	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	3,700		
11	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	120		
12	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	4,800		
13	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	1,610		
14	017309	MINOR CONCRETE (TYPE D CURB) (CRS 204)	N/A	LF	110		
15	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	11,000		
16	731502	MINOR CONCRETE (8" PAVEMENT)	N/A	SQFT	670		
17	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	3		
18	017315	MINOR CONCRETE (ADA ACCESSIBLE RAMP) (CRS 403 - CASE A PER DETAIL)	N/A	EA	1		
19	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	850		
20	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	5,300		
21	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	990		
22	394002	PLACE ASPHALT CONCRETE (DRIVEWAY TIE-IN)	N/A	SQFT	110		
23	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	20		
24	000001	ITEM DELETED BY ADDENDUM	---	---	---	---	---
25	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	860		
26	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	590		
27	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	3		

PROPOSAL (Revised)

Base Bid Schedule A (Continued)

ITEM No.	ITEM CODE	ITEM	Like Bid Item*	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
28	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	13		
29	000003	PAINT RED CURB	Like 16	LF	320		
30	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	10		

BASE BID SCH. A

SUB-TOTAL:

ITEMS 1-30

"WORDS"

\$

Base Bid Schedule B (Coahuilla Street 30+00 to 33+38.26, Date Palm Street 23+38 to 36+40.08)

ITEM No.	ITEM CODE	ITEM	Like Bid Item*	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
31	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1		
32	066102	DUST ABATEMENT	N/A	LS	1		
33	170101	DEVELOP WATER SUPPLY	N/A	LS	1		
34	074020	WATER POLLUTION CONTROL	N/A	LS	1		
35	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1		
36	160101	CLEARING AND GRUBBING (INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS)	N/A	LS	1		
37	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	1,000		
38	390130	HOT MIX ASPHALT	Like 02	TON	850		
39	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	1,060		
40	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	5,700		
41	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	1,400		
42	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	275		
43	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	N/A	LF	50		
44	017304	MINOR CONCRETE (CURB AND GUTTER) (TRANSITION 8" - 6")	N/A	LF	160		
45	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	2,500		
46	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	4		
47	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B AND PER DETAIL)	N/A	EA	1		
48	017315	MINOR CONCRETE (MODIFIED CURB RAMP) (CRS 403 - PER DETAIL)	N/A	EA	1		
49	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	1,600		

PROPOSAL (Revised)**Base Bid Schedule B (Continued)**

ITEM No.	ITEM CODE	ITEM	Like Bid Item*	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
50	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	480		
51	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	100		
52	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	45		
53	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	1,050		
54	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	620		
55	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	7		
56	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	9		
57	000003	PAINT RED CURB	Like 16	LF	640		
58	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	6		
59	000003	MISCELLANEOUS DIRECTED WORK	N/A	FA	1	95,000.00	95,000.00

BASE BID SCH. B

SUB-TOTAL:

ITEMS 31-59

"WORDS"

\$

Alternate Bid Schedule 1 (4th Street Cul De Sac)

ITEM No.	ITEM CODE	ITEM	Like Bid Item*	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
60	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1		
61	066102	DUST ABATEMENT	N/A	LS	1		
62	170101	DEVELOP WATER SUPPLY	N/A	LS	1		
63	074020	WATER POLLUTION CONTROL	N/A	LS	1		
64	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1		
65	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1		
66	190101 (F)	ROADWAY EXCAVATION	N/A	CY	840		
67	390130	HOT MIX ASPHALT	N/A	TON	200		
68	260201	CLASS 2 AGGREGATE BASE	N/A	CY	700		
69	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	N/A	SQYD	1,100		
70	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	N/A	LF	450		
71	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	SQFT	2,500		
72	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	N/A	SQFT	1,275		

PROPOSAL (Revised)

Alternate Bid Schedule 1 (Continued)

ITEM No.	ITEM CODE	ITEM	Like Bid Item*	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
73	000003	DRIVEWAY TIE-IN [0.33' PCC]	N/A	SQFT	390		
74	510502	MINOR CONCRETE (MINOR STRUCTURE) (CONCRETE U-DRAIN PER DETAIL AND MODIFIED UNDER SIDEWALK DRAIN PER CRS 309)	N/A	LS	1		
75	510502	MINOR CONCRETE (MINOR STRUCTURE) (UNDER SIDEWALK DRAIN (24" WIDE) PER CRS 309)	N/A	EA	2		
76	000003	CONTAMINATED SOIL MANAGEMENT	N/A	LS	1		
77	000003 (F)	CONTAMINATED SOIL MITIGATION/EXPORT	N/A	CY	235		
78	151281	SALVAGE ROADSIDE SIGN	N/A	EA	3		
79	000003	CHAIN LINK FENCE (6' HIGH)	N/A	LF	94		
80	000003	REMOVE EXISTING (MISCELLANEOUS)	N/A	LS	1		
81	198005	IMPORTED GRANULAR MATERIAL (DECOMPOSED GRANITE)	N/A	CY	7		

ALT BID SCH. 1


SUB-TOTAL: _____ \$ _____

ITEMS 60-81 "WORDS" _____


PROJECT TOTAL: _____ \$ _____

ITEMS 1-81 "WORDS" _____

* NOTE: See Page A8, Section "Like Bid Items" corrections will apply if proposal item cost discrepancies are submitted. Like bid items requirement does not apply to Alternate bid schedule. Like Bid Item Prices do not apply to Alternate Bid Schedule 1.



COUNTY OF RIVERSIDE TRANSPORTATION AND LAND MANAGEMENT AGENCY



Juan C. Perez, P.E., T.E.
Director

Patricia Romo, P.E.
Assistant Director

Transportation Department

ADDENDUM NUMBER 2

Dated December 4, 2013

to the
Specifications and Contract Documents
for the construction of

Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Project No. C1-0654
State Project No. SR2SL-5956(215)

Bids Due: (REVISED)
Wednesday, December 11, 2013; 2:00 p.m.
14th Street Transportation Annex
3525 14th Street; Riverside, CA 92501
(951) 955-6780

This Addendum is issued pursuant to the Instructions to Bidders, Item No. 8, of the Contract Documents for the reference project. This Addendum is issued as a supplement to the specification and special provisions for the referenced project. The revisions to the specifications shall become a part of the Contract Documents, and each bidder shall acknowledge receipt thereof on the Contractor's Proposal. Bidders are directed to sign this addendum as acknowledged, and attach the signed addendum to the contractor's submitted proposal.

Note: During the advertisement period of this project, this document and attachments (if any) are available upon request at the office of the Transportation Department, and are available as a free download at the Transportation Department's website:


http://www.rctlma.org/trans/con_bid_advertisements.html

MODIFICATIONS / CLARIFICATIONS TO SPECIAL PROVISIONS:

Item 1: The new designated date and time for the receipt and opening of bids is revised as follows:

Wednesday, December 11, 2013; 2:00 p.m.
14th Street Transportation Annex
3525 14th Street; Riverside, CA 92501
(951) 955-6780

Prepared by:



Joel Jimenez, PE; Senior Civil Engineer; Contracts/Bidding Unit

12/4/13

Acknowledged: _____ Date: _____

(Contractor)

JRJ:jrj



COUNTY OF RIVERSIDE TRANSPORTATION AND LAND MANAGEMENT AGENCY



Juan C. Perez, P.E., T.E.
Director of Transportation

Transportation Department

ADDENDUM NUMBER 3

Dated December 5, 2013

to the
Specifications and Contract Documents
for the construction of

Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca

Project No. C1-0654
State Project No. SR2SL-5956(215)

Bids Due: **Wednesday, December 11, 2013; 2:00 PM**
14th Street Transportation Annex
3525 14th Street, Riverside, CA 92501
(951) 955-6780

This Addendum is issued pursuant to the Instructions to Bidders, Item No. 8, of the Contract Documents for the reference project. This Addendum is issued as a supplement to the specification and special provisions for the referenced project. The revisions to the specifications shall become a part of the Contract Documents, and each bidder shall acknowledge receipt thereof on the Contractor's Bid. Bidders are directed to sign this addendum as acknowledged, and attach the signed addendum to the contractor's submitted Bid.

Note: During the advertisement period of this project, this document and attachments (if any) are available upon request at the office of the Transportation Department, and are available as a free download at the Transportation Department's website:

http://www.rctlma.org/trans/con_bid_advertisements.html

MODIFICATIONS / CLARIFICATIONS TO SPECIAL PROVISIONS:

Item 1: Like Bid Items Clarification

Refer to the Revised Proposal issued by Addendum No. 1. Like Bid Items requirements are applicable to Base Bid Schedule A and Base Bid Schedule B. Like Bid Item requirements are not applicable to Alternate Bid Schedule 1.


Item 2: Project Number correction.

Refer to Addendum No. 1 header section on pages 2-5. The State Project No. is SR2SL-5956(215).

Itc

Addendum No. 3
Mecca Group 4 Street Improvement Project
Project No. C1-0654, State Project No. SR2SL-5956(215)
December 5, 2013
Page 4 of 4

Recommended by:



Catherine M. Wampler, PE
County Project Manager

Concurrence:

 12/5/13

Khalid Nasim, PE
Engineering Division Manager

Acknowledged: _____ **Date:** _____
(Contractor)
JRJ:jrj:sb

Note: Refer to Instruction to Bidders Item No. 8, "Addenda". Submission of all addendum pages and non-bidding document attachments of addendum are not necessary for Bid submittal. Submittal of this acknowledgement page is adequate for Bid reception. Bidders are reminded to list addendum number(s) received on the first page of the Bid form (Proposal).

Contract

THIS CONTRACT is entered into at Riverside, California as of the date set forth below is between County of Riverside hereafter called "County" and **Golden Valley Construction, Inc.**, hereafter called "Contractor".

WITNESSETH

Recitals:

Contractor has submitted to County his Contractor's Proposal for the construction of County Project, **Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street and 4th Street, Community of Mecca, Project No. C1-0654, State Project No. – SR2SL-5956(215)**, in strict accordance with the Contract Documents identified below and County has accepted said Proposal.

1. Contractor states that he has reexamined his Contractor's Proposal and found it to be correct, has ascertained that his subcontractors are properly licensed and possess the requisite skill and forces, has reexamined the site and Contract Documents and is of the opinion that he can presently do the work in accordance with the Contract Documents for the money set forth in his Proposal to be paid as provided in the Contract Documents.

Agreement:

It is agreed by the parties as follows:

1. Contract Documents

The entire Contract consists of the following: (a) The Construction Contract, (b) The Notice Inviting Bids, (c) The Instruction to Bidders, (d) The Bid, (e) The Bid Bond, (f) The Payment Bond, (g) The Performance Bond, (h) The General Conditions, (i) The Special Provisions, (j) The Standard Specifications of the State of California Department of Transportation edition of May 2006 as modified in other portions of the Contract Documents and as amended by the State of California Department of Transportation, (k) The Standard Plans of the Department of Transportation identified on the plans or in the Special Provisions, (l) The Plans, (m) Addenda **(1, 2, and 3)**, (n) The Determination of Prevailing Wage Rates for Public Work, (o) Any Change Orders issued, (p) Any additional or supplemental specifications, notice, instructions and drawings issued in accordance with the provisions of the Contract Documents. All of said Documents presently in existence are by this reference incorporated herein with like effect as if here set forth in full and upon the proper issuance of other documents they shall likewise be deemed incorporated. The Bid Bond is exonerated upon execution of this Contract and the Payment Bond and Performance Bond.

2. The Work

Contractor shall do all tasks necessary to construct the work generally described in Recital No. 1 in accordance with the Contract Documents.

3. Liquidated Damages and Time of Completion

Attention is directed to the provisions in Section 8-1.06, "Time of Completion", and in Section 8-1.07 "Liquidated Damages", of the Standard Specifications and these Special Provisions.

Standard Specification Section 8-1.03, "Beginning of Work" is modified to read as follows:

The Contractor shall begin work within fifteen (15) calendar days, or as revised in the Special Provisions, of the date stated within the written "Notice to Proceed".

The Contractor shall notify the Engineer, in writing, of the Contractor's intent to begin work at least 72 hours before work is begun. If the project has more than one (1) location of work, Contractor shall submit a separate notice for each location. The notice shall be delivered to the Transportation Department's Construction Engineer and shall specify the date the Contractor intends to start at said location.

Should the Contractor begin work in advance of receiving a written "Notice to Proceed", any work performed by the Contractor in advance of the date stated in the "Notice to Proceed" shall be considered as having been done by the Contractor at his own risk and as a volunteer and subject to the following:

- A. The Contractor shall, on commencing operations, take all precautions required for public safety and shall observe all the provisions in the Specifications and the Special Provisions.
- B. All work done according to the contract, prior to the issuance of the "Notice to Proceed", will be considered authorized work and will be paid for as provided in the contract.
- C. The Contractor shall not be entitled to any additional compensation or an extension of time for any delay, hindrance or interference caused by or attributable to commencement of work prior to the issuance of the "Notice to Proceed".

4. Compensation

Contractor shall be paid in the manner set forth in the Contract Documents the amount of his Proposal as accepted by County, the above rates, subject to additions and deductions as provided in the Contract Documents. Said Proposal is on file in the Office of the Clerk of the Board of Supervisors of County.

**Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca**

**Project No. C1-0654
State Project No. – SR2SL-5956(215)**

Contract

Base Bid Schedule A : (Coahuilla Street, Sta. 20+33 to 30+00)

ITEM No.	ITEM CODE	ITEM	LIKE BID ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
1	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	10,000.00	10,000.00
2	066102	DUST ABATEMENT	N/A	LS	1	2,500.00	2,500.00
3	170101	DEVELOP WATER SUPPLY	N/A	LS	1	2,000.00	2,000.00
4	074020	WATER POLLUTION CONTROL	N/A	LS	1	1,500.00	1,500.00
5	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	7,000.00	7,000.00
6	000003	TEMPORARY CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN	N/A	EA	1	1,000.00	1,000.00
7	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	12,000.00	12,000.00
8	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	4,100	9.00	36,900.00
9	390130	HOT MIX ASPHALT	Like 02	TON	900	85.00	76,500.00
10	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	3,700	45.00	166,500.00
11	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	120	2.00	240.00
12	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	4,800	4.50	21,600.00
13	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	1,610	25.00	40,250.00
14	017309	MINOR CONCRETE (TYPE D CURB) (CRS 204)	N/A	LF	110	21.00	2,310.00
15	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	11,000	6.75	74,250.00
16	731502	MINOR CONCRETE (8" PAVEMENT)	N/A	SQFT	670	8.20	5,494.00
17	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	3	1,800.00	5,400.00
18	017315	MINOR CONCRETE (ADA ACCESSIBLE RAMP) (CRS 403 - CASE A PER DETAIL)	N/A	EA	1	1,800.00	1,800.00
19	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	850	9.75	8,287.50
20	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	5,300	6.50	34,450.00
21	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	990	7.00	6,930.00

Contract (Continued)

ITEM No.	ITEM CODE	ITEM	LIKE BID ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
22	394002	PLACE ASPHALT CONCRETE (DRIVEWAY TIE-IN)	N/A	SQFT	110	4.00	440.00
23	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	20	140.00	2,800.00
24	000001	ITEM DELETED BY ADDENDUM	----	-----	-----	-----	-----
25	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	860	1.15	989.00
26	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	590	5.00	2,950.00
27	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	3	150.00	450.00
28	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	13	200.00	2,600.00
29	000003	PAINT RED CURB	Like 16	LF	320	1.00	320.00
30	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	10	60.00	600.00

Base Bid
 Schedule A
 Sub-Total:
 Items 1-30

Five hundred twenty eight thousand, sixty dollars and fifty cents
 "WORDS"

\$528,060.50

Contract (Continued)

Base Bid Schedule B : (Coahuilla Street, Sta. 30+00 to 38+38.26, Date Palm Street Sta. 23+38 to 36+40.08)

ITEM No.	ITEM CODE	ITEM	LIKE BID ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
31	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	6,000.00	6,000.00
32	066102	DUST ABATEMENT	N/A	LS	1	2,000.00	2,000.00
33	170101	DEVELOP WATER SUPPLY	N/A	LS	1	2,000.00	2,000.00
34	074020	WATER POLLUTION CONTROL	N/A	LS	1	1,500.00	1,500.00
35	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	4,000.00	4,000.00
36	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	8,000.00	8,000.00
37	190101 (F)	ROADWAY EXCAVATION	Like 01	CY	1,000	9.00	9,000.00
38	390130	HOT MIX ASPHALT	Like 02	TON	850	85.00	72,250.00
39	260201	CLASS 2 AGGREGATE BASE	Like 03	CY	1,060	45.00	47,700.00
40	153103	COLD PLANE EXISTING AC PAVEMENT	Like 04	SQYD	5,700	2.00	11,400.00
41	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	Like 05	SQYD	1,400	4.50	6,300.00
42	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	Like 06	LF	275	25.00	6,875.00
43	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	N/A	LF	50	28.00	1,400.00
44	017304	MINOR CONCRETE (CURB AND GUTTER) (TRANSITION 8" - 6")	N/A	LF	160	18.00	2,880.00
45	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	Like 07	SQFT	2,500	6.75	16,875.00
46	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	Like 08	EA	4	1,800.00	7,200.00
47	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B AND PER DETAIL)	N/A	EA	1	1,800.00	1,800.00
48	017315	MINOR CONCRETE (MODIFIED CURB RAMP) (CRS 403 - PER DETAIL)	N/A	EA	1	1,800.00	1,800.00
49	017302	MINOR CONCRETE (CROSS-GUTTER) (CRS 209)	Like 09	SQFT	1,600	9.75	15,600.00
50	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	Like 10	SQFT	480	6.50	3,120.00
51	000003	DRIVEWAY TIE-IN [0.33' PCC]	Like 11	SQFT	100	7.00	700.00
52	000003	REMOVE EXISTING FENCE/GATE AND REPLACE WITH NEW CHAIN LINK FENCE/GATE OUTSIDE PUBLIC R/W	N/A	LF	45	75.00	3,375.00
53	840656	PAINT TRAFFIC STRIPE (2 COAT)	Like 12	LF	1,050	1.15	1,207.50
54	840519	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	Like 13	SQFT	620	5.00	3,100.00

Contract (Continued)

Base Bid Schedule B : (Coahuilla Street, Sta. 30+00 to 38+38.26, Date Palm Street Sta. 23+38 to 36+40.08)

ITEM No.	ITEM CODE	ITEM	LIKE BID ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
55	152390	RELOCATE ROADSIDE SIGN	Like 14	EA	7	150.00	1,050.00
56	566011	ROADSIDE SIGN - ONE POST	Like 15	EA	9	200.00	1,800.00
57	000003	PAINT RED CURB	Like 16	LF	640	1.00	640.00
58	151281	SALVAGE ROADSIDE SIGN	Like 17	EA	6	60.00	360.00
59	000003	MISCELLANEOUS DIRECTED WORK	N/A	FA	1	95,000.00	95,000.00

Base Bid
Schedule B
Sub-Total:
Items 31-59

Three hundred thirty four thousand, nine hundred thirty two dollars and fifty cents
"WORDS"

\$334,932.50

Alternate Bid Schedule 1 (4th Street Cul De Sac)

ITEM No.	ITEM CODE	ITEM	LIKE BID ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
60	760090	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	N/A	LS	1	8,000.00	8,000.00
61	066102	DUST ABATEMENT	N/A	LS	1	4,000.00	4,000.00
62	170101	DEVELOP WATER SUPPLY	N/A	LS	1	2,000.00	2,000.00
63	074020	WATER POLLUTION CONTROL	N/A	LS	1	1,500.00	1,500.00
64	120100	TRAFFIC CONTROL SYSTEM	N/A	LS	1	4,000.00	4,000.00
65	160101	CLEARING AND GRUBBING [INCLUDING VARIOUS ITEMS LISTED IN SPECIAL PROVISIONS]	N/A	LS	1	6,000.00	6,000.00
66	190101 (F)	ROADWAY EXCAVATION	N/A	CY	840	9.00	7,560.00
67	390130	HOT MIX ASPHALT	N/A	TON	200	100.00	20,000.00
68	260201	CLASS 2 AGGREGATE BASE	N/A	CY	700	45.00	31,500.00
69	393001	PAVEMENT REINFORCING FABRIC (GEOGRID 2-LAYERS)	N/A	SQYD	1,100	6.50	7,150.00
70	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	N/A	LF	450	30.00	13,500.00
71	731521	MINOR CONCRETE (SIDEWALK) (CRS 401)	N/A	SQFT	2,500	6.75	16,875.00
72	731516	MINOR CONCRETE (DRIVEWAY) (CRS 207)	N/A	SQFT	1,275	8.00	10,200.00

Contract (Continued)

Alternate Bid Schedule 1 (4th Street Cul De Sac)

ITEM No.	ITEM CODE	ITEM	LIKE BID ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
73	000003	DRIVEWAY TIE-IN [0.33' PCC]	N/A	SQFT	390	8.00	3,120.00
74	510502	MINOR CONCRETE (MINOR STRUCTURE) (CONCRETE U-DRAIN PER DETAIL AND MODIFIED UNDER SIDEWALK DRAIN PER CRS 309)	N/A	LS	1	2,500.00	2,500.00
75	510502	MINOR CONCRETE (MINOR STRUCTURE) (UNDER SIDEWALK DRAIN (24" WIDE) PER CRS 309)	N/A	EA	2	1,500.00	3,000.00
76	000003	CONTAMINATED SOIL MANAGEMENT	N/A	LS	1	5,000.00	5,000.00
77	000003 (F)	CONTAMINATED SOIL MITIGATION/EXPORT	N/A	CY	235	25.00	5,875.00
78	151281	SALVAGE ROADSIDE SIGN	N/A	EA	3	60.00	180.00
79	000003	CHAIN LINK FENCE (6' HIGH)	N/A	LF	94	40.00	3,760.00
80	000003	REMOVE EXISTING (MISCELLANEOUS)	N/A	LS	1	5,000.00	5,000.00
81	198005	IMPORTED GRANULAR MATERIAL (DECOMPOSED GRANITE)	N/A	CY	7	50.00	350.00

Alt. Bid
Schedule 1
Sub-Total:
Items 60-81

One hundred sixty one thousand, seventy dollars and zero cents
"WORDS"

\$161,070.00

PROJECT
TOTAL:
ITEMS 1-81

One million, twenty four thousand, sixty three dollars and zero cents
"WORDS"

\$1,024,063.00

Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street
Community of Mecca


Project No. C1-0654
State Project No. - SR2SL-5956(215)

IN WITNESS WHEREOF the parties hereto have executed this Contract as of the date set forth below.

COUNTY OF RIVERSIDE

Golden Valley Construction, Inc.

BY: _____
Chairman, Board of Supervisors

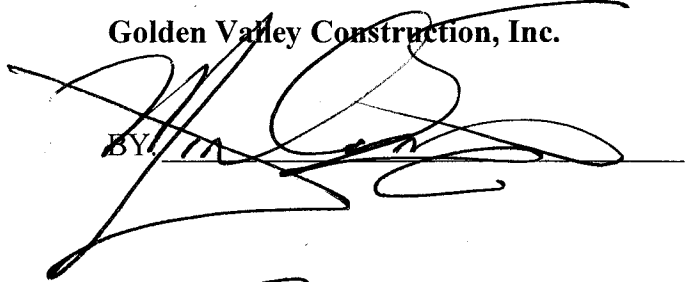
BY: _____

DATED: _____

TITLE: President
(If Corporation, affix Seal)

ATTEST:
Kecia Harper-Ihem, Clerk of the Board

ATTEST:

BY: _____
Deputy

TITLE: _____

Licensed in accordance with an act providing
for the registration of Contractors,

License No. 776249

Federal Employer Identification Number:

95-4730261

BY _____
"County"

"Corporation"
(Seal)

FORM APPROVED COUNTY COUNSEL
BY: MS Victor 2/11/14
MARSHAL VICTOR DATE

Corporate Resolution of:

Golden Vista Construction, Inc. dba Golden Valley Construction

We, the undersigned, being all the directors of this corporation consent and agree that the following corporate resolution was made on 12/02/2013 date at 12:36pm time at 2000 Executive Drive, Palm Springs, CA 92262 location

We do hereby consent to the adoption of the following as if it was adopted at a regularly called meeting of the board of directors of this corporation. In accordance with State law and the bylaws of this corporation, by unanimous consent, the board of directors decided that:

We authorize Mike Honz, General Manager of the Palm Springs Division to be a signer on behalf of Golden Valley Construction for the Mecca Group 4 Street Improvement Project Coachella Street, Date Palm Street and 4th Street, Community of Mecca Project No. C1-0654 State Project No. SR2SL-5956(215)

Therefore, it is resolved, that the corporation shall:

Approve and authorize Mike Honz, General Manager of the Palm Springs Division to be a signer on behalf of Golden Valley Construction for the Mecca Group 4 Street Improvement Project Coachella Street, Date Palm Street and 4th Street, Community of Mecca Project No. C1-0654 State Project No. SR2SL-5956(215)

The officers of this corporation are authorized to perform the acts to carry out this corporate resolution.



Director signature

Michael Emerson

Printed name

12/02/2013

Date



Director signature

Shannon Murphey

Printed name

12/02/2013

Date

Director signature

Printed name

Date

Director signature

Printed name

Date

Director signature

Printed name


Date

Director signature

Printed name

Date

The Secretary of the Corporation, certifies that the above is a true and correct copy of the resolution that was duly adopted at a meeting of the dated meeting of the board of directors.


Signature of Secretary

12/02/2013

Date

Shannon Murphey

Printed name of Secretary

Performance Bond

Recitals:

1. **Golden Valley Construction** (Contractor) has entered into an Agreement with COUNTY OF RIVERSIDE (County) for construction of public work known as **Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street and 4th Street, Community of Mecca, Project No. C1-0654, State Project No. – SR2SL-5956(215)**.

2. _____, a _____ corporation (Surety), is the Surety under this Bond.

Agreement:

We, Contractor as Principal and Surety as Surety, jointly and severally agree, state, and are bound unto County, as obligee, as follows:

1. The amount of the obligation of this Bond is 100% of the estimated contract price for the Project of **\$1,024,063.00 (One million, twenty four thousand, sixty three dollars and zero cents)** and inures to the benefit of County.

2. This Bond is exonerated by Contractor doing all things to be kept and performed by it in strict conformance with the Contract Documents for this project, otherwise it remains in full force and effect for the recovery of loss, damage and expense of County resulting from failure of Contractor to so act. All of said Contract Documents are incorporated herein.

3. This obligation is binding on our successors and assigns.

4. For value received, Surety stipulates and agrees that no change, time extension, prepayment to Contractor, alteration or addition to the terms and requirements of the Contract Documents or the work to be performed thereunder shall affect its obligations hereunder and waives notice as to such matters, except the total contract price cannot be increased by more than 10% without approval of Surety.

THIS BOND is executed as of _____.

By _____

By _____

By _____

Type Name _____

Its Attorney in Fact
"Surety"

Title _____

"Contractor"

(Corporate Seal)

(Corporate Seal)

NOTE: This Bond must be executed by both parties with corporate seal affixed. All signatures must be acknowledged. (Attach acknowledgements).

Payment Bond

(Public Works - Civil Code §9550 et seq.)

The makers of this Bond are **Golden Valley Construction** as Principal and Original Contractor and _____, a corporation, authorized to issue Surety Bonds in California, as Surety, and this Bond is issued in conjunction with that certain public works contract to be executed between Principal and COUNTY OF RIVERSIDE a public entity, as Owner, for **\$1,024,063.00 (One million, twenty four thousand, sixty three dollars and zero cents)**, the total amount payable. The amount of this bond is one hundred percent (100%) of said sum. Said contract is for public work generally consisting of **Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street and 4th Street, Community of Mecca, Project No. C1-0654, State Project No. – SR2SL-5956(215)**.

The beneficiaries of this Bond are as is stated in 9554 of the Civil Code and requirements and conditions of this Bond are as is set forth in 9554, 9558, 9560 and 9564 of said code. Without notice, Surety consents to extension of time for performance, change in requirements, amount of compensation, or prepayment under said contract.

Dated: _____

Original Contractor – Principal

Surety

By _____

By _____

Title _____

Its Attorney In Fact

(If corporation, affix seal)

(Corporate Seal)

(Corporate Seal)

STATE OF _____
COUNTY OF _____ }

ss. SURETY'S ACKNOWLEDGEMENT

On _____ before me, _____ personally appeared, _____, known to me, or proved to me on the basis of satisfactory evidence, to be the person whose name is subscribed to the within instrument and acknowledged to me that he executed the same in his authorized capacities, and that by his signature on the instrument the person, or the entity upon behalf of which the person acted, executed the instrument.

WITNESS my hand and official seal.

Signature of Notary Public

Notary Public (Seal)

NOTE: This Bond must be executed by both parties with corporate seal affixed. All signatures must be acknowledged. (Attach acknowledgements).

Performance Bond

Recitals:

Golden Vista Construction, Inc. dba

1. **Golden Valley Construction** (Contractor) has entered into an Agreement with COUNTY OF RIVERSIDE (County) for construction of public work known as **Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street and 4th Street, Community of Mecca, Project No. C1-0654, State Project No. - SR2SL-5956(215)**.
2. North American Specialty Insurance Company, a New Hampshire corporation (Surety), is the Surety under this Bond.

Agreement:

We, Contractor as Principal and Surety as Surety, jointly and severally agree, state, and are bound unto County, as obligee, as follows:

1. The amount of the obligation of this Bond is 100% of the estimated contract price for the Project of **\$1,024,063.00 (One million, twenty four thousand, sixty three dollars and zero cents)** and inures to the benefit of County.
2. This Bond is exonerated by Contractor doing all things to be kept and performed by it in strict conformance with the Contract Documents for this project, otherwise it remains in full force and effect for the recovery of loss, damage and expense of County resulting from failure of Contractor to so act. All of said Contract Documents are incorporated herein.
3. This obligation is binding on our successors and assigns.
4. For value received, Surety stipulates and agrees that no change, time extension, prepayment to Contractor, alteration or addition to the terms and requirements of the Contract Documents or the work to be performed thereunder shall affect its obligations hereunder and waives notice as to such matters, except the total contract price cannot be increased by more than 10% without approval of Surety.

THIS BOND is executed as of December 27, 2013

Golden Vista Construction, Inc. dba

North American Specialty Insurance Company

By Golden Valley Construction

By [Signature]

By [Signature]

Type Name Donna L. Welsh, Attorney-in-Fact

Its Attorney in Fact
"Surety"

Title President

"Contractor"

(Corporate Seal)

(Corporate Seal)

NOTE: This Bond must be executed by both parties with corporate seal affixed. All signatures must be acknowledged. (Attach acknowledgements).

CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT

State of California

County of MARIN


On December 27, 2013 before me, Donna J. Frowd, Notary Public, personally appeared Donna L. Welsh who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

(seal)

Signature Donna J. Frowd



NAS SURETY GROUP

NORTH AMERICAN SPECIALTY INSURANCE COMPANY
WASHINGTON INTERNATIONAL INSURANCE COMPANY

GENERAL POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS, THAT North American Specialty Insurance Company, a corporation duly organized and existing under laws of the State of New Hampshire, and having its principal office in the City of Manchester, New Hampshire, and Washington International Insurance Company, a corporation organized and existing under the laws of the State of New Hampshire and having its principal office in the City of Schaumburg, Illinois, each does hereby make, constitute and appoint:

MICHAEL B. MCGOWAN, SUSAN J. MCGOWAN, DONNA L. WELSH,

DEBBIE L. WELSH and DONNA J. FROWD

JOINTLY OR SEVERALLY

Its true and lawful Attorney(s)-in-Fact, to make, execute, seal and deliver, for and on its behalf and as its act and deed, bonds or other writings obligatory in the nature of a bond on behalf of each of said Companies, as surety, on contracts of suretyship as are or may be required or permitted by law, regulation, contract or otherwise, provided that no bond or undertaking or contract or suretyship executed under this authority shall exceed the amount of:

FIFTY MILLION (\$50,000,000.00) DOLLARS

This Power of Attorney is granted and is signed by facsimile under and by the authority of the following Resolutions adopted by the Boards of Directors of both North American Specialty Insurance Company and Washington International Insurance Company at meetings duly called and held on the 9th of May, 2012:

"RESOLVED, that any two of the Presidents, any Managing Director, any Senior Vice President, any Vice President, any Assistant Vice President, the Secretary or any Assistant Secretary be, and each or any of them hereby is authorized to execute a Power of Attorney qualifying the attorney named in the given Power of Attorney to execute on behalf of the Company bonds, undertakings and all contracts of surety, and that each or any of them hereby is authorized to attest to the execution of any such Power of Attorney and to attach therein the seal of the Company; and it is

FURTHER RESOLVED, that the signature of such officers and the seal of the Company may be affixed to any such Power of Attorney or to any certificate relating thereto by facsimile, and any such Power of Attorney or certificate bearing such facsimile signatures or facsimile seal shall be binding upon the Company when so affixed and in the future with regard to any bond, undertaking or contract of surety to which it is attached."



By [Signature] Steven P. Anderson, Senior Vice President of Washington International Insurance Company & Senior Vice President of North American Specialty Insurance Company




By [Signature] David M. Layman, Vice President of Washington International Insurance Company & Vice President of North American Specialty Insurance Company

IN WITNESS WHEREOF, North American Specialty Insurance Company and Washington International Insurance Company have caused their official seals to be hereunto affixed, and these presents to be signed by their authorized officers this 26th day of June, 2012.

North American Specialty Insurance Company
Washington International Insurance Company

State of Illinois
County of Cook ss:

On this 26th day of June, 2012, before me, a Notary Public personally appeared Steven P. Anderson, Senior Vice President of Washington International Insurance Company and Senior Vice President of North American Specialty Insurance Company and David M. Layman, Vice President of Washington International Insurance Company and Vice President of North American Specialty Insurance Company, personally known to me, who being by me duly sworn, acknowledged that they signed the above Power of Attorney as officers of and acknowledged said instrument to be the voluntary act and deed of their respective companies.



[Signature] Donna D. Sklens, Notary Public

I, Jeffrey Goldberg, the duly elected Assistant Secretary of North American Specialty Insurance Company and Washington International Insurance Company, do hereby certify that the above and foregoing is a true and correct copy of a Power of Attorney given by said North American Specialty Insurance Company and Washington International Insurance Company, which is still in full force and effect.

IN WITNESS WHEREOF, I have set my hand and affixed the seals of the Companies this 27th day of December, 2013.

[Signature] Jeffrey Goldberg, Vice President & Assistant Secretary of Washington International Insurance Company & North American Specialty Insurance Company

CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT

CIVIL CODE § 1189


State of California

County of Los Angeles }

On Dec 31, 2013 before me, Carrie L. Dranow, Notary Public,
Date Here Insert Name and Title of the Officer

personally appeared Michael Emerson
Name(s) of Signer(s)

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is are subscribed to the within instrument and acknowledged to me that he she they executed the same in his her their authorized capacity(ies), and that by his her their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.



I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature: Carrie L. Dranow
Signature of Notary Public

Place Notary Seal Above

OPTIONAL

Though the information below is not required by law, it may prove valuable to persons relying on the document and could prevent fraudulent removal and reattachment of this form to another document.

Description of Attached Document

Title or Type of Document: Performance Bond

Document Date: 12-31-13 Number of Pages: 3

Signer(s) Other Than Named Above: Donna L. Welsh

Capacity(ies) Claimed by Signer(s)

Signer's Name: Michael Emerson Signer's Name: _____

- Corporate Officer — Title(s): President Corporate Officer — Title(s): _____
- Individual Individual
- Partner — Limited General Partner — Limited General
- Attorney in Fact Attorney in Fact
- Trustee Trustee
- Guardian or Conservator Guardian or Conservator
- Other: _____ Other: _____

Signer Is Representing: Golden Vista Construction Inc.

Signer Is Representing: _____

Payment Bond

(Public Works - Civil Code §9550 et seq.)

The makers of this Bond are Golden Vista Construction, Inc. dba Golden Valley Construction as Principal and Original Contractor and North American Specialty Insurance Company, a corporation, authorized to issue Surety Bonds in California, as Surety, and this Bond is issued in conjunction with that certain public works contract to be executed between Principal and COUNTY OF RIVERSIDE a public entity, as Owner, for \$1,024,063.00 (One million, twenty four thousand, sixty three dollars and zero cents), the total amount payable. The amount of this bond is one hundred percent (100%) of said sum. Said contract is for public work generally consisting of Mecca Group 4 Street Improvement Project, Coahuilla Street, Date Palm Street and 4th Street, Community of Mecca, Project No. C1-0654, State Project No. - SR2SL-5956(215).

The beneficiaries of this Bond are as is stated in 9554 of the Civil Code and requirements and conditions of this Bond are as is set forth in 9554, 9558, 9560 and 9564 of said code. Without notice, Surety consents to extension of time for performance, change in requirements, amount of compensation, or prepayment under said contract.

Dated: December 27, 2013

Golden Vista Construction, Inc. dba
Golden Valley Construction

Original Contractor - Principal

[Handwritten Signature]

By

Title President

(If corporation, affix seal)

North American Specialty Insurance Company

Surety

By *[Handwritten Signature]*

Donna L. Welsh
Its Attorney In Fact

(Corporate Seal)

(Corporate Seal)

STATE OF _____
COUNTY OF _____ }

See attached Notary Acknowledgment and Power of Attorney
ss. SURETY'S ACKNOWLEDGEMENT

On _____ before me, _____ personally appeared, _____, known to me, or proved to me on the basis of satisfactory evidence, to be the person whose name is subscribed to the within instrument and acknowledged to me that he executed the same in his authorized capacities, and that by his signature on the instrument the person, or the entity upon behalf of which the person acted, executed the instrument.

WITNESS my hand and official seal.

Signature of Notary Public

Notary Public (Seal)

NOTE: This Bond must be executed by both parties with corporate seal affixed. All signatures must be acknowledged. (Attach acknowledgements).

CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT

State of California

County of MARIN


On December 27, 2013 before me, Donna J. Frowd, Notary Public, personally appeared Donna L. Welsh who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/~~are~~ subscribed to the within instrument and acknowledged to me that he/~~she/they~~ executed the same in his/~~her/their~~ authorized capacity(ies), and that by his/~~her/their~~ signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

(seal)

Signature Donna J. Frowd



NAS SURETY GROUP

NORTH AMERICAN SPECIALTY INSURANCE COMPANY
WASHINGTON INTERNATIONAL INSURANCE COMPANY

GENERAL POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS, THAT North American Specialty Insurance Company, a corporation duly organized and existing under laws of the State of New Hampshire, and having its principal office in the City of Manchester, New Hampshire, and Washington International Insurance Company, a corporation organized and existing under the laws of the State of New Hampshire and having its principal office in the City of Schaumburg, Illinois, each does hereby make, constitute and appoint:

MICHAEL B. MCGOWAN, SUSAN J. MCGOWAN, DONNA L. WELSH,

DEBBIE L. WELSH and DONNA J. FROWD

JOINTLY OR SEVERALLY

Its true and lawful Attorney(s)-in-Fact, to make, execute, seal and deliver, for and on its behalf and as its act and deed, bonds or other writings obligatory in the nature of a bond on behalf of each of said Companies, as surety, on contracts of suretyship as are or may be required or permitted by law, regulation, contract or otherwise, provided that no bond or undertaking or contract or suretyship executed under this authority shall exceed the amount of:

FIFTY MILLION (\$50,000,000.00) DOLLARS

This Power of Attorney is granted and is signed by facsimile under and by the authority of the following Resolutions adopted by the Boards of Directors of both North American Specialty Insurance Company and Washington International Insurance Company at meetings duly called and held on the 9th of May, 2012:

“RESOLVED, that any two of the Presidents, any Managing Director, any Senior Vice President, any Vice President, any Assistant Vice President, the Secretary or any Assistant Secretary be, and each or any of them hereby is authorized to execute a Power of Attorney qualifying the attorney named in the given Power of Attorney to execute on behalf of the Company bonds, undertakings and all contracts of surety, and that each or any of them hereby is authorized to attest to the execution of any such Power of Attorney and to attach therein the seal of the Company; and it is

FURTHER RESOLVED, that the signature of such officers and the seal of the Company may be affixed to any such Power of Attorney or to any certificate relating thereto by facsimile, and any such Power of Attorney or certificate bearing such facsimile signatures or facsimile seal shall be binding upon the Company when so affixed and in the future with regard to any bond, undertaking or contract of surety to which it is attached.”



By [Signature]
Steven P. Anderson, Senior Vice President of Washington International Insurance Company
& Senior Vice President of North American Specialty Insurance Company




By [Signature]
David M. Layman, Vice President of Washington International Insurance Company
& Vice President of North American Specialty Insurance Company

IN WITNESS WHEREOF, North American Specialty Insurance Company and Washington International Insurance Company have caused their official seals to be hereunto affixed, and these presents to be signed by their authorized officers this 26th day of June, 2012.

North American Specialty Insurance Company
Washington International Insurance Company

State of Illinois
County of Cook ss:

On this 26th day of June, 2012, before me, a Notary Public personally appeared Steven P. Anderson, Senior Vice President of Washington International Insurance Company and Senior Vice President of North American Specialty Insurance Company and David M. Layman, Vice President of Washington International Insurance Company and Vice President of North American Specialty Insurance Company, personally known to me, who being by me duly sworn, acknowledged that they signed the above Power of Attorney as officers of and acknowledged said instrument to be the voluntary act and deed of their respective companies.



[Signature]
Donna D. Sklens, Notary Public

I, Jeffrey Goldberg, the duly elected Assistant Secretary of North American Specialty Insurance Company and Washington International Insurance Company, do hereby certify that the above and foregoing is a true and correct copy of a Power of Attorney given by said North American Specialty Insurance Company and Washington International Insurance Company, which is still in full force and effect.

IN WITNESS WHEREOF, I have set my hand and affixed the seals of the Companies this 27th day of December, 2013.

[Signature]
Jeffrey Goldberg, Vice President & Assistant Secretary of
Washington International Insurance Company & North American Specialty Insurance Company

CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT

CIVIL CODE § 1189

State of California

County of Los Angeles

On Dec. 31, 2013 before me, Carrie L. Dranow, Notary Public


Date

Here Insert Name and Title of the Officer

personally appeared Michael Emerson

Name(s) of Signer(s)

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) ~~is~~ subscribed to the within instrument and acknowledged to me that ~~he~~ ~~she~~ ~~they~~ executed the same in ~~his~~ ~~her~~ ~~their~~ authorized capacity(ies), and that by ~~his~~ ~~her~~ ~~their~~ signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.



I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature: Carrie L. Dranow

Place Notary Seal Above

Signature of Notary Public

OPTIONAL

Though the information below is not required by law, it may prove valuable to persons relying on the document and could prevent fraudulent removal and reattachment of this form to another document.

Description of Attached Document

Title or Type of Document: Payment Bond

Document Date: 12-31-13

Number of Pages: 3

Signer(s) Other Than Named Above: Donna G. Welsh

Capacity(ies) Claimed by Signer(s)

Signer's Name: Michael Emerson

Signer's Name: _____

Corporate Officer — Title(s): President

Corporate Officer — Title(s): _____

Individual

Individual

Partner — Limited General

Partner — Limited General

Attorney in Fact

Attorney in Fact

Trustee

Trustee

Guardian or Conservator

Guardian or Conservator

Other: _____

Other: _____

Signer Is Representing: Golden Vista Construction Inc.

Signer Is Representing: _____



- Company Profile
- Company Search
- Company Search Results
- Company Information
- Old Company Names
- Agent for Service Reference Information
- NAIC Group List
- Lines of Business
- Workers' Compensation
- Complaint and Request for Action/Appeals
- Contact Information
- Financial Statements PDF's
- Annual Statements
- Quarterly Statements
- Company Complaint
- Company Performance & Comparison Data
- Company Enforcement Action
- Composite Complaints Studies
- Additional Info
- Find A Company Representative In Your Area
- View Financial Disclaimer

COMPANY PROFILE

Company Information

NORTH AMERICAN SPECIALTY INSURANCE COMPANY

**650 ELM STREET, 6TH FLOOR
MANCHESTER, NH 03101-2524**

Old Company Names

Effective Date

Agent For Service

NANCY FLORES
C/O CT CORPORATION SYSTEM
818 WEST SEVENTH STREET
LOS ANGELES CA 90017

Reference Information

NAIC #:	29874
California Company ID #:	3208-6
Date Authorized in California:	06/30/1989
License Status:	UNLIMITED-NORMAL
Company Type:	Property & Casualty
State of Domicile:	NEW HAMPSHIRE

[back to top](#)

NAIC Group List

NAIC Group #: 0181 SWISS RE GRP

Lines Of Business

The company is authorized to transact business within these lines of insurance. For an explanation of any of these terms, please refer to the glossary.

- AIRCRAFT
- AUTOMOBILE
- BOILER AND MACHINERY
- BURGLARY
- DISABILITY
- FIRE
- LIABILITY
- MARINE
- PLATE GLASS
- SPRINKLER
- SURETY
- WORKERS' COMPENSATION

[back to top](#)

ACORD CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

01/10/2013

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER Southland Insurance Brokers 19069 Van Buren Blvd. #114-484 Riverside, CA 92508	CONTACT NAME: Arda Williams PHONE (A/C, No, Ext): 951.789.9901 FAX (A/C, No): 951.534.5500 E-MAIL ADDRESS:													
	<table border="1"> <tr> <th>INSURER(S) AFFORDING COVERAGE</th> <th>NAIC #</th> </tr> <tr> <td>INSURER A: WESCO Insurance Co.</td> <td>25011</td> </tr> <tr> <td>INSURER B: Century Surety Co.</td> <td>36951</td> </tr> <tr> <td>INSURER C:</td> <td></td> </tr> <tr> <td>INSURER D:</td> <td></td> </tr> <tr> <td>INSURER E:</td> <td></td> </tr> <tr> <td>INSURER F:</td> <td></td> </tr> </table>	INSURER(S) AFFORDING COVERAGE	NAIC #	INSURER A: WESCO Insurance Co.	25011	INSURER B: Century Surety Co.	36951	INSURER C:		INSURER D:		INSURER E:		INSURER F:
INSURER(S) AFFORDING COVERAGE	NAIC #													
INSURER A: WESCO Insurance Co.	25011													
INSURER B: Century Surety Co.	36951													
INSURER C:														
INSURER D:														
INSURER E:														
INSURER F:														
INSURED Golden Vista Construction Inc. DBA: Golden Valley Construction 44815 Fig Ave. #117 Lancaster, CA 93534														


COVERAGES CERTIFICATE NUMBER: 2013-2014 A/I REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSUR LTR	TYPE OF INSURANCE	AUOL SUBR INSR I WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	GENERAL LIABILITY <input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC	X	WPA103088802	05/11/2013	05/11/2014	EACH OCCURRENCE \$ 1,000,000
	DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 50,000 MED EXP (Any one person) \$ 5,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS COMP/OP AGG \$ 2,000,000					
A	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input checked="" type="checkbox"/> ALL OWNED AUTOS <input checked="" type="checkbox"/> HIRED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input checked="" type="checkbox"/> NON-OWNED AUTOS	X	WPA103088802	05/11/2013	05/11/2014	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000
	BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$					
B	UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> DED <input type="checkbox"/> RETENTION \$	X	CCP821166	05/15/2013	05/11/2014	EACH OCCURRENCE \$ 2,000,000
	AGGREGATE \$ 2,000,000					
A	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below Y/N <input type="checkbox"/> Y <input checked="" type="checkbox"/> N/A	N/A	WVC3057142	03/31/2013	03/31/2014	<input checked="" type="checkbox"/> WVC STATU- LURY LIMITS <input type="checkbox"/> OTH- ER
	E.L. EACH ACCIDENT \$ 1,000,000 E.L. DISEASE - EA EMPLOYEE \$ 1,000,000 E.L. DISEASE - POLICY LIMIT \$ 1,000,000					
A	Rented or Leased Equipment	X	WPA103088802	05/11/2013	05/11/2014	\$25,000 Limit \$1,000 Deductible

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

30 day notice of cancellation
 Project: Mecca Group 4 Street Improvement Project Coahuilla Street, Date Palm Street and 4th Street Community of Mecca / Project No.C1-0654
 The County of Riverside, its Directors, Officers, Special Districts, Board of Supervisors employees, agents and representatives are named additional insured "see attached for more additional insureds"

CERTIFICATE HOLDER County of Riverisde Transportation Department 3524 14th Street 2nd Floor Riverside, CA 92502	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	AUTHORIZED REPRESENTATIVE Arda Williams 

County of Riverside

Certificate issued to County of Riverside

01/10/2013

Southland Insurance Brokers

01/16/2014

Coachella Valley Water District (CVWD), its directors officers elected and appointed officials, employees agents and representatives are named additional insured.

Imperial Irrigation District (IID), its directors officers elected and appointed officials, employees agents and representatives are named additional insured.

The State of California, its directors officers elected and appointed officials, employees agents and representatives are named additional insured.

POLICY NUMBER: WPA1030888 02

COMMERCIAL GENERAL LIABILITY
CG 20 10 07 04

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

**ADDITIONAL INSURED – OWNERS, LESSEES OR
CONTRACTORS – SCHEDULED PERSON OR
ORGANIZATION**

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART

SCHEDULE

Name Of Additional Insured Person(s) Or Organization(s):	Location(s) Of Covered Operations
Blanket as required by written contract and effective during the policy period as stated in the policy declarations.	Blanket as required by written contract. Primary Insurance applies: It is agreed that such insurance as is afforded by this policy for the benefit of the Additional Insured shown shall be primary insurance, and any other insurance maintained by the Additional Insured(s) shall be excess and non-contributory as respects any claim, loss or liability allegedly arising out of the operations of the named insured, provided however that this insurance will not apply to any claim loss or liability which is determined to be solely the result of the Additional Insured's negligence or solely the Additional Insured's responsibility.

Information required to complete this Schedule, if not shown above, will be shown in the Declarations.

A. Section II – Who Is An Insured is amended to include as an additional insured the person(s) or organization(s) shown in the Schedule, but only with respect to liability for "bodily injury", "property damage" or "personal and advertising injury" caused, in whole or in part, by:

1. Your acts or omissions; or
2. The acts or omissions of those acting on your behalf;

in the performance of your ongoing operations for the additional insured(s) at the location(s) designated above.

B. With respect to the insurance afforded to these additional insureds, the following additional exclusions apply:

This insurance does not apply to "bodily injury" or "property damage" occurring after:

1. All work, including materials, parts or equipment furnished in connection with such work, on the project (other than service, maintenance or repairs) to be performed by or on behalf of the additional insured(s) at the location of the covered operations has been completed; or
2. That portion of "your work" out of which the injury or damage arises has been put to its intended use by any person or organization other than another contractor or subcontractor engaged in performing operations for a principal as a part of the same project.



Authorized Representative Signature

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

POLICY CHANGES

Policy Change
Number 11

POLICY NUMBER WPA1030888 02	POLICY CHANGES EFFECTIVE 01/08/14	COMPANY Wesco, CA, Prem-Auto
NAMED INSURED GOLDEN VALLEY CONSTRUCTION INC GOLDEN VISTA CONSTRUCTION DBA:		AUTHORIZED REPRESENTATIVE Jim Furey
COVERAGE PARTS AFFECTED ITEM FOUR - COMMERCIAL GENERAL LIABILITY - GENERAL CHANGE		

CHANGES

In consideration of an Additional Premium of \$ 42 it is agreed that the following change has been made to the policy

PROCESSED ATTACHED INDIVIDUAL ADDITIONAL INSURED.

ALL OTHER TERMS AND CONDITIONS REMAIN UNCHANGED.

IL 12 01 11 85

Copyright, Insurance Services Office, Inc. 1983
Copyright, ISO Commercial Risk Services, Inc. 1983

Authorized Representative Signature

01/10/14
Handler # 185

INSURED

**GOLDEN VALLEY CONSTRUCTION INC. GOLDEN VISTA CONSTRUCTION DBA:
WPA1030888 02**

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

ADDITIONAL INSURED – DESIGNATED PERSON OR ORGANIZATION

This endorsement modifies insurance provided under the following:

- BUSINESS AUTO COVERAGE FORM
- GARAGE COVERAGE FORM
- TRUCKERS COVERAGE FORM

SCHEDULE

Name of Person or Organization:

**Blanket as required by written contract and
Effective during the policy period as stated in the policy
declarations.**

Description of Covered "Auto"

Per Schedule on file with company

(If no entry appears in the Schedule above, information required to complete this endorsement will be shown in the Declarations as applicable to this endorsement.)

The WHO IS AN INSURED provision under LIABILITY COVERAGE is changed to include as an "insured" The person or organization shown in the Schedule, but only with respect to liability arising out of:

1. Your operations or services performed for that person or organization at the location shown in the Schedule; or
2. The ownership, maintenance or use of the covered "autos" described in the Schedule.


A person's or organization's status as an additional insured under this endorsement ends when:

1. Your operations or services performed for that person or organization are completed; or
2. That person's or organization's interest in the described "auto" ends.

CA990009 1004

Includes copyrighted material of Insurance Services Office, Inc., with its permission.

PRODUCING AGENT



Authorized Representative Signature

ABA22682

POLICY NUMBER: WPA1030888 02

COMMERCIAL GENERAL LIABILITY
CG 24 04 03 09

WAIVER OF TRANSFER OF RIGHTS OF RECOVERY AGAINST OTHERS TO US

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART
PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART

SCHEDULE

Name Of Person Or Organization:

Blanket as required by written contract and effective during the policy period as stated in the policy declarations.

Information required to complete this Schedule, if not shown above, will be shown in the Declarations.

The following is added to Paragraph 8. **Transfer Of Rights Of Recovery Against Others To Us of Section IV - Conditions:**

We waive any right of recovery we may have against the person or organization shown in the Schedule above because of payments we make for injury or damage arising out of your ongoing operations or "your work" done under a contract with that person or organization and included in the "products-completed operations hazard". This waiver applies only to the person or organization shown in the Schedule above.


Authorized Representative Signature

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

POLICY CHANGES

Policy Change
Number 12

POLICY NUMBER WPA1030888 02	POLICY CHANGES EFFECTIVE 01/08/14	COMPANY Wesco, CA, Prem-Auto
NAMED INSURED GOLDEN VALLEY CONSTRUCTION INC GOLDEN VISTA CONSTRUCTION DBA:		AUTHORIZED REPRESENTATIVE Jim Furey
COVERAGE PARTS AFFECTED ITEM THREE - SCHEDULE OF COVERED AUTOS YOU OWN		


CHANGES

ADDITIONAL INSURED CA990009 ATTACHED

ALL OTHER TERMS AND CONDITIONS REMAIN UNCHANGED.

IL 12 01 11 85

Copyright, Insurance Services Office, Inc. 1983
Copyright, ISO Commercial Risk Services, Inc. 1983


 Authorized Representative Signature

01/10/14
Handler # 185

WORKERS COMPENSATION AND EMPLOYERS LIABILITY INSURANCE POLICY

WC 04 03 06

(Ed. 4-84)

WAIVER OF OUR RIGHT TO RECOVER FROM OTHERS ENDORSEMENT-CALIFORNIA

We have the right to recover our payments from anyone liable for an injury covered by this policy. We will not enforce our right against the person or organization named in the Schedule. (This agreement applies only to the extent that you perform work under a written contract that requires you to obtain this agreement from us.)

You must maintain payroll records accurately segregating the remuneration of your employees while engaged in the work described in the Schedule.

The additional premium for this endorsement shall be 2% of the California workers' compensation premium otherwise due on such remuneration.

Schedule

Any person or organization as required by written contract. \$590.00

This endorsement changes the policy to which it is attached and is effective on the date issued unless otherwise stated.

Endorsement Effective	3/31/2013	Policy No.	WWC3057142	Endorsement No.	WC040306
Insured	Golden Vista Construction, Inc. (a corp)			Premium \$	22610
Insurance Company	Wesco Insurance Company				

Countersigned by





Century Surety Company

465 Cleveland Avenue
Westerville, Ohio 43082
www.centurysurety.com

COMMERCIAL EXCESS LIABILITY POLICY

Item	1 POLICY NO.: CCP 821166 New NAMED INSURED AND MAILING ADDRESS: GOLDEN VALLEY CONSTRUCTION 44815 FIG AVE. #117 LANCASTER CA 93534		CODE NO. :5909K INSUREDS AGENT: SOUTHLAND INSURANCE BROKERS 19069 VAN BUREN BLVD. #114-484 RIVERSIDE CS 92508																																																	
2 INSURED LOCATION:	<input type="checkbox"/> Same as Mailing Address Above		If Different Than Mailing Show Below: SEE ENDT A FOR LOCATIONS																																																	
3	POLICY PERIOD: From: 05/15/2013 To: 05/11/2014 at 12:01 A.M. Standard time at your mailing address shown above. Business Description: GRADING AND PAVING CONTRACTOR <input type="checkbox"/> Individual <input type="checkbox"/> Joint Venture <input type="checkbox"/> Partnership <input type="checkbox"/> Limited Liability Company (LLC) <input checked="" type="checkbox"/> Organization (Other than Partnership or Joint Venture)																																																			
4	LIMIT OF LIABILITY (a) Each Occurrence \$ 2,000,000 (b) Aggregate Limit (where applicable) \$ 2,000,000 (c) Self Insured Retained Limit \$ N/A																																																			
5	PREMIUM COMPUTATION: <table style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 30%;">Premium:</td> <td style="width: 10%;">\$</td> <td style="width: 20%;">4,785</td> <td style="width: 10%; text-align: center;">X</td> <td style="width: 10%;">Flat</td> <td style="width: 10%;">Adjustable</td> </tr> <tr> <td>Adjustable Rate:</td> <td>\$</td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Premium Basis:</td> <td>\$</td> <td>N/A</td> <td></td> <td>Sales</td> <td>Payroll</td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> <td colspan="2" style="text-align: center;">Primary Premium</td> </tr> <tr> <td>Annual Minimum Premium:</td> <td>\$</td> <td>4,785</td> <td></td> <td></td> <td></td> </tr> <tr> <td>Advance Premium:</td> <td>\$</td> <td>4,785</td> <td></td> <td></td> <td></td> </tr> <tr> <td>Trial Coverage:</td> <td>\$</td> <td>REJECTED</td> <td></td> <td></td> <td>CA SURPLUS LINES TAX \$143.55</td> </tr> <tr> <td>Total Premium:</td> <td>\$</td> <td>4,785</td> <td></td> <td></td> <td>CA STAMPING FEE \$9.57</td> </tr> </table>				Premium:	\$	4,785	X	Flat	Adjustable	Adjustable Rate:	\$					Premium Basis:	\$	N/A		Sales	Payroll					Primary Premium		Annual Minimum Premium:	\$	4,785				Advance Premium:	\$	4,785				Trial Coverage:	\$	REJECTED			CA SURPLUS LINES TAX \$143.55	Total Premium:	\$	4,785			CA STAMPING FEE \$9.57
Premium:	\$	4,785	X	Flat	Adjustable																																															
Adjustable Rate:	\$																																																			
Premium Basis:	\$	N/A		Sales	Payroll																																															
				Primary Premium																																																
Annual Minimum Premium:	\$	4,785																																																		
Advance Premium:	\$	4,785																																																		
Trial Coverage:	\$	REJECTED			CA SURPLUS LINES TAX \$143.55																																															
Total Premium:	\$	4,785			CA STAMPING FEE \$9.57																																															
6	25 % of the Policy Premium is fully earned as of the effective date of this policy and is not subject to return or refund.																																																			
7	During the past year no insurer has cancelled any similar insurance issued to the named insured, nor declined to issue such insurance, unless otherwise stated herein. ** ** ABSENCE OF AN ENTRY MEANS " NO EXCEPTION "																																																			
8	Service of Suit (if form CCP 2010 is attached) may be made upon: Crump Insurance Services, Inc. 8105 Irvine Center Drive Suite 450 Irvine CA 92618																																																			
9	FORMS AND ENDORSEMENTS: Forms and Endorsements applying to this Coverage and made part of this policy at time of issue : See Attached Schedule of Forms, CIL 1500b 02 02																																																			

Any person who, with intent to defraud or knowing that he is facilitating a fraud against an insurer, submits an application or files a claim containing false or deceptive statement is guilty of insurance fraud.

COMPANY REPRESENTATIVE:

Crump Insurance Services, Inc.
8105 Irvine Center Drive
Suite 450
Irvine CA 92618

06/11/2013 DS

Countersigned By _____

Authorized Representative

IN WITNESS WHEREOF, this Company has executed and attested these presents; but this policy shall not be valid unless countersigned by the duly Authorized Agent of this Company at the Agency hereinbefore mentioned.

Secretary

President



Century Surety Company

COMMERCIAL EXCESS LIABILITY POLICY

SCHEDULE OF UNDERLYING INSURANCE

Policy No: CCP 821166

Effective Date: 05/15/2013 **
12:01 A.M. Standard Time

NAMED INSURED: GOLDEN VALLEY CONSTRUCTION

CARRIER, POLICY NUMBER, POLICY PERIOD	TYPE OF POLICY	APPLICABLE LIMITS OF LIABILITY
NOT COVERED	Employers Liability	Coverage B - Employers' Liability \$ NOT COVERED each accident \$ NOT COVERED disease policy limit \$ NOT COVERED disease each employee
WESCO 05/11/2013 TO 05/11/2014 POLICY NUMBER AS PER ON FILE WITH COMPANY	Commercial General Liability <input type="checkbox"/> Non Owned Auto <input type="checkbox"/> Hired Auto	Bodily Injury/Property Damage Liability \$ 2,000,000 General Aggregate Limit (other than Prods/Comp Ops) \$ 2,000,000 Products/Completed Operations Aggregate Limit \$ 1,000,000 Personal and Advertising Injury Limit \$ 1,000,000 Each Occurrence Limit
WESCO 05/11/2013 TO 05/11/2014 POLICY NUMBER AS PER ON FILE WITH COMPANY	Automobile Liability	Bodily Injury Liability \$ NOT COVERED each person \$ NOT COVERED each occurrence Property Damage Liability \$ NOT COVERED each occurrence Bodily Injury/Property Damage Liability Combined Single Limit \$ 1,000,000 each occurrence
NOT COVERED		

Policy Number: CCP 821166 01

CIL 15 00b 02 02

SCHEDULE OF FORMS AND ENDORSEMENTS

(other than applicable forms and endorsements shown elsewhere in the policy)

Forms and Endorsements applying to the Coverage Parts listed below and made a part of this policy at time of issue:

Form/ Endt. #	Edition Date	Title	Total # of Forms Selected: 19
Forms Applicable to this Coverage part - INTERLINE-ALL COVERAGE PARTS			
CAPN	0002 07 11	D2 Notice Form	
CCP	2010 05 08	Service of Suit Clause	
CIL	1500B 02 02	Schedule of Forms and Endorsements	
CSCP	1000 02 04	Century Surety Company Policy Jacket	
IL	0003 09 08	Calculation of Premium	
IL	0017 11 98	Common Policy Conditions	
IL	1201 11 85	General Purpose Endorsement	
PRIV	0001 11 09	Privacy Statement	
TRIA	0001 10 08	Policyholder Disclosure Notice of Terrorism	

9 Forms

Forms Applicable to this Coverage part - EXCESS

CUP	1503 07 07	Exclusion - Employee Benefits	
CUP	1512 07 07	Exclusion - Assault And Battery	
CUP	1516 07 07	Cyber, Media, Internet Exclusion Endorsement	
CUP	1517 07 07	Terrorism Exclusion Endorsement	
CUP	1522 05 09	Exclusion - Recording And Distribution Of Material Or Info	
CUP	2123 07 07	Nuclear Energy Liability Exclusion Endorsement	
CXL	1500 05 09	Commercial Excess Liability Policy Declarations	
CXL	1500a 07 07	Schedule Of Underlying Insurance	
CXL	1501 12 11	Commercial Excess Liability Coverage Part	
CXL	1551 02 12	Contractors Commercial Liability Special Exclusions And Limitations Endorsement	

10 Forms

COMMON POLICY CONDITIONS

All Coverage parts included in this policy are subject to the following conditions.

A. Cancellation

1. The first Named Insured shown in the Declarations may cancel this policy by mailing or delivering to us advanced written notice of cancellation.
2. We may cancel this policy by mailing or delivering to the first Named Insured written notice of cancellation at least:
 - a. 10 days before the effective date of cancellation if we cancel for nonpayment of premium; or
 - b. 30 days before the effective date of cancellation if we cancel for any other reason.
3. We will mail or deliver our notice to the first Named Insured's last mailing address known to us.
4. Notice of cancellation will state the effective date of cancellation. The policy period will end on that date.
5. If this policy is cancelled, we will send the first Named Insured any premium refund due. If we cancel, the refund will be pro rata. If the first Named Insured cancels, the refund may be less than pro rata. The cancellation will be effective even if we have not made or offered a refund.
6. If notice is mailed, proof of mailing will be sufficient proof of notice.

B. Changes

This policy contains all the agreements between you and us concerning the insurance afforded. The first named Insured shown in the Declarations is authorized to make changes in the terms of this policy with our consent. This policy's terms can be amended or waived only by endorsement issued by us and made a part of this policy.

C. Examination Of Your Books And Records

We may examine and audit your books and records as they relate to this policy at any time during the policy period and up to three years afterward.

D. Inspections And Surveys

1. We have the right to:
 - a. Make inspections and surveys at any time;

- b. Give you reports on the conditions we find; and

- c. Recommend changes.

2. We are not obligated to make any inspections, surveys, reports or recommendations and any such actions we do undertake relate only to insurability and the premiums to be charged. We do not make safety inspections. We do not undertake to perform the duty of any person or organization to provide for the health or safety of workers or the public. And we do not warrant that conditions:
 - a. Are safe or healthful; or
 - b. Comply with laws, regulations, codes or standards.

3. Paragraphs 1. and 2. of this condition apply not only to us, but also to any rating, advisory, rate services or similar organization which makes insurance inspections, surveys, reports or recommendations.

4. Paragraph 2. of this condition does not apply to any inspections, surveys, reports or recommendations we may make relative to certification, under state or municipal statutes, ordinances or regulations, of boilers, pressure vessels or elevators.

E. Premiums

The first Named Insured shown in the Declarations:

1. Is responsible for the payment of all premiums; and
2. Will be the payee for any return premiums we pay.

F. Transfer Of Your Rights And Duties Under This Policy

Your rights and duties under this policy may not be transferred without our written consent except in the case of death of an individual named insured.

If you die, your rights and duties will be transferred to your legal representative but only while acting within the scope of duties as your legal representative. Until your legal representative is appointed, anyone having proper temporary custody of your property will have your rights and duties but only with respect to that property.



- Company Profile
- Company Search
- Company Search Results
- Company Information
- Old Company Names
- Agent for Service
- Reference Information
- NAIC Group List
- Lines of Business
- Workers' Compensation Complaint and Request for Action/Appeals Contact Information
- Financial Statements PDF's
 - Annual Statements
 - Quarterly Statements
- Company Complaint
 - Company Performance & Comparison Data
 - Company Enforcement Action
 - Composite Complaints Studies
- Additional Info
 - Find A Company Representative In Your Area
 - View Financial Disclaimer

COMPANY PROFILE

Company Information

WESCO INSURANCE COMPANY

**59 MAIDEN LANE
NEW YORK, NY 10038
212222027120**

Old Company Names

Effective Date

Agent For Service

KAREN HARRIS
C/O CORPORATION SERVICE COMPANY
2710 GATEWAY OAKS DRIVE, SUITE 150N
SACRAMENTO CA 95833-3505

Reference Information

NAIC #:	25011
California Company ID #:	4378-6
Date Authorized in California:	09/24/1996
License Status:	UNLIMITED-NORMAL
Company Type:	Property & Casualty
State of Domicile:	DELAWARE

back to top

NAIC Group List

NAIC Group #: 2538 Amtrust Grp

Lines Of Business

The company is authorized to transact business within these lines of insurance. For an explanation of any of these terms, please refer to the glossary.

- AUTOMOBILE
- BOILER AND MACHINERY
- BURGLARY
- COMMON CARRIER LIABILITY
- CREDIT
- DISABILITY
- FIRE
- LIABILITY
- MARINE
- MISCELLANEOUS
- PLATE GLASS
- SPRINKLER
- SURETY
- TEAM AND VEHICLE
- WORKERS' COMPENSATION

Berkley Regional Specialty Insurance Company (Delaware)	04/12/2012
Berkshire Hathaway International Insurance Limited (UK)	04/01/2008
Bracken Hill Specialty Insurance Company Inc. (Illinois) (Name changed from Hiscox Specialty Insurance Company Inc. effective 07/09/2012)	10/08/2010
Burlington Insurance Company (North Carolina)	11/17/1995
Canopus US Insurance, Inc. (Delaware) (Name changed from Omega US Insurance, Inc. effective 08/20/2012)	07/20/2011
Capitol Specialty Insurance Corporation (Wisconsin)	05/15/2008
Catlin Insurance Company (UK) Limited	04/10/2007
Catlin Specialty Insurance Company (Delaware) (Name changed from Wellington Specialty Insurance Company effective 03/31/2007)	06/14/2006
Century Surety Company (Ohio)	09/01/1995
Chubb Custom Insurance Company (New Jersey) (Domicile changed from Delaware to New Jersey, effective 04/01/2013)	08/04/1995
The Cincinnati Specialty Underwriters Insurance Company (Delaware)	01/31/2011
Colony Insurance Company (Virginia)	09/01/1995
Colony National Insurance Company (Virginia) (Name changed from Preferred National Insurance Company effective 04/01/2002)	12/17/1996
Columbia Casualty Company (Illinois)	07/06/1995
Companion Specialty Insurance Company (District of Columbia)	07/20/2011
Covington Specialty Insurance Company (New Hampshire)	07/20/2011
Crum & Forster Specialty Insurance Company (Arizona) (Name changed from Transnational Insurance Company effective 12/26/2000. Domicile changed from Connecticut to Arizona effective 02/12/2002.)	04/20/1998
CUMIS Specialty Insurance Company, Inc. (Iowa)	05/15/2008
Darwin Select Insurance Company (Arkansas) (Name changed from ULICO Indemnity Company effective 05/02/2005)	12/22/1995

[Back to Top](#)**E - G**

Insurer	Date Approved
Empire Indemnity Insurance Company (Oklahoma)	12/01/1995
Endurance American Specialty Insurance Company (Delaware) (Name changed from Traders & Pacific Insurance Company effective 06/08/2006)	02/23/1996
Energy Insurance Mutual Limited (Barbados)	12/17/1997
Essex Insurance Company (Delaware)	07/06/1995
Evanston Insurance Company (Illinois)	08/11/1995
Everest Indemnity Insurance Company (Delaware)	08/14/1998
Executive Risk Specialty Insurance Company (Connecticut)	09/01/1995
Fireman's Fund Insurance Company of Ohio (Ohio)	05/19/1999
First Mercury Insurance Company (Illinois)	10/16/1997
First Specialty Insurance Corporation (Missouri)	09/01/1995
Founders Insurance Company (Illinois)	10/16/2007
Gemini Insurance Company (Delaware)	02/23/1998
General Security Indemnity Company of Arizona (Arizona) (Name changed from Fulcrum Insurance Company effective 05/03/2002)	09/01/1995
General Star Indemnity Company (Delaware) (Domicile changed from Connecticut to Delaware, effective 12/31/2012)	08/11/1995
Gotham Insurance Company (New York)	08/04/1995



COUNTY OF RIVERSIDE

TRANSPORTATION AND LAND MANAGEMENT AGENCY



Transportation Department

Juan C. Perez, P.E., T.E.
Director of Transportation

December 20, 2013

Jason A. Mordhorst, Vice President
Hazard Construction Company
6465 Marindustry Place
San Diego, CA 92121

**RE: Response to Bid Protest Letter
Mecca Group 4 Street Improvement Project
Coahuilla Street, Date Palm Street and 4th Street, Community of Mecca
Project No. C1-0654, State Project No. SR2SL-5956(215)**

Dear Mr. Mordhorst:

We received a letter from your company dated December 13, 2013 regarding the above referenced project (attached). On December 11, 2013, seven (7) bids were received in the Office of Director of Transportation and Land Management for the subject project. After the public bid opening, Golden Vista Construction, Inc. dba Golden Valley Construction (Golden Valley) was announced as the apparent low bidder and Hazard Construction Company (Hazard) was the second low bidder. See attached bid summary for information regarding the all 7 received bids.

Your request to declare Golden Valley as a non-responsive bidder, and award this project to the second low bidder, Hazard, is denied.

At the bid opening, a Hazard representative, requested to review Golden Valley's Bid documents. Your company's representative was granted this request immediately after all bid opening attendees were dismissed. Your representative did not make any comments about Golden Valley's Bid at that time.

On Friday December 13, 2013, I received your phone call and provided you, by e-mail, a scanned copy of the Bid documents received from Golden Valley. You were also offered to review the original Bid documents in our office. After your company's review of the Bid documents, a bid protest letter was submitted.

Your letter basically discusses two subjects for grounds to declare the apparent low bidder as non-responsive: failure to acknowledge all of the addenda received and failure to sign the Bid forms with the signature of a properly authorized representative from Golden Valley.

Addenda Acknowledgement

As you are aware, Golden Valley wrote the number "3" on page B1. The list of 1, 2, and 3 was not written, however, Golden Valley submitted a copy of the addendum and acknowledgement signature page with Golden Valley's signature for each addendum received: Addendum No. 1, Addendum No. 2, and Addendum No. 3. It was not required for Golden Valley to submit each addendum; nevertheless, this documentation, submitted by Golden Valley, for Addenda acknowledgement is acceptable and responsive. The minor bid irregularity of not listing each addendum on page B1 of the Bid is waived by the County.

Authorized Signature

- Your company's review of the Bid states that the signature of Mike Honz, General Manager, is throughout the Bid documents submitted by Golden Valley. All submitted bid documents, with the exception of the Bid Bond, has Mike Honz' signature.
- At the bottom of the Bidder Data and Signature on Page B7 of the Contract Documents states: "(If the Bidder is a Corporation, attach the Corporate Resolution which authorizes the signature to represent the Corporation. Certification for Authorized Signatures of Officers and Certificate of Incumbency are also acceptable and document must show that person who signs is authorized to do so for the company.)"
- Your company's review of the Bid states that Golden Valley failed to provide a Corporate Resolution, Certification for Authorized Signatures of Officers or Certificate of Incumbency authorizing Mike Honz to sign the Bid documents on behalf of the Corporation.
- The submitted Bid includes a letter dated December 5, 2013, on Golden Valley letter head, written and signed by Michael Emerson (President) giving authority to Mr. Michael Honz to sign as General Manager and act on behalf of Golden Valley.
- Your company claims that providing a letter from the President, Michael Emerson giving authority to sign to Mr. Michael Honz does not meet the requirement to provide a Corporate Resolution, Certification for Authorized Signatures of Officers or Certificate of Incumbency and is invalid.
- During our review of the of the Bid documents, we were able to confirm that Michael Emerson is the Responsible Managing Officer and President of Golden Valley. Golden Valley also proved they had a Corporate Resolution on file. See attached Corporate Resolution dated 12/2/2013 approving and authorizing Mike Honz, General Manager of the Palm Springs Division to be a signer on behalf of Golden Valley.
- We recognize that there are several instruments that a corporation can approve and authorize a person to sign on its behalf. The chief purpose of the bid requirement is to solicit evidence of authority to act on behalf of the bidder. The letter dated December 5, 2013 was submitted with the Bid and was signed by the president of the corporation, an individual authorized to act for the corporation. This is responsive to the request for evidence of authority to sign on behalf of the bidder and the form is a minor irregularity waived by the County.

Please refer to "Instruction to Bidder" Section 14, "Bids" (3rd paragraph on page A8). The County reserves the right, as stated in these provisions, to make a determination regarding such items. The Addenda acknowledgement for this Bid is a minor bid irregularity that the County deems waived. After verifying and confirming Michael Emerson's company position and authority, Golden Valley's letter submitted with the Bid is acceptable. These two matters are minor irregularities which will be waived at the County's discretion to best protect the public interest in the prompt commencement and economical completion of this project.

The County intends to award to Golden Valley which is the responsive low bidder for this project.

Response to Hazard Construction Company Bid Protest Letter

December 20, 2013

Page 3 of 3

If you have any questions or need additional information, please contact me at your convenience at (951) 955-1537.

Sincerely,



**Joel Jimenez, P.E.
Senior Civil Engineer
Contracts / Bidding Unit**

JRJ:jjr:sb

Attachments: Copy of Hazard Construction letter dated December 13, 2013
Copy of Bid Summary
Copy of Golden Valley Letter dated December 5, 2013 (originally included with the Bid)
Copy of Golden Valley Corporate Resolution dated December 2, 2013

cc: Khalid Nasim / Cathy Wampler / Hugh Smith, Transportation Department
Marsha Victor, County Counsel
Chronological File
Construction/Inspection File
Project File with Attachments



Phone (858) 587-3600
Fax (858) 453-6034
6465 Marindustry Place
San Diego, CA 92121
hazardconstruction.com
License No. 750542A/B

December 13, 2013

County of Riverside
Transportation Department
3525 14th Street
Riverside, CA 92501
Attention: Contracts/Bidding Unit: Joel Jimenez

Project: Mecca Group 4 Street Improvement Project
County Project No.C1-0654, State Project No.SR2SL-5956(215)

Subject: Bid Protest of Apparent Low Bidder

Dear Mr. Jimenez:

Hazard Construction ("Hazard") has reviewed the Bid forms as submitted by the apparent low bidder, Golden Valley Construction ("Golden Valley") and asks that the County of Riverside find Golden Valley non-responsive due to failure to acknowledge all of the addendums issued for the project and failure to sign the bid forms with a properly authorized signature that represents the Corporation.

Section 8 - Addenda, page A4, second paragraph states "To be considered responsive, the Bid must list and take into account all issued Addenda." The third paragraph goes on to state "In addition to listing the acknowledged addenda (if any) on the Bid, Bidders should submit each addendum's acknowledgement signature page and attach each one to the Bid." Page B1 of the Bid documents, submitted by Golden Valley, indicate that they have acknowledged only addenda #3 (See Attached). They have failed to acknowledge Addenda #1 dated November 20, 2013 and Addenda #2 dated December 4, 2013. Failure to acknowledge addenda on the Bid form as required by the specifications stated above is grounds for finding the Bid Non-Responsive.

Page B7 of the Bid Documents, last paragraph states "If the Bidder is a Corporation, attach the Corporate Resolution which authorizes the signature to represent the Corporation. Certification for Authorized Signatures of Officers and Certificate of Incumbency are also acceptable and document must show that person who signs is authorized to do so for the company." The Bid Documents submitted by Golden Valley have the signature of Mike Honz, General Manager throughout. Golden Valley is a Corporation in the State of California and failed to provide a Corporate Resolution, Certification for Authorized Signatures of Officers or Certificate of Incumbency authorizing Mike Honz to sign the Bid documents on behalf of the Corporation. Providing a letter from the President, Michael Emerson giving authority to sign to Mr. Michael Honz does not meet the requirement to provide a Corporate Resolution, Certification for Authorized Signatures of Officers or Certificate of Incumbency and is invalid. As such, the Bid is invalid as it has not be signed by an authorized representative for the Corporation.

Hazard Construction ("Hazard") hereby protests any award to Golden Valley because they are non-responsive due to two different reasons stated above. We ask that the County of Riverside award the contract to Hazard, the true apparent low bidder, having met all of the requirements of the contract.

If you have any questions regarding any of these matters or need further clarification, please do not hesitate to call myself at the main office. Thank you for your attention to this matter.

Sincerely,
HAZARD CONSTRUCTION COMPANY



Jason A. Mordhorst
Vice President

cc: Bid File
Attachment
