

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



864  
A

**FROM:** TLMA - Transportation Department

**SUBMITTAL DATE:**  
May 13, 2010

**SUBJECT:** Construction of Clinton Street from Miles Avenue to Fred Waring Drive, Indio area.

**RECOMMENDED MOTION:** That the Board accept the low bid of Cooley Construction, Inc. of Hesperia, CA in the amount of \$2,924,295. Award the contract to that firm and authorize the Chairman of the Board to execute the contract documents. Amend the TIP by approval of the proposed project budget shown on Attachment A.

**BACKGROUND:** By Minute Order dated April 6, 2010 (agenda item 3.76) the Board authorized the Clerk of the Board to advertise for the construction of Clinton Street from Miles Avenue to Fred Waring Drive, Indio area. Bids for the project were opened in the office of the Director of Transportation at 2:00 PM, Wednesday, April 28, 2010. Seven bids were received. The Transportation Department's established basis for the selection of a contractor is the lowest

Juan C. Perez  
Director of Transportation

JCP:jj:sb  
(Continued On Attached Pages)

<b>FINANCIAL DATA</b>	Current F.Y. Total Cost:	\$ 2,924,595	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2009/2010

<b>SOURCE OF FUNDS:</b> TUMF [CVAG] (95.08%), Proposition 42 (1.91%), Miscellaneous [Valley Sanitation District] (2.64%), Miscellaneous [Imperial Irrigation District] (0.37%)	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

**C.E.O. RECOMMENDATION:**

APPROVE

BY:   
Tina Grande

County Executive Office Signature

**MINUTES OF THE BOARD OF SUPERVISORS**

On motion of Supervisor Stone, seconded by Supervisor Benoit and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Buster, Tavaglione, Stone, Benoit and Ashley  
Nays: None  
Absent: None  
Date: May 25, 2010  
xc: Transp.

Kecia Harper-Ihem  
Clerk of the Board  
By:   
Deputy

Prev. Agn. Ref. 4/6/10, Item 3.76 | District: 4 | Agenda Number:

3.57

ATTACHMENTS FILED  
WITH THE CLERK OF THE BOARD

FORM APPROVED BY COUNTY COUNSEL  
BY: NEAL R. KIPNIS  
DATE: 5/17/10  
Departmental Concurrence

Dep't Recomm.:  Policy  
Per Exec. Ofc.:  Policy  
 Consent  
 Consent

The Honorable Board of Supervisors

RE: Construction of Clinton Street from Miles Avenue to Fred Waring Drive, Indio area.

May 13, 2010

Page 2

responsive and responsible bid for all schedules of work. The lowest and best total bid was submitted by Cooley Construction, Inc. of Hesperia, CA in the amount of \$2,924,595. The total bid price, submitted by Cooley Construction, Inc., is \$1,239,015 (29.76%) below the Engineer's Estimate.

The widening of Clinton Street represents the third and final phase of a project to construct the Miles Avenue bridge over the Whitewater River (Phase 1 award; January 15, 2008, Item 3.45), widen Miles Avenue to four lanes from the Whitewater River to Clinton Street (Phase 2A award; February 24, 2009, Item 3.54) and widen Clinton Street to four lanes from Miles Avenue to Fred Waring Drive (Phase 2B).

The principle scope of work (Base Bid Schedule) is being financed by the County of Riverside, City of Indio, and the Coachella Valley Association of Governments (CVAG) under the terms of a cooperative agreement executed between and among the County of Riverside, City of Indio and CVAG (September 4, 2007, Item 3.39). This cooperative agreement includes a provision for CVAG to provide a loan to the County for funding of its portion of the project with reimbursement to be made, by the County, over a period of 10 years.

The project is within both the City of Indio and the County of Riverside. This final phase of the project will reconstruct and widen Clinton Street between Miles Avenue and Fred Waring Drive to provide four through lanes of traffic and modify the traffic signals at:

1. Clinton Street and Miles Avenue
2. Clinton Street and Palmyra Avenue and Lyndon B. Johnson Elementary School

The traffic signal modifications will provide protected traffic movements and improve traffic safety.

The award documents include the following schedules of work:

- Base Bid: Primary items of work.
- Alternate A: Domestic water line extension and improvements, adjustment of water valve covers and the relocation of fire hydrants. This work is the responsibility of the Indio Water Authority. However, the County will fund the work in exchange for road improvements previously performed by the City on County right of way on Clinton Street.
- Alternate B: Manhole adjustment, to be funded by Valley Sanitation District, under the terms of a letter agreement to be executed prior to or concurrently with the submission of the construction contract for award.
- Alternate C: Construction of conduits, transformer pad and a medium manhole enclosure, to be funded by Imperial Irrigation District, under the terms of a letter agreement to be executed prior to or concurrently with the submission of the construction contract for award.

The Honorable Board of Supervisors

RE: Construction of Clinton Street from Miles Avenue to Fred Waring Drive, Indio area.

May 13, 2010

Page 3

We have requested concurrence from each utility owner and anticipate approval to award the alternate bid schedules as bid by the apparent low bidder. These alternate bid schedules are therefore included in the submitted contract for award. The costs for the work to be performed under Alternate Bid Schedules "B" and "C" will be funded by the respective utility owners. In the event that the utility owners do not provide final approval, these items will be deducted from the contract and the work will be done by the utilities.

The Contractor is in the process of executing the contract and providing bonds and insurance documents. There is great urgency on the part of the City of Indio to have us do this work this Summer while school is on break. Approval of this Form 11 will allow the Contractor to start ordering material ahead of the final executed contract. The Contractor is qualified.

A cooperative agreement was executed between the County, CVAG and the City of Indio on September 4, 2007 as item 3.39. Terms of that agreement provide that CVAG front CVAG's 75% share of costs plus the 12.5% County share and the 12.5% City share. County and City shares are to be paid back to CVAG over a ten year period, with interest. The first installment is due the fiscal year after completion of all work, which will be FY 11/12. The Transportation Department will program reimbursement to CVAG as part of the annual Transportation Improvement Program using District IV Road Funds. Annual installments for all three projects are estimated to be \$275,000, subject to final costs.

Project No: B2-03892

WHEN DOCUMENT IS FULLY EXECUTED RETURN

**CLERK'S COPY**

to Riverside County Clerk of the Board, Stop 1010  
Post Office Box 1147, Riverside, Ca 92502-1147  
Thank you.

Riverside County Contract No. 10-05-007

**AGREEMENT**

THIS AGREEMENT is entered into at Riverside, California as of the date set forth below is between County of Riverside hereafter called "County" and **Cooley Construction, Inc.**, hereafter called "Contractor".

W I T N E S S E T H

RECITALS:

1. Contractor has submitted to County his Contractor's Proposal for the construction of County Project, **Clinton Street in the City of Indio and County of Riverside Street Improvement Plans, Project No. B2-03892**, in strict accordance with the Contract Documents identified below and County has accepted said Proposal.
2. Contractor states that he has reexamined his Contractor's Proposal and found it to be correct, has ascertained that his subcontractors are properly licensed and possess the requisite skill and forces, has reexamined the site and Contract Documents and is of the opinion that he can presently do the work in accordance with the Contract Documents for the money set forth in his Proposal to be paid as provided in the Contract Documents.

AGREEMENT:

IT IS AGREED BY THE PARTIES AS FOLLOWS:

1. Contract Documents. The entire contract consists of the following: (a) The Agreement. (b) The Notice Inviting Bids. (c) The Instruction to Bidders. (d) The Contractor's Proposal. (e) The Bid Bond. (f) The Payment Bond. (g) The Performance Bond. (h) The General Conditions. (i) The Special Provisions. (j) The Standard Specifications of the State of California Department of Transportation edition of May 2006 as modified in other portions of the Contract Documents. (k) The Standard Plans of the Department of Transportation identified on the plans or in the Special Provisions. (l) The Plans. (m) Addenda **No.1**. (n) The Determination of Prevailing Wage Rates for Public Work. (o) Any Change Orders issued. (p) Any additional or supplemental specifications, notice, instructions and drawings issued in accordance with the provisions of the Contract Documents. All of said Documents presently in existence are by this reference incorporated herein with like effect as if here set forth in full and upon the proper issuance of other documents they shall likewise be deemed incorporated. The Bid Bond is exonerated upon execution of this Agreement and the Payment Bond and Faithful Performance Bond.
2. The Work. Contractor shall do all things necessary to construct the work generally described in Recital No. 1 in accordance with the Contract Documents.

3. Liquidated Damages and Time of Completion. Attention is directed to the provisions in Section 8-1.06, "Time of Completion", and in Section 8-1.07, "Liquidated Damages", of the Standard Specifications and these Special Provisions.

The Contractor shall begin work within 15 days of the date stated within the written "Notice to Proceed".

The Contractor shall notify the Engineer, in writing, of his intent to begin work at least 72 hours before work is begun. The notice shall be delivered to the Transportation Department's Construction Engineer and shall specify the date the Contractor intends to start. If the project has more than one location of work, a separate notice shall be given for each location.

Should the Contractor begin work in advance of receiving a written "Notice to Proceed", any work performed by him in advance of the date stated in the "Notice to Proceed" shall be considered as having been done by him at his own risk and as a volunteer and subject to the following:

- (1) The Contractor shall, on commencing operations, take all precautions required for public safety and shall observe all the provisions in the Specifications and the Special Provisions.
  - (2) All work done according to the contract prior to the issuance of the "Notice to Proceed", will be considered authorized work and will be paid for as provided in the contract.
  - (3) The Contractor shall not be entitled to any additional compensation or an extension of time for any delay, hindrance or interference caused by or attributable to commencement of work prior to the issuance of the "Notice to Proceed".
4. Compensation. Contractor shall be paid in the manner set forth in the Contract Documents the amount of his Proposal as accepted by County, the above rates, subject to additions and deductions as provided in the Contract Documents. Said Proposal is on file in the Office of the Clerk of the Board of Supervisors of County.

**CLINTON STREET  
IN THE CITY OF INDIO AND COUNTY OF RIVERSIDE**

**STREET IMPROVEMENT PLANS**

**PROJECT NO. B2-03892**

**AGREEMENT**

ITEM No.	ITEM CODE	ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
1	999990	MOBILIZATION	LS	1	90,000.00	90,000.00
2	160101	CLEARING AND GRUBBING	LS	1	147,000.00	147,000.00
3	066102	DUST ABATEMENT	LS	1	7,300.00	7,300.00
4	170101	DEVELOP WATER SUPPLY	LS	1	3,200.00	3,200.00
5	066105	RESIDENT ENGINEERS OFFICE	LS	1	8,400.00	8,400.00
6	074020	WATER POLLUTION CONTROL	LS	1	10,600.00	10,600.00
7	190101	ROADWAY EXCAVATION	CY	10,300	15.50	159,650.00
8	220101	FINISHING ROADWAY	LS	1	13,700.00	13,700.00
9	120100	TRAFFIC CONTROL SYSTEMS	LS	1	41,000.00	41,000.00
10	153103	COLD PLANE ASPHALT CONCRETE PAVEMENT [0.15' MAXIMUM]	SQYD	1,320	4.20	5,544.00
11	390130	HOT MIX ASPHALT	TON	3,680	74.00	272,320.00
12	013901	ASPHALT RUBBER HOT MIX	TON	2,080	92.00	191,360.00
13	260201	CLASS 2 AGGREGATE BASE	CY	5,960	27.70	165,092.00
14	731516	MINOR CONCRETE (DRIVEWAY)	SQFT	7,940	4.30	34,142.00
15	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	3,760	17.40	65,424.00
16	017310	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207)	EA	17	1,280.00	21,760.00
17	017312	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207A)	EA	5	4,350.00	21,750.00
18	017317	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	6,500	8.90	57,850.00
19	731521	MINOR CONCRETE (SIDEWALK)	SQFT	22,700	4.40	99,880.00
20	017309	MINOR CONCRETE (TYPE "D" CURB) (CRS 204)	LF	15	43.00	645.00
21	000003	MINOR CONCRETE (TYPE "D-1" CURB) (CRS 203)	LF	20	35.00	700.00
22	510503	MINOR CONCRETE (STRUCTURE) [CONCRETE BULKHEAD-RCFC&WCD M816] [66" BULKHEAD]	EA	1	1,700.00	1,700.00
23	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	4	3,140.00	12,560.00
24	017316	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	15	2,400.00	36,000.00
25	000003	INSTALL 24" BOX TREE [ACACIA ANEURA MULGA / PINUS ELDARICA TREES]	EA	8	424.00	3,392.00
26	000003	REMOVE AND REINSTALL STREET LIGHT PER COI STD 202	EA	7	1,200.00	8,400.00
27	000003	ADJUST STORM DRAIN MANHOLE TO GRADE	EA	2	1,080.00	2,160.00

## AGREEMENT (CONTINUED)

ITEM No.	ITEM CODE	ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
28	518201	MASONRY BLOCK WALL	SQFT	650	48.40	31,460.00
29	833088	TUBULAR HANDRAILING	LF	184	60.00	11,040.00
30	650014	18" REINFORCED CONCRETE PIPE	LF	655	63.00	41,265.00
31	000003	24" REINFORCED CONCRETE PIPE	LF	340	70.00	23,800.00
32	000003	66" REINFORCED CONCRETE PIPE	LF	2,812	198.00	556,776.00
33	000003	REINFORCED CONCRETE 4'X6' TRANSITION STRUCTURE	EA	1	11,600.00	11,600.00
34	017003	CATCH BASIN (CURB INLET) (CRS 300)	EA	23	6,600.00	151,800.00
35	017101	MANHOLE (RCFC&WCDS MH 251)	EA	6	5,300.00	31,800.00
36	017103	MANHOLE (RCFC&WCDS MH 252)	EA	7	6,500.00	45,500.00
37	000003	JUNCTION STRUCTURE (RCFC&WCDS JS 227)	EA	11	1,770.00	19,470.00
38	840656	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,000	0.35	4,900.00
39	840515	THERMOPLASTIC PAVEMENT MARKING	SQFT	1,400	4.20	5,880.00
40	850102	PAVEMENT MARKER (REFLECTIVE)	EA	700	2.54	1,778.00
41	566011	ROADSIDE SIGN - ONE POST	EA	24	237.00	5,688.00
42	066565	RELOCATE SIGN	EA	16	105.00	1,680.00
43	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND MILES AVE]	EA	1	103,000.00	103,000.00
44	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND PALMYRA AVE]	EA	1	110,000.00	110,000.00
45	000003	SPECIAL SIGN	EA	10	680.00	6,800.00
46	000003	SPECIAL SIGN (BUSINESS SIGN)	FA	1	10,000.00	10,000.00
47	000003	4" PVC PRIVATE WATER SYSTEM	LS	1	7,900.00	7,900.00
48	000003	CONCRETE WHEEL STOP	EA	18	52.00	936.00
49	000003	PIPE SLURRY PLUG	EA	3	950.00	2,850.00
50	860811	DETECTOR LOOP	EA	30	238.00	7,140.00
51	000003	SLURRY BACKFILL CONCRETE IRRIGATION PIPE (14")	LF	1,435	7.40	10,619.00
52	000003	ENCROACHMENT PERMIT [CWWD]	FA	1	3,000.00	3,000.00
53	000003	MISCELLANEOUS PRIVATE UTILITY WORK	FA	1	20,000.00	20,000.00
53.A	000003	MISCELLANEOUS DIRECTED WORK	FA	1	50,000.00	50,000.00

SUB-TOTAL:	Two million, seven hundred fifty eight thousand, two hundred eleven dollars and zero cents	\$ 2,758,211.00
ITEMS 1-53.A	"WORDS"	

### AGREEMENT (CONTINUED)

ITEM No.	ITEM CODE	ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
----------	-----------	------	------	--------------------	-------------------------	--------------------

**Alternate Bid Items - Indio Water Authority**

54	152351	RELOCATE HYDRANT	EA	5	2,440.00	12,200.00
55	000003	6" DIP WATER MAIN HORIZONTAL BEND ASSEMBLY	EA	5	4,640.00	23,200.00
56	152452	ADJUST WATER VALVE COVER	EA	31	450.00	13,950.00
57	000003	1" WATER SERVICE LATERAL PER IWA STD 700	EA	6	1,700.00	10,200.00
58	000003	RELOCATE BLOW-OFF ASSEMBLY	EA	1	2,530.00	2,530.00
59	000003	BACKFLOW ASSEMBLY PER IWA STD 702	EA	1	2,320.00	2,320.00

SUB-TOTAL:	Sixty four thousand four hundred dollars and zero cents	<b>\$ 64,400.00</b>
ITEMS 54-59	"WORDS"	

**Alternate Bid Items - Valley Sanitary District**

60	152440	ADJUST MANHOLE TO GRADE	EA	20	780.00	15,600.00
61	000003	8" SDR 35 PVC SEWER PIPE	LF	340	155.00	52,700.00
62	152400	ADJUST SEWER CLEANOUT TO GRADE	EA	2	850.00	1,700.00
63	000003	4" SEWER CLEANOUT	EA	2	850.00	1,700.00
64	000003	4" SEWER LATERAL WITH CONCRETE ENCASEMENT	LF	56	74.00	4,144.00
64.A	000003	ADJUST 8" PVC SEWER PIPE	LF	30	84.00	2,520.00
64.B	000003	REMOVE AND REPLACE 8" SDR 35 PVC 8" x 6" PVC WYE	EA	2	5,300.00	10,600.00

SUB-TOTAL:	Eighty eight thousand nine hundred sixty four dollars and zero cents	<b>\$ 88,964.00</b>
ITEMS 60-64.B	"WORDS"	

**Alternate Bid Items - Imperial Irrigation District**

65	000003	4" SCHEDULE 40 PVC	LF	30	33.00	990.00
66	000003	5" SCHEDULE 40 PVC	LF	290	17.00	4,930.00
67	000003	SINGLE PHASE TRANSFORMER PAD PER IID STANDARD	EA	1	1,300.00	1,300.00
68	000003	MEDIUM HANDHOLE ENCLOSURE (4' x 6.5' x 5') PER IID STANDARD	EA	1	5,800.00	5,800.00

SUB-TOTAL:	Thirteen thousand twenty dollars and zero cents	<b>\$ 13,020.00</b>
ITEMS 65-68	"WORDS"	

PROJECT TOTAL:	Two million, nine hundred twenty four thousand, five hundred nintey five dollars and zero cents	<b>\$ 2,924,595.00</b>
ITEMS 1-68	"WORDS"	



IN WITNESS WHEREOF the parties hereto have executed this agreement as of the date set forth below.

COUNTY OF RIVERSIDE

COOLEY CONSTRUCTION, INC.

BY Marion Ashley  
Chairman, Board of Supervisors

BY Paul R Cooley-Tr

MARION ASHLEY

Dated MAY 25 2010

TITLE: President  
(If Corporation, Affix Seal)

ATTEST:

Kecia Harper-Ihem, Clerk of the Board

ATTEST:

Cheryl Olson  
Cheryl Olson

BY Tom Ehlers  
Deputy

TITLE: Asst Secretary

FORM APPROVED COUNTY COUNSEL

BY: Neal R. Kipnis DATE 5/17/10

Licensed in accordance with an act providing for the registration of Contractors,

License No. 348038

Federal Employer Identification Number:

95-3134038

BY \_\_\_\_\_  
"County"  
(Seal)

\_\_\_\_\_  
"Corporation"  
(Seal)

WHEN DOCUMENT IS FULLY EXECUTED RETURN  
CLERK'S COPY

to Riverside County Clerk of the Board, Stop 1010  
Post Office Box 1147, Riverside, Ca 92502-1147

YOU.

**ACKNOWLEDGMENT**

State of California  
County of San Bernardino

On May 28, 2010 before me, Karen M Shackelford, Notary Public  
(insert name and title of the officer)

personally appeared Paul R Cooley Jr. & Cheryl Olson  
who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are  
subscribed to the within instrument and acknowledged to me that he/she/they executed the same in  
his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the  
person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing  
paragraph is true and correct.

WITNESS my hand and official seal.

Signature Karen M Shackelford (Seal)



**MINUTES OF ACTION OF BOARD OF DIRECTORS**

**OF**

**COOLEY CONSTRUCTION, INC.**

**TAKEN WITHOUT A MEETING BY UNANIMOUS WRITTEN CONSENT**

**July 16, 2007**

The actions described in these Minutes of Action were taken by the Board of Directors of the Corporation by unanimous written consent pursuant to a provision in the Corporation's Bylaws permitting such action to be taken.

The Directors hereby adopt the following recitals, resolutions, and statements:

Delegation of Authority to Officers

WHEREAS, the Bylaws of the Corporation provide that the Board of Directors of the Corporation may empower Officers or agents to execute contracts and instruments for and on behalf of the Corporation; and


WHEREAS, the Board of Directors deems it to be in the best interest of the Corporation to delegate such signing authority to the Officers of the Corporation;


NOW BE IT RESOLVED: That the following Officers of the Corporation, whether acting alone or in concert with each other, are each authorized to negotiate and enter into contracts and to execute any instruments or documents in the name of or on behalf of the Corporation, to pledge its credit, or to render it liable for any purpose or for any amount:


<u>Name</u>	<u>Office</u>
Paul R. Cooley, Jr.	President
Glen Wesley Daniels	Vice President/Chief Financial Officer
Scott C. Daniels	Vice President/Secretary
Thomas Sternfield	Vice President
Cheryl Olson	Vice President/Assistant Secretary

RESOLVED FURTHER: That the authority granted to the Officers of the Corporation named immediately above shall remain in effect until revoked by action of the Directors of the Corporation.

The undersigned, constituting all of the Directors of the Corporation, hereby adopt these Minutes of Action effective on and as of July 16, 2007.

  
Paul R. Cooley, Sr.

  
Paul R. Cooley, Jr.

  
Glen Wesley Daniels

  
Scott C. Daniels

**PERFORMANCE BOND**

**Recitals:**

1. Cooley Construction, Inc. (Contractor) has entered into an Agreement with COUNTY OF RIVERSIDE (County) for construction of public work known as Clinton Street In the City of Indio and County of Riverside Street Improvement Plans, Project No. B2-03892
2. Fidelity and Deposit Company of Maryland, a Maryland corporation (Surety), is the Surety under this Bond.

**Agreement:**

We, Contractor, as Principal, and Surety, as Surety, jointly and severally agree, state, and are bound unto County, as obligee, as follows:

1. The amount of the obligation of this Bond is 100% of the estimated contract price for the Project of \$ 2,924,595.00 (Two million, nine hundred twenty four thousand, five hundred ninety five dollars and zero cents) and inures to the benefit of County.
2. This Bond is exonerated by Contractor doing all things to be kept and performed by it in strict conformance with the Contract Documents for the Project, otherwise it remains in full force and effect for the recovery of loss, damage and expense of County resulting from failure of Contractor to so act. All of said Contract Documents are incorporated herein.
3. This obligation is binding on our successors and assigns.
4. For value received, Surety stipulates and agrees that no change, time extension, prepayment to Contractor, alteration or addition to the terms and requirements of the Contract Documents or the work to be performed thereunder shall affect its obligations hereunder and waives notice as to such matters, except the total contract price cannot be increased by more than 10% without approval of Surety.

THIS BOND is executed as of May 7, 2010  
 Cooley Construction, Inc. Fidelity and Deposit Company of Maryland

By [Signature] By [Signature]  
 By Paul R Cooley Jr Type Name Betty L. Tolentino  
 Title President Its Attorney in Fact  
"Contractor" "Surety"

(Corporate Seal)

(Corporate Seal)

**NOTE: This Bond must be executed by both parties with corporate seal affixed for each party. All signatures must be acknowledged. (Attach acknowledgements).**

*Notarial Certificate Attached*

# CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT

State of California

County of San Francisco

On May 7, 2010 before me, Virginia L. Ledford-Black, Notary Public  
Date Here Insert Name and Title of the Officer


personally appeared Betty L. Tolentino  
Name(s) of Signer(s)

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature Virginia L. Ledford-Black  
Signature of Notary Public



Place Notary Seal Above

## OPTIONAL

*Though the information below is not required by law, it may prove valuable to persons relying on the document and could prevent fraudulent removal and reattachment of this form to another document.*

### Description of Attached Document

Title or Type of Document: \_\_\_\_\_

Document Date: \_\_\_\_\_ Number of Pages: \_\_\_\_\_

Signer(s) Other Than Named Above: \_\_\_\_\_

### Capacity(ies) Claimed by Signer(s)

Signer's Name: \_\_\_\_\_

- Individual
- Corporate Officer — Title(s): \_\_\_\_\_
- Partner —  Limited  General
- Attorney in Fact
- Trustee
- Guardian or Conservator
- Other: \_\_\_\_\_

RIGHT THUMBPRINT OF SIGNER

Top of thumb here

Signer Is Representing: \_\_\_\_\_

Signer's Name: \_\_\_\_\_

- Individual
- Corporate Officer — Title(s): \_\_\_\_\_
- Partner —  Limited  General
- Attorney in Fact
- Trustee
- Guardian or Conservator
- Other: \_\_\_\_\_

RIGHT THUMBPRINT OF SIGNER

Top of thumb here

Signer Is Representing: \_\_\_\_\_

**ACKNOWLEDGMENT**

State of California  
County of San Bernardino )


On May 11, 2010 before me, Karen M Shackelford, Notary Public  
(insert name and title of the officer)

personally appeared Paul R Cooley Jr.  
who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are  
subscribed to the within instrument and acknowledged to me that he/she/they executed the same in  
his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the  
person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing  
paragraph is true and correct.

WITNESS my hand and official seal.

Signature Karen M Shackelford (Seal)



Executed in Duplicate

Bond No. 08998339  
Premium Included in  
Performance Bond

**PAYMENT BOND**

(Public Work - Civil Code 3247 et seq.)

The makers of this Bond are Cooley Construction, Inc., as Principal and Original Contractor and Fidelity and Deposit Company of Maryland, a corporation, authorized to issue Surety Bonds in California, as Surety, and this Bond is issued in conjunction with that certain public works contract to be executed between Principal and COUNTY OF RIVERSIDE a public entity, as Owner, for \$ 2,924,595.00 (Two million, nine hundred twenty four thousand, five hundred ninety five dollars and zero cents), the total amount payable. THE AMOUNT OF THIS BOND IS ONE HUNDRED PERCENT OF SAID SUM. Said contract is for public work generally consisting of, Clinton Street in the City of Indio and County of Riverside Street Improvement Plans, Project No. B2-03892

The beneficiaries of this Bond are as is stated in 3248 of the Civil Code and requirements and conditions of this Bond are as is set forth in 3248, 3249, 3250 and 3252 of said code. Without notice, Surety consents to extension of time for performance, change in requirements, amount of compensation, or prepayment under said contract.

DATED: May 7, 2010

Cooley Construction, Inc.  
Original Contractor - Principal

Fidelity and Deposit Company of Maryland  
Surety

By [Signature]  
Paul R Cooley Jr

By [Signature]  
Its Attorney In Fact  
Betty L. Tolentino

Title President  
(If corporation, affix seal)

(Corporate Seal)

(Corporate Seal)

STATE OF CALIFORNIA }  
COUNTY OF \_\_\_\_\_ } ss. SURETY'S ACKNOWLEDGEMENT

On \_\_\_\_\_ before me, \_\_\_\_\_ personally appeared, \_\_\_\_\_, known to me, or proved to me on the basis of satisfactory evidence, to be the person whose name is subscribed to the within instrument and acknowledged to me that he/she executed the same in his/her authorized capacities, and that by his/her signature on the instrument the person, or the entity upon behalf of which the person acted, executed the instrument.

WITNESS my hand and official seal.

Notarial Certificate Attached

\_\_\_\_\_  
Signature of Notary Public

Notary Public (Seal)

Note: This Bond must be executed by both parties with corporate seal affixed for each party. All signatures must be notarized. (Attach acknowledgements).



**CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT**

State of California

County of San Francisco

On May 7, 2010 before me, Virginia L. Ledford-Black, Notary Public  
Date Here Insert Name and Title of the Officer


personally appeared Betty L. Tolentino  
Name(s) of Signer(s)

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature Virginia L. Ledford-Black  
Signature of Notary Public



Place Notary Seal Above

**OPTIONAL**

*Though the information below is not required by law, it may prove valuable to persons relying on the document and could prevent fraudulent removal and reattachment of this form to another document.*

**Description of Attached Document**

Title or Type of Document: \_\_\_\_\_

Document Date: \_\_\_\_\_ Number of Pages: \_\_\_\_\_

Signer(s) Other Than Named Above: \_\_\_\_\_

**Capacity(ies) Claimed by Signer(s)**

Signer's Name: \_\_\_\_\_

- Individual
- Corporate Officer — Title(s): \_\_\_\_\_
- Partner —  Limited  General
- Attorney in Fact
- Trustee
- Guardian or Conservator
- Other: \_\_\_\_\_

RIGHT THUMBPRINT OF SIGNER  
Top of thumb here

Signer Is Representing: \_\_\_\_\_

Signer's Name: \_\_\_\_\_

- Individual
- Corporate Officer — Title(s): \_\_\_\_\_
- Partner —  Limited  General
- Attorney in Fact
- Trustee
- Guardian or Conservator
- Other: \_\_\_\_\_

RIGHT THUMBPRINT OF SIGNER  
Top of thumb here

Signer Is Representing: \_\_\_\_\_

## ACKNOWLEDGMENT

State of California  
County of San Bernardino )


On May 11, 2010 before me, Karen M Shackelford, Notary Public  
(insert name and title of the officer)

personally appeared Paul R Cooley Jr.  
who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) ~~is~~ are  
subscribed to the within instrument and acknowledged to me that ~~he~~ ~~she~~ they executed the same in  
~~his~~ ~~her~~ their authorized capacity(~~ies~~), and that by ~~his~~ ~~her~~ their signature(s) on the instrument the  
person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing  
paragraph is true and correct.

WITNESS my hand and official seal.

Signature Karen M Shackelford (Seal)



**Power of Attorney  
FIDELITY AND DEPOSIT COMPANY OF MARYLAND**

KNOW ALL MEN BY THESE PRESENTS: That the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, a corporation of the State of Maryland, by THEODORE G. MARTINEZ, Vice President, and ERIC D. BARNES, Assistant Secretary, in pursuance of authority granted by Article VI, Section 2, of the By-Laws of said Company, which are set forth on the reverse side hereof and are hereby certified to be in full force and effect on the date hereof, does hereby nominate, constitute and appoint **Susan HECKER, Janet C. ROJO, Betty L. TOLENTINO, M. MOODY, Maureen O'CONNELL, J.M. ALBADA, Brian F. COOPER, Robert P. WRIXON and Virginia L. BLACK, all of San Francisco, California, EACH** its true and lawful agent and Attorney-in-Fact, to make, execute, seal and deliver for, and on its behalf as surety, and as its act and deed: **any and all bonds and undertakings**, and the execution of such bonds or undertakings in pursuance of these presents, shall be as binding upon said Company, as fully and amply, to all intents and purposes, as if they had been duly executed and acknowledged by the regularly elected officers of the Company at its office in Baltimore, Md., in their own proper persons. This power of attorney revokes that issued on behalf of Susan HECKER, Janet C. ROJO, Betty L. TOLENTINO, M. MOODY, Maureen O'CONNELL, J.M. ALBADA, Brian F. COOPER, Robert P. WRIXON, dated July 14, 2008.

The said Assistant Secretary does hereby certify that the extract set forth on the reverse side hereof is a true copy of Article VI, Section 2, of the By-Laws of said Company, and is now in force.

IN WITNESS WHEREOF, the said Vice-President and Assistant Secretary have hereunto subscribed their names and affixed the Corporate Seal of the said FIDELITY AND DEPOSIT COMPANY OF MARYLAND, this 15th day of October, A.D. 2008.

ATTEST:

**FIDELITY AND DEPOSIT COMPANY OF MARYLAND**



*Eric D. Barnes*

*Theodore G. Martinez*

By:

Eric D. Barnes

Assistant Secretary

Theodore G. Martinez

State of Maryland }  
Baltimore County } ss:

On this 15th day of October, A.D. 2008, before the subscriber, a Notary Public of the State of Maryland, duly commissioned and qualified, came THEODORE G. MARTINEZ, Vice President, and ERIC D. BARNES, Assistant Secretary of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, to me personally known to be the individuals and officers described in and who executed the preceding instrument, and they each acknowledged the execution of the same, and being by me duly sworn, severally and each for himself depose and saith, that they are the said officers of the Company aforesaid, and that the seal affixed to the preceding instrument is the Corporate Seal of said Company, and that the said Corporate Seal and their signatures as such officers were duly affixed and subscribed to the said instrument by the authority and direction of the said Corporation.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed my Official Seal the day and year first above written.



*Dennis R. Hayden*

Dennis R. Hayden

Notary Public

My Commission Expires: February 15, 2013

## Company Profile

### FIDELITY AND DEPOSIT COMPANY OF MARYLAND

1400 AMERICAN LANE, 19TH FLOOR TOWER 1  
SCHUAMBURG, IL 60196-1056  
800-382-2150

#### Agent for Service of Process

KAREN HARRIS, 2730 GATEWAY OAKS DRIVE SUITE 100 SACRAMENTO, CA 95833

Unable to Locate the Agent for Service of Process?

#### Reference Information

NAIC #:	39306
NAIC Group #:	<u>0212</u>
California Company ID #:	2479-4
Date authorized in California:	January 01, 1982
License Status:	UNLIMITED-NORMAL
Company Type:	Property & Casualty
State of Domicile:	MARYLAND

#### Lines of Insurance Authorized to Transact

The company is authorized to transact business within these lines of insurance. For an explanation of any of these terms, please refer to the glossary.

AIRCRAFT  
AUTOMOBILE  
BOILER AND MACHINERY  
BURGLARY  
CREDIT  
FIRE  
LIABILITY  
MARINE  
MISCELLANEOUS  
PLATE GLASS  
SPRINKLER  
SURETY  
TEAM AND VEHICLE  
WORKERS' COMPENSATION

#### Company Complaint Information

[Company Enforcement Action Documents](#)

[Company Performance & Comparison Data](#)

[Composite Complaint Studies](#)

#### Want More?

[Help Me Find a Company Representative in My Area](#)

[Financial Rating Organizations](#)

Last Revised - June 26, 2009 05:53 PM  
Copyright © California Department of Insurance



# CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)  
05/19/10

PRODUCER LIC #0726293 1-415-391-1500  
Gallagher Construction Services/  
Arthur J. Gallagher & Co. Insurance Brokers of CA Inc.  
1 Market St., Spear Tower #200  
San Francisco, CA 94105

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW.

INSURED  
Cooley Construction, Inc.  
17525 Eucalyptus Street, Suite G  
Hesperia, CA 92345

INSURERS AFFORDING COVERAGE	NAIC #
INSURER A: ARCH INS CO	11150
INSURER B: EVEREST NATL INS CO	10120
INSURER C: SEABRIGHT INS CO	15563
INSURER D:	
INSURER E:	

### COVERAGES

THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. AGGREGATE LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR ADD'L LTR INSRD	TYPE OF INSURANCE	POLICY NUMBER	POLICY EFFECTIVE DATE (MM/DD/YYYY)	POLICY EXPIRATION DATE (MM/DD/YYYY)	LIMITS
A X	GENERAL LIABILITY <input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS MADE <input checked="" type="checkbox"/> OCCUR <input checked="" type="checkbox"/> Primary <input checked="" type="checkbox"/> Contractual Liability GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input checked="" type="checkbox"/> LOC	71PKG2257005	08/01/09	08/01/10	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 100,000 MED EXP (Any one person) \$ 5,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMP/OP AGG \$ 2,000,000
A X	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input checked="" type="checkbox"/> HIRED AUTOS <input checked="" type="checkbox"/> NON-OWNED AUTOS <input checked="" type="checkbox"/> Comp Ded: \$1000 <input checked="" type="checkbox"/> Coll Ded: \$1000	71PKG2257005	08/01/09	08/01/10	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ AUTO ONLY - EA ACCIDENT \$ OTHER THAN EA ACC AGG \$
	GARAGE LIABILITY <input type="checkbox"/> ANY AUTO				
B	EXCESS / UMBRELLA LIABILITY <input checked="" type="checkbox"/> OCCUR <input type="checkbox"/> CLAIMS MADE <input type="checkbox"/> DEDUCTIBLE <input type="checkbox"/> RETENTION \$	71C7000010-091	08/01/09	08/01/10	EACH OCCURRENCE \$ 8,000,000 AGGREGATE \$ 8,000,000 \$ \$ \$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? <input type="checkbox"/> Y/N (Mandatory in NH) If yes, describe under SPECIAL PROVISIONS below	BB1090712	08/01/09	08/01/10	<input checked="" type="checkbox"/> WC STATUTORY LIMITS <input type="checkbox"/> OTH-ER E.L. EACH ACCIDENT \$ 1,000,000 E.L. DISEASE - EA EMPLOYEE \$ 1,000,000 E.L. DISEASE - POLICY LIMIT \$ 1,000,000
	OTHER				

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES / EXCLUSIONS ADDED BY ENDORSEMENT / SPECIAL PROVISIONS  
Project #B2-03892  
RE: Clinton Street Improvements  
ADDITIONAL INSURED(S): County of Riverside; The City of Indio, its officers, directors, agents and employees; Indio Water Authority, its officers, directors, agents and employees; Valley Sanitary District, its officers, directors, agents and employees; Imperial Irrigation District, its officers, directors, agents and employees; Coachella Valley Water District, its officers, directors, agents and employees and Redevelopment Agency County of Riverside, its officers, directors, agents and employees. Umbrella policy is "follow form"

CERTIFICATE HOLDER  
Project #B2-03892  
County of Riverside  
Transportation Department  
Attn: Joel Jimenez  
14th Street Transportation Annex  
3525 14th Street  
Riverside, CA 92501  
USA

CANCELLATION 10 day notice for nonpayment of premium  
SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, THE ISSUING INSURER WILL SEND BY MAIL 30 DAYS WRITTEN NOTICE TO THE CERTIFICATE HOLDER NAMED TO THE LEFT, BUT NOT LATER THAN 30 DAYS BEFORE THE EXPIRATION DATE OF THE POLICY.  
AUTHORIZED REPRESENTATIVE

## IMPORTANT

If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

## DISCLAIMER

This Certificate of Insurance does not constitute a contract between the issuing insurer(s), authorized representative or producer, and the certificate holder, nor does it affirmatively or negatively amend, extend or alter the coverage afforded by the policies listed thereon.

**THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.**

**ADDITIONAL INSURED ENDORSEMENT**

This endorsement modifies insurance provided under the following.

**BUSINESS AUTO COVERAGE FORM**

With respect to coverage provided by this endorsement, the provisions of the Coverage Form apply unless modified by the endorsement.

This endorsement is effective on the inception date of the policy unless another date is indicated below.

SECTION II -LIABILITY COVERAGE, 1. WHO IS AN INSURED is amended to include as an "insured" the person(s) or organization(s) named in the Schedule below, but only with respect to their legal liability for acts or omissions of a person for whom Liability Coverage is afforded under this policy. You are authorized to act for the additional insured named in the Schedule in all matters pertaining to this insurance.

**SCHEDULE**

**Name and Address of Additional Insured:**

ANY PERSON OR ORGANISATION THAT YOU HAVE AGREED IN A WRITTEN CONTRACT, THAT SUCH PERSON OR ORGANIZATION IS AN ADDITIONAL INSURED ON THIS POLICY.

All other terms and conditions of this Policy remain unchanged.

Endorsement Number: **00 CA007000 0906**

AUTHORIZED REPRESENTATIVE 

Policy Number: **71PKG2257005**

Named Insured: **COOLEY CONSTRUCTION, INC.**

Endorsement Effective Date: **08-01-09** local Standard Time at the First Named Insured's address.

**THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.**

**ADDITIONAL INSURED - AUTOMATIC STATUS WHEN REQUIRED BY A  
CONSTRUCTION AGREEMENT WITH YOU - COMPLETED OPERATIONS -  
PRIMARY AND NON-CONTRIBUTORY ENDORSEMENT**

This endorsement modifies insurance provided under the following:

Section II - Who is an "Insured" is amended to include as an insured any person or organization for whom you are performing operations when you are specifically required by a written construction contract or agreement with such person or organization to include them as an additional insured on your policy- and provide coverage for such additional insured only for liability arising out of:

- i) "your work" at the location designated; or
- ii) The "products completed operations hazard."

Coverage afforded to these additional insured parties will be primary to, and non-contributory with, any other insurance available to that person or organization.

All other terms and conditions of this Policy remain unchanged.

AUTHORIZED REPRESENTATIVE



Policy Number: **71PKG2257005**

Named Insured: COOLEY CONSTRUCTION, INC.

This endorsement is effective on the inception date of this Policy unless otherwise stated herein:

Endorsement Effective Date: **08-01-09**



**WAIVER OF OUR RIGHT TO RECOVER FROM OTHERS ENDORSEMENT- CALIFORNIA**

We have the right to recover our payments from anyone liable for an injury covered by this policy. We will not enforce our right against the person or organization named in the Schedule. (This agreement applies only to the extent that you perform work under a written contract that requires you to obtain this agreement from us.)

You must maintain payroll records accurately segregating the remuneration of your employees while engaged in the work described in the Schedule.

The additional premium for this endorsement shall be \* % of the California workers' compensation premium otherwise due on such remuneration.

Schedule

**Person or Organization**

WHERE YOU ARE REQUIRED BY WRITTEN CONTRACT TO OBTAIN THIS AGREEMENT FROM US, PROVIDED THE CONTRACT IS SIGNED & DATED PRIOR TO THE DATE OF LOSS TO WHICH THIS WAIVER APPLIES. IN NO INSTANCE SHALL THE PROVISIONS AFFORDED BY THIS ENDORSEMENT BENEFIT ANY COMPANY OPERATING AIRCRAFT FOR HIRE.

**Job Description**

WHERE REQUIRED BY WRITTEN CONTRACT.  
.  
.  
.  
.  
.

\*The policy premium charge for this endorsement shall be 2% of the premium developed in the State of California, but not less than \$500 policy minimum premium

.  
. .  
. .  
. .

This endorsement changes the policy to which it is attached and is effective on the date unless otherwise stated.

**(The information below is required only when this endorsement is issued subsequent to preparation of the policy.)**

Endorsement Effective: 08/01/09

Policy No. BB1090712

Endorsement No. .

Insured:  
Cooley Construction, Inc.

Insurance Company:  
SEABRIGHT INS CO

Countersigned By: 



Gallagher Construction Services

Arthur J. Gallagher & Co. Insurance Brokers of California, Inc.

May 19, 2010

Re: Cooley Construction, Inc.  
Coverage: Umbrella (9/91)  
Policy Number: 71C7000010091

To Whom It May Concern:

Please let it be known that the above Insured's Umbrella policy is "follow form" and that there is no "Additional Insured" endorsements to send do to this fact. Should you have any questions or concerns, please feel free to contact us.

Sincerely,

Aaron Cosgrove  
Account Assistant  
Gallagher Construction Services  
Arthur J. Gallagher Insurance Brokers of CA, Inc.  
One Market Plaza  
Spear Street Tower, Suite 200  
San Francisco, CA 94105  
aaron\_cosgrove@ajg.com

One Market Plaza  
Spear Tower, Suite 200  
San Francisco, CA 94105  
Main 415.391.1500  
Fax 415.391.1882  
Toll Free 800.500.7202  
License #0726293  
AJG.com

# SUPPLEMENT TO CERTIFICATE OF INSURANCE

DATE  
05/19/10

NAME OF INSURED: Cooley Construction, Inc.

Additional Description of Operations/Remarks from Page 1:

Additional Information:

GENERAL LIABILITY:

- \*Additional Insured when required by written contract per Form 00ML001900 0806 (construction)
- \*Primary Non Contribution when required by written contract per Form 00ML001900 0806
- \*Waiver of Subrogation when required by written contract per Form CG2404 1093
- \*Severability of Interest/Separation of Insured per policy forms

AUTOMOBILE:

- \*Additional Insured when required by written contract per Form 00CA007000 0906
- \*Waiver of Subrogation when required by written contract per Form 00CA003200 1003

WORKERS' COMPENSATION:

- \*Waiver of Subrogation when required by written contract per Form WC040306 484 (CA)

UMBRELLA:

Excess coverage follows primary policies, subject to policy terms, conditions and exclusions.

## Company Profile

## ARCH INSURANCE COMPANY

300 PLAZA 3  
 JERSEY CITY, NJ 07311  
 800-821-5546

## Former Names for Company

Old Name: FIRST AMERICAN INSURANCE COMPANY DBA AMERICAN FIRST INSURANCE COMPANY  
 Old Name: FIRST AMERICAN INSURANCE COMPANY

Effective Date: 11-06-2002

Effective Date: 01-05-1987

## Agent for Service of Process

JERE KEPRIOS, C/O CT CORPORATION SYSTEM 818 WEST SEVENTH STREET, 2ND FLOOR LOS ANGELES, CA 90017 JERE KEPRIOS, C/O CT CORPORATION SYSTEM 818 WEST SEVENTH ST LOS ANGELES, CA 90017

Unable to Locate the Agent for Service of Process?

## Reference Information

NAIC #:	11150
NAIC Group #:	1279
California Company ID #:	3005-6
Date authorized in California:	July 19, 1985
License Status:	UNLIMITED-NORMAL
Company Type:	Property & Casualty
State of Domicile:	MISSOURI

## Lines of Insurance Authorized to Transact

The company is authorized to transact business within these lines of insurance. For an explanation of any of these terms, please refer to the [glossary](#).

AIRCRAFT  
 AUTOMOBILE  
 BOILER AND MACHINERY  
 BURGLARY  
 COMMON CARRIER LIABILITY  
 DISABILITY  
 FIRE  
 LIABILITY  
 MARINE  
 SURETY  
 TEAM AND VEHICLE  
 WORKERS' COMPENSATION

## Company Complaint Information

[Company Enforcement Action Documents](#)

[Company Performance & Comparison Data](#)

[Composite Complaint Studies](#)

## Want More?

[Help Me Find a Company Representative in My Area](#)

[Financial Rating Organizations](#)

Last Revised - June 26, 2009 05:53 PM  
 Copyright © California Department of Insurance

## Company Profile

**EVEREST NATIONAL INSURANCE COMPANY**  
 477 MARTINSVILLE ROAD  
 LIBERTY CORNER, NJ 07938-0830  
 800-438-4375

**Former Names for Company**

**Old Name:** PRUDENTIAL NATIONAL INSURANCE COMPANY  
**Old Name:** DRYDEN GUARANTY INSURANCE COMPANY

**Effective Date:** 06-17-1996

**Effective Date:** 10-20-1993

**Agent for Service of Process**

NANCY CARAVACA, 1111 BROADWAY SUITE 2050 OAKLAND, CA 94607  
Unable to Locate the Agent for Service of Process?

**Reference Information**

NAIC #:	10120
NAIC Group #:	<u>1120</u>
California Company ID #:	3138-5
Date authorized in California:	March 02, 1988
License Status:	UNLIMITED-NORMAL
Company Type:	Property & Casualty
State of Domicile:	DELAWARE

**Lines of Insurance Authorized to Transact**

The company is authorized to transact business within these lines of insurance. For an explanation of any of these terms, please refer to the glossary.

AIRCRAFT  
 AUTOMOBILE  
 BOILER AND MACHINERY  
 BURGLARY  
 COMMON CARRIER LIABILITY  
 FIRE  
 LIABILITY  
 MARINE  
 PLATE GLASS  
 SPRINKLER  
 SURETY  
 TEAM AND VEHICLE  
 WORKERS' COMPENSATION

**Company Complaint Information**

[Company Enforcement Action Documents](#)  
[Company Performance & Comparison Data](#)  
[Composite Complaint Studies](#)

**Want More?**

[Help Me Find a Company Representative in My Area](#)

[Financial Rating Organizations](#)

Last Revised - June 26, 2009 05:53 PM  
 Copyright © California Department of Insurance

## Company Profile

### SEABRIGHT INSURANCE COMPANY

1501 4TH AVENUE, SUITE 2600  
SEATTLE, WA 98101

#### Former Names for Company

Old Name: KEMPER EMPLOYERS INSURANCE COMPANY

Effective Date: 03-16-2004

#### Agent for Service of Process

KAREN HARRIS, 2730 GATEWAY OAKS DRIVE SUITE 100 SACRAMENTO, CA 95833

Unable to Locate the Agent for Service of Process?

---

### Reference Information

NAIC #:	15563
NAIC Group #:	<u>0000</u>
California Company ID #:	4648-2
Date authorized in California:	August 15, 2000
License Status:	UNLIMITED-NORMAL
Company Type:	Property & Casualty
State of Domicile:	ILLINOIS

---

### Lines of Insurance Authorized to Transact

The company is authorized to transact business within these lines of insurance. For an explanation of any of these terms, please refer to the glossary.

AUTOMOBILE  
LIABILITY  
MARINE  
WORKERS' COMPENSATION

---

### Company Complaint Information

Company Enforcement Action Documents  
Company Performance & Comparison Data  
Composite Complaint Studies

---

### Want More?

Help Me Find a Company Representative in My Area

Financial Rating Organizations

---

Last Revised - June 26, 2009 05:53 PM  
Copyright © California Department of Insurance

# Attachment "A"

Riverside County Transportation Department

Project: **Clinton Street Reconstruction and Widening Project (Phase 2B)**

Project No.(s): **B2-03892**

### Project Costs and Budget

Activity	Incurred Costs	Projected Costs	Total Costs	Existing Budget	Proposed Budget
Preliminary Survey					
Environmental					
Design					
Right-of-way					
Utilities					
Construction		2,924,595	2,924,595	4,000,000	3,217,000
Construction Contingency <span style="float: right;">10.0%</span>		292,460	292,460		
Construction Engineering & Inspection	4,517	350,000	354,517	560,000	355,000
Construction Survey	5,193	140,000	145,193	200,000	145,000
<b>Totals:</b>	<b>9,710</b>	<b>3,707,055</b>	<b>3,716,764</b>	<b>4,760,000</b>	<b>3,717,000</b>

### Project Funding

Code	Name	Existing Budget	Proposed Budget
340	Transportation Uniform Mitigation Fee (CVAG)	3,299,000	3,534,000
990	Miscellaneous (Valley Sanitation District)		98,000
990	Miscellaneous (Imperial Irrigation District)		14,000
214	Proposition 42		71,000
999	Unfunded	1,461,000	
<b>Totals</b>		<b>4,760,000</b>	<b>3,717,000</b>


### Comments

# CLINTON STREET IN THE CITY OF INDIO AND COUNTY OF RIVERSIDE

---

## STREET IMPROVEMENT PLANS

A PORTION OF THE NORTHWEST QUARTER OF  
SECTION 22, T.5S., R.7E., SAN BERNARDINO BASE AND MERIDIAN  
LENGTH OF PROJECT (0.53 MI)

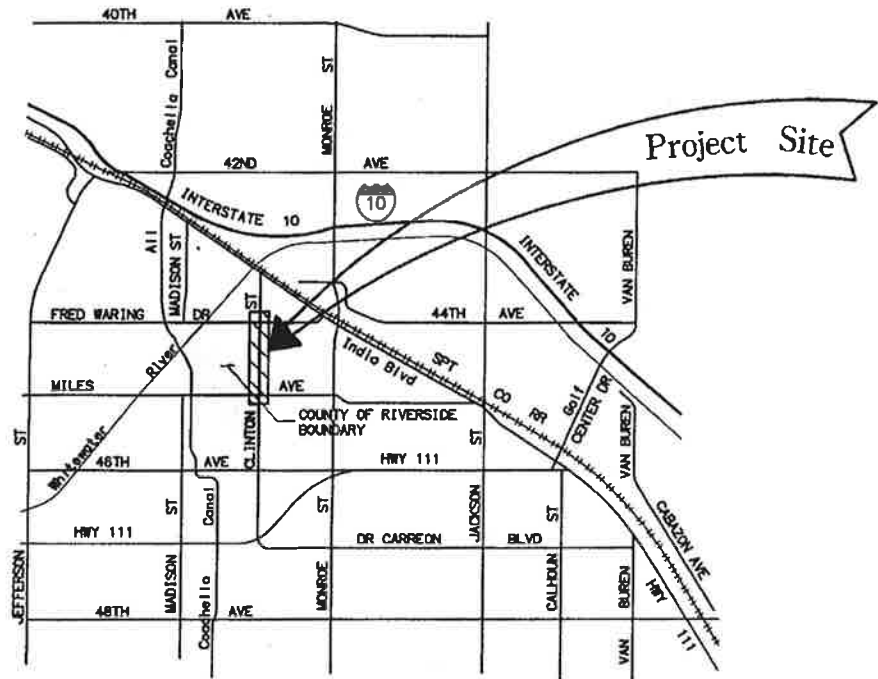

VICINITY MAP



# Attachment "A"

Riverside County Transportation Department

Project: **Miles Avenue Bridge over the Whitewater River (Phase 1), Miles Avenue Reconstruction and Widening (Phase 2A), Clinton Street Reconstruction and Widening (Phase 2B)**

Project No.(s): **B2-0389**

### Project Costs and Budget

Activity	Incurred Costs	Projected Costs	Total Costs	Existing Budget	Proposed Budget
Preliminary Survey	33,679		33,679	34,000	34,000
Environmental	492,657		492,657	464,000	493,000
Design	1,834,206	25,000	1,859,206	2,066,000	1,859,000
Right-of-way	1,028,339		1,028,339	1,142,000	1,028,000
Utilities	159,281		159,281	32,000	159,000
Construction	11,988,369	3,519,499	15,507,868	16,922,000	15,800,000
Construction Contingency 10.0%		292,460	292,460		
Construction Engineering & Inspection	2,007,440	388,500	2,395,940	2,406,000	2,396,000
Construction Survey	710,617	140,000	850,617	940,000	851,000
<b>Totals:</b>	<b>18,254,588</b>	<b>4,365,459</b>	<b>22,620,047</b>	<b>24,006,000</b>	<b>22,620,000</b>

### Project Funding

Code	Name	Existing Budget	Proposed Budget
340	Transportation Uniform Mitigation Fee (CVAG)	22,000,000	21,954,000
711	City of Indio Water Authority	545,000	481,000
990	Miscellaneous (Valley Sanatation District)		100,000
990	Miscellaneous (Imperial Irrigation District)		14,000
214	Proposition 42		71,000
999	Unfunded	1,461,000	
<b>Totals</b>		<b>24,006,000</b>	<b>22,620,000</b>

### Comments

In order to reduce construction cost and accelerate construction, the project will be constructed in 3 phases. Phase 1 will construct the Miles Avenue Bridge across the Whitewater River. Phase 2A is the construction of the roadway and storm drain improvements along Miles Avenue. Phase 2B is the construction of the roadway and storm drain improvements along Clinton Street.

The costs shown for Preliminary Survey, Environmental, Design, Right-of-Way and Utilities are for the Phase 1, Phase 2A and Phase 2B work. The costs shown for Construction (including contingency), Construction Engineering & Inspection and Construction Survey are for Phase 1 and Phase 2A work only. Projected Costs for construction includes the construction estimated cost for Phase 2B (\$3,217,000) and the balance to pay for the improvements of Phase 1 and Phase 2A.

CVAG will reimburse 75% of total cost and the County and the City of Indio will equally share the remaining 25%. CVAG will upfront 100% of the total cost and the City and County have executed an agreement to reimburse CVAG for their share over a 10 year period.

# Attachment "A"

Riverside County Transportation Department

Project: **Miles Avenue Bridge over the Whitewater River (Phase 1)**

Project No.(s): **B2-0389**

## Project Costs and Budget

Activity	Incurred Costs	Projected Costs	Total Costs	Existing Budget	Proposed Budget
Preliminary Survey	33,679		33,679	34,000	34,000
Environmental	492,657		492,657	464,000	493,000
Design	1,834,206	25,000	1,859,206	2,066,000	1,859,000
Right-of-way	1,028,339		1,028,339	1,142,000	1,028,000
Utilities	159,281		159,281	32,000	159,000
Construction	9,632,252	383,748	10,016,000	10,528,000	10,016,000
Construction Contingency 10.0%					
Construction Engineering & Inspection	1,691,503	28,500	1,720,003	1,646,000	1,720,000
Construction Survey	578,965		578,965	627,000	579,000
<b>Totals:</b>	<b>15,450,882</b>	<b>437,248</b>	<b>15,888,130</b>	<b>16,539,000</b>	<b>15,888,000</b>

## Project Funding

Code	Name	Existing Budget	Proposed Budget
340	Transportation Uniform Mitigation Fee (CVAG)	16,153,000	15,570,000
711	City of Indio Water Authority	386,000	318,000
<b>Totals</b>		<b>16,539,000</b>	<b>15,888,000</b>

## Comments

In order to reduce construction cost and accelerate construction, the project will be constructed in 3 phases. Phase 1 will construct the Miles Avenue Bridge across the Whitewater River. Phase 2A is the construction of the roadway and storm drain improvements along Miles Avenue. Phase 2B is the construction of the roadway and storm drain improvements along Clinton Street.

The costs shown for Preliminary Survey, Environmental, Design and utilities are for the Phase 1, Phase 2A and Phase 2B work. The costs shown for Construction (including contingency), Construction Engineering & Inspection and Construction Survey are for Phase 1 work only. A revised Attachment A will be completed for the Phase 2A and Phase 2B work once the project is ready to be advertised for construction.

CVAG will reimburse 75% of total cost and the County and the City of Indio will equally share the remaining 25%. CVAG will upfront 100% of the total cost and the City and County have executed an agreement to reimburse CVAG for their share over a 10 year period.

# Attachment "A"

Riverside County Transportation Department

Project: **Miles Avenue Reconstruction and Widening Project (Phase 2A)**

Project No.(s): **B2-03891**

### Project Costs and Budget

Activity	Incurred Costs	Projected Costs	Total Costs	Existing Budget	Proposed Budget
Preliminary Survey					
Environmental					
Design					
Right-of-way					
Utilities					
Construction	2,356,117	211,156	2,567,273	2,394,000	2,587,000
Construction Contingency 10.0%					
Construction Engineering & Inspection	311,420	10,000	321,420	200,000	321,000
Construction Survey	126,459		126,459	113,000	126,000
<b>Totals:</b>	<b>2,793,996</b>	<b>221,156</b>	<b>3,015,152</b>	<b>2,707,000</b>	<b>3,014,000</b>

### Project Funding

Code	Name	Existing Budget	Proposed Budget
340	Transportation Uniform Mitigation Fee (CVAG)	2,548,000	2,849,000
711	City of Indio Water Authority	159,000	163,000
990	Miscellaneous (Indio Water Authority)		
990	Miscellaneous (Valley Sanatery)		2,000
<b>Totals</b>		<b>2,707,000</b>	<b>3,014,000</b>

### Comments

## Form 11 Attachment

### Contract/Lease/Purchase Summary Data

**Contract (for Services)**

- Approval/Renewal
- Sole Source
- Personal Services
- Independent Contractor
- Other than Low Bid
- Change Order
- Public Works

**Lease**

- Approval/Renewal
- Multi-Year Lease
- Equipment
- Real Property
- Change Order

**Purchase (for Materials)**

- Sole Source
- Other than Low Bid
- Change Order

**Selection Committee Member Names (RFP's Only)**

<b>User Department:</b>	Transportation Department
-------------------------	---------------------------

N/A

<b>Vendor/Lessor Name:</b>	Cooley Construction, Inc.
----------------------------	---------------------------

**Minority Status:**

M    W    DV    None

<b>Vendor/Lessor Location:</b>	Hesperia, CA
--------------------------------	--------------

**Local Preference Applied:**  Yes    No    N/A

**Local Preference Award Cost \$**  
(5% maximum preference)

**Local Preference FYTD:** Cost \$ \_\_\_\_\_ # of Orders \_\_\_\_\_

**Applicable Board Policy #**

**Comments:**

**RFQ/RFP Process:**

Date Mailed:  
Response Date:  
# of Responses:  
# of Qualified Responses:

**Bidding Process:**

Bid Range: \$ 2,924,595.00 to \$ 3,468,468.00  
Local Bid Range: N/A  
Responsive and Responsible Bid Range: \$ 2,924,595.00 to \$ 3,468,468.00

**Contract/Lease Renewals Only**

Existing Agreement Items

Proposed Agreement Items

1. Rates
2. Terms
3. Conditions
4. Legal Issues
5. Accountability
6. Utilities

(continue on blank sheet if necessary)

**NOTE: COMPETITIVELY BID PUBLIC WORKS CONTRACT**

**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

BASE BID ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	COUNTY'S ESTIMATE			Cooley Construction, Inc. Hesperia, CA 92340-1810	
					UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE	
1	999990	MOBILIZATION	LS	1	95,600.00	95,600.00	90,000.00	90,000.00	
2	160101	CLEARING AND GRUBBING	LS	1	175,000.00	175,000.00	147,000.00	147,000.00	
3	066102	DUST ABATEMENT	LS	1	8,500.00	8,500.00	7,300.00	7,300.00	
4	170101	DEVELOP WATER SUPPLY	LS	1	10,000.00	10,000.00	3,200.00	3,200.00	
5	066105	RESIDENT ENGINEERS OFFICE	LS	1	15,000.00	15,000.00	8,400.00	8,400.00	
6	074020	WATER POLLUTION CONTROL	LS	1	10,000.00	10,000.00	10,600.00	10,600.00	
7	190101	ROADWAY EXCAVATION	CY	10,300	28.00	288,400.00	15.50	159,650.00	
8	220101	FINISHING ROADWAY	LS	1	35,000.00	35,000.00	13,700.00	13,700.00	
9	120100	TRAFFIC CONTROL SYSTEMS	LS	1	50,000.00	50,000.00	41,000.00	41,000.00	
10	153103	COLD PLANE ASPHALT CONCRETE PAVEMENT [0.15' MAXIMUM]	SQYD	1,320	3.50	4,620.00	4.20	5,544.00	
11	390130	HOT MIX ASPHALT	TON	3,680	95.00	349,600.00	74.00	272,320.00	
12	013901	ASPHALT RUBBER HOT MIX	TON	2,080	105.00	218,400.00	92.00	191,360.00	
13	260201	CLASS 2 AGGREGATE BASE	CY	5,960	35.00	208,600.00	27.70	165,092.00	
14	731516	MINOR CONCRETE (DRIVEWAY)	SQFT	7,940	4.50	35,730.00	4.30	34,142.00	
15	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	3,760	15.50	58,280.00	17.40	65,424.00	
16	017310	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207)	EA	17	970.00	16,490.00	1,280.00	21,760.00	
17	017312	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207A)	EA	5	5,000.00	25,000.00	4,350.00	21,750.00	
18	017317	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	6,500	10.00	65,000.00	8.90	57,850.00	
19	731521	MINOR CONCRETE (SIDEWALK)	SQFT	22,700	4.00	90,800.00	4.40	99,880.00	
20	017309	MINOR CONCRETE (TYPE "D" CURB) (CRS 204)	LF	15	30.00	450.00	43.00	645.00	
21	000003	MINOR CONCRETE (TYPE "D-1" CURB) (CRS 203)	LF	20	30.00	600.00	35.00	700.00	
22	510503	MINOR CONCRETE (STRUCTURE) [CONCRETE BULKHEAD-RCFC&WCD M816] [66" BULKHEAD]	EA	1	2,000.00	2,000.00	1,700.00	1,700.00	
23	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	4	1,800.00	7,200.00	3,140.00	12,560.00	
24	017316	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	15	1,800.00	27,000.00	2,400.00	36,000.00	
25	000003	INSTALL 24" BOX TREE [ACACIA ANEURA MULGA / PINUS ELDARICA TREES]	EA	8	450.00	3,600.00	424.00	3,392.00	
26	000003	REMOVE AND REINSTALL STREET LIGHT PER COI STD 202	EA	7	3,100.00	21,700.00	1,200.00	8,400.00	
27	000003	ADJUST STORM DRAIN MANHOLE TO GRADE	EA	2	1,000.00	2,000.00	1,080.00	2,160.00	
28	518201	MASONRY BLOCK WALL	SQFT	650	175.00	113,750.00	48.40	31,460.00	
29	833088	TUBULAR HANDRAILING	LF	184	35.00	6,440.00	60.00	11,040.00	
30	650014	18" REINFORCED CONCRETE PIPE	LF	655	80.00	52,400.00	63.00	41,265.00	
31	000003	24" REINFORCED CONCRETE PIPE	LF	340	95.00	32,300.00	70.00	23,800.00	
32	000003	66" REINFORCED CONCRETE PIPE	LF	2,812	450.00	1,265,400.00	198.00	556,776.00	
33	000003	REINFORCED CONCRETE 4'X6' TRANSITION STRUCTURE	EA	1	15,000.00	15,000.00	11,600.00	11,600.00	
34	017003	CATCH BASIN (CURB INLET) (CRS 300)	EA	23	7,500.00	172,500.00	6,600.00	151,800.00	

**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

BASE BID (CONTINUED)		COUNTY'S ESTIMATE				Cooley Construction Hesperia, CA 92340-1810		
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
35	017101	MANHOLE (RCFC&WCDS MH 251)	EA	6	4,500.00	27,000.00	5,300.00	31,800.00
36	017103	MANHOLE (RCFC&WCDS MH 252)	EA	7	8,500.00	59,500.00	6,500.00	45,500.00
37	000003	JUNCTION STRUCTURE (RCFC&WCDS JS 227)	EA	11	1,800.00	19,800.00	1,770.00	19,470.00
38	840656	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,000	0.55	7,700.00	0.35	4,900.00
39	840515	THERMOPLASTIC PAVEMENT MARKING	SQFT	1,400	6.00	8,400.00	4.20	5,880.00
40	850102	PAVEMENT MARKER (REFLECTIVE)	EA	700	3.00	2,100.00	2.54	1,778.00
41	566011	ROADSIDE SIGN - ONE POST	EA	24	275.00	6,600.00	237.00	5,688.00
42	066585	RELOCATE SIGN	EA	16	150.00	2,400.00	105.00	1,680.00
43	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND MILES AVE]	EA	1	105,000.00	105,000.00	103,000.00	103,000.00
44	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND PALMYRA	EA	1	105,000.00	105,000.00	110,000.00	110,000.00
45	000003	SPECIAL SIGN	EA	10	500.00	5,000.00	680.00	6,800.00
46	000003	SPECIAL SIGN (BUSINESS SIGN)	FA	1	10,000.00	10,000.00	10,000.00	10,000.00
47	000003	4" PVC PRIVATE WATER SYSTEM	LS	1	12,000.00	12,000.00	7,900.00	7,900.00
48	000003	CONCRETE WHEEL STOP	EA	18	750.00	13,500.00	52.00	936.00
49	000003	PIPE SLURRY PLUG	EA	3	1,200.00	3,600.00	950.00	2,850.00
50	860811	DETECTOR LOOP	EA	30	350.00	10,500.00	238.00	7,140.00
51	000003	SLURRY BACKFILL CONCRETE IRRIGATION PIPE (14")	LF	1,435	20.00	28,700.00	7.40	10,619.00
52	000003	ENCROACHMENT PERMIT [CVWD]	FA	1	3,000.00	3,000.00	3,000.00	3,000.00
53	000003	MISCELLANEOUS PRIVATE UTILITY WORK	FA	1	20,000.00	20,000.00	20,000.00	20,000.00
53.A	000003	MISCELLANEOUS DIRECTED WORK	FA	1	50,000.00	50,000.00	50,000.00	50,000.00
<b>SUBTOTAL</b>						<b>3,982,160.00</b>		<b>2,758,211.00</b>
ITEMS 1-53.A								

ALTERNATE BID ITEMS - INDIO WATER AUTHORITY		COUNTY'S ESTIMATE				Cooley Construction Hesperia, CA 92340-1810		
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	ENG ESTIMATE	BID UNIT PRICE	BID ESTIMATE
54	152351	RELOCATE HYDRANT	EA	5	7,000.00	35,000.00	2,440.00	12,200.00
55	000003	6" DIP WATER MAIN HORIZONTAL BEND ASSEMBLY	EA	5	4,000.00	20,000.00	4,640.00	23,200.00
56	152452	ADJUST WATER VALVE COVER	EA	31	750.00	23,250.00	450.00	13,950.00
57	000003	1" WATER SERVICE LATERAL PER IWA STD 700	EA	6	2,500.00	15,000.00	1,700.00	10,200.00
58	000003	RELOCATE BLOW-OFF ASSEMBLY	EA	1	2,000.00	2,000.00	2,530.00	2,530.00
59	000003	BACKFLOW ASSEMBLY PER IWA STD 702	EA	1	2,000.00	2,000.00	2,320.00	2,320.00
<b>SUBTOTAL</b>						<b>97,250.00</b>		<b>64,400.00</b>
ITEMS 54-59								







**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

BASE BID (CONTINUED)		Dateiland Construction Co. Inc. Indio, CA 92201		Hardy & Harper, Inc. Santa Ana, CA 92705				
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
35	017101	MANHOLE (RCFC&WCDS MH 251)	EA	6	4,515.00	27,090.00	4,000.00	24,000.00
36	017103	MANHOLE (RCFC&WCDS MH 252)	EA	7	5,625.00	39,375.00	5,000.00	35,000.00
37	000003	JUNCTION STRUCTURE (RCFC&WCDS JS 227)	EA	11	1,180.00	12,980.00	2,200.00	24,200.00
38	840656	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,000	0.29	4,060.00	0.30	4,200.00
39	840515	THERMOPLASTIC PAVEMENT MARKING	SQFT	1,400	3.65	5,110.00	4.00	5,600.00
40	850102	PAVEMENT MARKER (REFLECTIVE)	EA	700	3.75	2,625.00	4.00	2,800.00
41	566011	ROADSIDE SIGN - ONE POST	EA	24	243.50	5,844.00	255.00	6,120.00
42	068565	RELOCATE SIGN	EA	16	75.00	1,200.00	75.00	1,200.00
43	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND MILES AVE]	EA	1	101,700.00	101,700.00	95,000.00	95,000.00
44	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND PALMYRA	EA	1	108,600.00	108,600.00	124,927.20	124,927.20
45	000003	SPECIAL SIGN	EA	10	1,400.00	14,000.00	750.00	7,500.00
46	000003	SPECIAL SIGN (BUSINESS SIGN)	FA	1	10,000.00	10,000.00	10,000.00	10,000.00
47	000003	4" PVC PRIVATE WATER SYSTEM	LS	1	6,465.00	6,465.00	17,000.00	17,000.00
48	000003	CONCRETE WHEEL STOP	EA	18	31.00	558.00	40.00	720.00
49	000003	PIPE SLURRY PLUG	EA	3	875.00	2,625.00	1,700.00	5,100.00
50	860811	DETECTOR LOOP	EA	30	235.00	7,050.00	300.00	9,000.00
51	000003	SLURRY BACKFILL CONCRETE IRRIGATION PIPE (14")	LF	1,435	6.25	8,968.75	16.00	22,960.00
52	000003	ENCROACHMENT PERMIT [CVWD]	FA	1	3,000.00	3,000.00	3,000.00	3,000.00
53	000003	MISCELLANEOUS PRIVATE UTILITY WORK	FA	1	20,000.00	20,000.00	20,000.00	20,000.00
53.A	000003	MISCELLANEOUS DIRECTED WORK	FA	1	50,000.00	50,000.00	50,000.00	50,000.00
		<b>SUBTOTAL</b>				<b>2,867,209.00</b>		<b>2,927,000.00</b>
		ITEMS 1-53.A						

ALTERNATE BID ITEMS - INDIO WATER AUTHORITY		Dateiland Construction Indio, CA 92201		Hardy & Harper Santa Ana, CA 92705				
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
54	152351	RELOCATE HYDRANT	EA	5	4,115.00	20,575.00	3,900.00	19,500.00
55	000003	6" DIP WATER MAIN HORIZONTAL BEND ASSEMBLY	EA	5	2,525.00	12,625.00	3,900.00	19,500.00
56	152452	ADJUST WATER VALVE COVER	EA	31	575.00	17,825.00	600.00	18,600.00
57	000003	1" WATER SERVICE LATERAL PER IWA STD 700	EA	6	3,160.00	18,960.00	200.00	1,200.00
58	000003	RELOCATE BLOW-OFF ASSEMBLY	EA	1	1,445.00	1,445.00	9,000.00	9,000.00
59	000003	BACKFLOW ASSEMBLY PER IWA STD 702	EA	1	1,785.00	1,785.00	3,000.00	3,000.00
		<b>SUBTOTAL</b>				<b>73,215.00</b>		<b>70,800.00</b>
		ITEMS 54-59						

**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

ALTERNATE BID ITEMS - VALLEY SANITARY DISTRICT		Dateland Construction Indio, CA 92201			Hardy & Harper Santa Ana, CA 92705			
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
60	152440	ADJUST MANHOLE TO GRADE	EA	20	475.00	9,500.00	1,000.00	20,000.00
61	000003	8" SDR 35 PVC SEWER PIPE	LF	340	62.00	21,080.00	85.00	28,900.00
62	152400	ADJUST SEWER CLEANOUT TO GRADE	EA	2	400.00	800.00	1,000.00	2,000.00
63	000003	4" SEWER CLEANOUT	EA	2	695.00	1,390.00	1,500.00	3,000.00
64	000003	4" SEWER LATERAL WITH CONCRETE ENCASUREMENT	LF	56	53.65	3,004.40	130.00	7,280.00
64.A	000003	ADJUST 8" PVC SEWER PIPE	LF	30	55.00	1,650.00	150.00	4,500.00
64.B	000003	REMOVE AND REPLACE 8" SDR 35 PVC 8" x 6" PVC WYE	EA	2	1,040.00	2,080.00	1,600.00	3,200.00
		<b>SUBTOTAL</b>				<b>39,504.40</b>		<b>68,880.00</b>
		ITEMS 60-64.B						

ALTERNATE BID ITEMS - IMPERIAL IRRIGATION DISTRICT		Dateland Construction Indio, CA 92201			Hardy & Harper Santa Ana, CA 92705			
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
65	000003	4" SCHEDULE 40 PVC	LF	30	9.50	285.00	30.00	900.00
66	000003	5" SCHEDULE 40 PVC	LF	290	10.25	2,972.50	35.00	10,150.00
67	000003	SINGLE PHASE TRANSFORMER PAD PER IID STANDARD	EA	1	1,100.00	1,100.00	2,000.00	2,000.00
68	000003	MEDIUM HANDHOLE ENCLOSURE (4' x 6.5' x 5') PER IID STANDARD	EA	1	5,335.00	5,335.00	5,470.00	5,470.00
		<b>SUBTOTAL</b>				<b>9,692.50</b>		<b>18,520.00</b>
		ITEMS 65-68						

PROJECT TOTAL				2,989,620.90		3,085,200.00	
ITEMS 1-68							

**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

BASE BID		Hazard Construction Company San Diego, CA 92121			Riverside Construction Company, Inc. Riverside, CA 92502			
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
1	999990	MOBILIZATION	LS	1	90,000.00	90,000.00	90,000.00	90,000.00
2	160101	CLEARING AND GRUBBING	LS	1	175,000.00	175,000.00	175,000.00	175,000.00
3	066102	DUST ABATEMENT	LS	1	10,300.00	10,300.00	42,000.00	42,000.00
4	170101	DEVELOP WATER SUPPLY	LS	1	7,000.00	7,000.00	9,200.00	9,200.00
5	066105	RESIDENT ENGINEERS OFFICE	LS	1	11,000.00	11,000.00	7,000.00	7,000.00
6	074020	WATER POLLUTION CONTROL	LS	1	35,000.00	35,000.00	25,000.00	25,000.00
7	190101	ROADWAY EXCAVATION	CY	10,300	17.00	175,100.00	18.00	185,400.00
8	220101	FINISHING ROADWAY	LS	1	6,000.00	6,000.00	9,000.00	9,000.00
9	120100	TRAFFIC CONTROL SYSTEMS	LS	1	55,000.00	55,000.00	60,000.00	60,000.00
10	153103	COLD PLANE ASPHALT CONCRETE PAVEMENT (0.15' MAXIMUM)	SQYD	1,320	6.00	7,920.00	4.00	5,280.00
11	390130	HOT MIX ASPHALT	TON	3,680	77.00	283,360.00	72.00	264,960.00
12	013901	ASPHALT RUBBER HOT MIX	TON	2,080	103.00	214,240.00	96.00	199,680.00
13	260201	CLASS 2 AGGREGATE BASE	CY	5,960	29.00	172,840.00	33.00	196,680.00
14	731516	MINOR CONCRETE (DRIVEWAY)	SQFT	7,940	5.30	42,082.00	8.75	69,475.00
15	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	3,760	14.80	55,648.00	24.00	90,240.00
16	017310	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207)	EA	17	600.00	10,200.00	3,100.00	52,700.00
17	017312	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207A)	EA	5	5,000.00	25,000.00	8,100.00	40,500.00
18	017317	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	6,500	7.90	51,350.00	11.00	71,500.00
19	731521	MINOR CONCRETE (SIDEWALK)	SQFT	22,700	4.10	93,070.00	5.00	113,500.00
20	017309	MINOR CONCRETE (TYPE "D" CURB) (CRS 204)	LF	15	12.00	180.00	26.00	390.00
21	000003	MINOR CONCRETE (TYPE "D-1" CURB) (CRS 203)	LF	20	12.00	240.00	32.00	640.00
22	510503	MINOR CONCRETE (STRUCTURE) [CONCRETE BULKHEAD-RCFC&WCD M8'16] [66" BULKHEAD]	EA	1	1,300.00	1,300.00	1,200.00	1,200.00
23	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	4	1,200.00	4,800.00	7,000.00	28,000.00
24	017316	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	15	1,000.00	15,000.00	4,200.00	63,000.00
25	000003	INSTALL 24" BOX TREE [ACACIA ANEURA MULGA / PINUS ELDARICA TREES]	EA	8	550.00	4,400.00	740.00	5,920.00
26	000003	REMOVE AND REINSTALL STREET LIGHT PER COI STD 202	EA	7	2,500.00	17,500.00	1,200.00	8,400.00
27	000003	ADJUST STORM DRAIN MANHOLE TO GRADE	EA	2	1,000.00	2,000.00	475.00	950.00
28	518201	MASONRY BLOCK WALL	SQFT	650	49.00	31,850.00	50.00	32,500.00
29	833088	TUBULAR HANDRAILING	LF	184	70.00	12,880.00	55.00	10,120.00
30	650014	18" REINFORCED CONCRETE PIPE	LF	655	67.00	43,885.00	94.00	61,570.00
31	000003	24" REINFORCED CONCRETE PIPE	LF	340	78.00	26,520.00	260.00	88,400.00
32	000003	66" REINFORCED CONCRETE PIPE	LF	2,812	228.00	641,136.00	196.00	551,152.00
33	000003	REINFORCED CONCRETE 4'X6' TRANSITION STRUCTURE	EA	1	13,600.00	13,600.00	17,000.00	17,000.00
34	017003	CATCH BASIN (CURB INLET) (CRS 300)	EA	23	5,500.00	126,500.00	5,700.00	131,100.00

**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

BASE BID (CONTINUED)		Hazard Construction Company San Diego, CA 92121			Riverside Construction Company, Inc. Riverside, CA 92502			
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
35	017101	MANHOLE (RCFC&WCDS MH 251)	EA	6	4,300.00	25,800.00	5,000.00	30,000.00
36	017103	MANHOLE (RCFC&WCDS MH 252)	EA	7	5,100.00	35,700.00	5,700.00	39,900.00
37	000003	JUNCTION STRUCTURE (RCFC&WCDS JS 227)	EA	11	1,600.00	17,600.00	1,200.00	13,200.00
38	840656	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,000	0.28	3,920.00	0.30	4,200.00
39	840515	THERMOPLASTIC PAVEMENT MARKING	SQFT	1,400	3.60	5,040.00	3.50	4,900.00
40	850102	PAVEMENT MARKER (REFLECTIVE)	EA	700	3.00	2,100.00	3.25	2,275.00
41	566011	ROADSIDE SIGN - ONE POST	EA	24	320.00	7,680.00	250.00	6,000.00
42	066565	RELOCATE SIGN	EA	16	140.00	2,240.00	75.00	1,200.00
43	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND MILES AVE]	EA	1	136,000.00	136,000.00	105,000.00	105,000.00
44	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND PALMYRA	EA	1	133,000.00	133,000.00	110,000.00	110,000.00
45	000003	SPECIAL SIGN	EA	10	700.00	7,000.00	900.00	9,000.00
46	000003	SPECIAL SIGN (BUSINESS SIGN)	FA	1	10,000.00	10,000.00	10,000.00	10,000.00
47	000003	4" PVC PRIVATE WATER SYSTEM	LS	1	11,200.00	11,200.00	9,600.00	9,600.00
48	000003	CONCRETE WHEEL STOP	EA	18	40.00	720.00	40.00	720.00
49	000003	PIPE SLURRY PLUG	EA	3	550.00	1,650.00	500.00	1,500.00
50	860811	DETECTOR LOOP	EA	30	300.00	9,000.00	235.00	7,050.00
51	000003	SLURRY BACKFILL CONCRETE IRRIGATION PIPE (14")	LF	1,435	10.00	14,350.00	6.00	8,610.00
52	000003	ENCROACHMENT PERMIT (CVWD)	FA	1	3,000.00	3,000.00	3,000.00	3,000.00
53	000003	MISCELLANEOUS PRIVATE UTILITY WORK	FA	1	20,000.00	20,000.00	20,000.00	20,000.00
53.A	000003	MISCELLANEOUS DIRECTED WORK	FA	1	50,000.00	50,000.00	50,000.00	50,000.00
<b>SUBTOTAL</b>						<b>2,957,901.00</b>		<b>3,143,612.00</b>
<b>ITEMS 1-53.A</b>								

ALTERNATE BID ITEMS - INDIO WATER AUTHORITY		Hazard Construction Company San Diego, CA 92121			Riverside Construction Company, Inc. Riverside, CA 92502			
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
54	152351	RELOCATE HYDRANT	EA	5	3,500.00	17,500.00	1,800.00	9,000.00
55	000003	6" DIP WATER MAIN HORIZONTAL BEND ASSEMBLY	EA	5	3,500.00	17,500.00	3,500.00	17,500.00
56	152452	ADJUST WATER VALVE COVER	EA	31	870.00	26,970.00	30.00	930.00
57	000003	1" WATER SERVICE LATERAL PER IWA STD 700	EA	6	2,700.00	16,200.00	2,300.00	13,800.00
58	000003	RELOCATE BLOW-OFF ASSEMBLY	EA	1	2,800.00	2,800.00	1,800.00	1,800.00
59	000003	BACKFLOW ASSEMBLY PER IWA STD 702	EA	1	4,900.00	4,900.00	5,800.00	5,800.00
<b>SUBTOTAL</b>						<b>85,870.00</b>		<b>48,830.00</b>
<b>ITEMS 54-59</b>								



**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

BASE BID ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	Matich Corporation Riverside, CA 92501		Granite Construction Company Indio, CA 92203	
					UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
1	999990	MOBILIZATION	LS	1	75,000.00	75,000.00	90,000.00	90,000.00
2	160101	CLEARING AND GRUBBING	LS	1	280,044.25	280,044.25	127,733.00	127,733.00
3	066102	DUST ABATEMENT	LS	1	7,500.00	7,500.00	6,500.00	6,500.00
4	170101	DEVELOP WATER SUPPLY	LS	1	7,000.00	7,000.00	1,500.00	1,500.00
5	066105	RESIDENT ENGINEERS OFFICE	LS	1	7,500.00	7,500.00	4,500.00	4,500.00
6	074020	WATER POLLUTION CONTROL	LS	1	5,000.00	5,000.00	1,200.00	1,200.00
7	190101	ROADWAY EXCAVATION	CY	10,300	28.00	288,400.00	36.00	370,800.00
8	220101	FINISHING ROADWAY	LS	1	2,000.00	2,000.00	2,000.00	2,000.00
9	120100	TRAFFIC CONTROL SYSTEMS	LS	1	50,000.00	50,000.00	70,000.00	70,000.00
10	153103	COLD PLANE ASPHALT CONCRETE PAVEMENT [0.15' MAXIMUM]	SQYD	1,320	5.75	7,590.00	10.00	13,200.00
11	390130	HOT MIX ASPHALT	TON	3,680	69.00	253,920.00	81.00	298,080.00
12	013901	ASPHALT RUBBER HOT MIX	TON	2,080	92.00	191,360.00	133.00	276,640.00
13	260201	CLASS 2 AGGREGATE BASE	CY	5,960	23.00	137,080.00	32.00	190,720.00
14	731516	MINOR CONCRETE (DRIVEWAY)	SQFT	7,940	5.50	43,670.00	5.50	43,670.00
15	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	3,760	15.75	59,220.00	32.00	120,320.00
16	017310	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207)	EA	17	1,375.00	23,375.00	700.00	11,900.00
17	017312	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207A)	EA	5	3,300.00	16,500.00	6,200.00	31,000.00
18	017317	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	6,500	5.75	37,375.00	6.50	42,250.00
19	731521	MINOR CONCRETE (SIDEWALK)	SQFT	22,700	5.25	119,175.00	4.50	102,150.00
20	017309	MINOR CONCRETE (TYPE "D" CURB) (CRS 204)	LF	15	75.00	1,125.00	100.00	1,500.00
21	000003	MINOR CONCRETE (TYPE "D-1" CURB) (CRS 203)	LF	20	75.00	1,500.00	75.00	1,500.00
22	510503	MINOR CONCRETE (STRUCTURE) [CONCRETE BULKHEAD- RCF&WCD M816] [66" BULKHEAD]	EA	1	2,100.00	2,100.00	8,500.00	8,500.00
23	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	4	2,100.00	8,400.00	2,000.00	8,000.00
24	017316	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	15	2,100.00	31,500.00	1,000.00	15,000.00
25	000003	INSTALL 24" BOX TREE [ACACIA ANEURA MULGA / PINUS ELDARICA TREES]	EA	8	750.00	6,000.00	1,200.00	9,600.00
26	000003	REMOVE AND REINSTALL STREET LIGHT PER COI STD 202	EA	7	2,300.00	16,100.00	1,100.00	7,700.00
27	000003	ADJUST STORM DRAIN MANHOLE TO GRADE	EA	2	850.00	1,700.00	1,200.00	2,400.00
28	518201	MASONRY BLOCK WALL	SQFT	650	50.00	32,500.00	50.00	32,500.00
29	833088	TUBULAR HANDRAILING	LF	184	55.00	10,120.00	55.00	10,120.00
30	650014	18" REINFORCED CONCRETE PIPE	LF	655	115.00	75,325.00	80.00	52,400.00
31	000003	24" REINFORCED CONCRETE PIPE	LF	340	135.00	45,900.00	80.00	27,200.00
32	000003	66" REINFORCED CONCRETE PIPE	LF	2,812	240.00	674,880.00	240.00	674,880.00
33	000003	REINFORCED CONCRETE 4'X6' TRANSITION STRUCTURE	EA	1	13,000.00	13,000.00	25,000.00	25,000.00
34	017003	CATCH BASIN (CURB INLET) (CRS 300)	EA	23	6,300.00	144,900.00	7,000.00	161,000.00

**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

BASE BID (CONTINUED)		Match Corporation Riverside, CA 92501			Granite Construction Company Indio, CA 92203			
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
35	017101	MANHOLE (RCFC&WCDS MH 251)	EA	6	4,500.00	27,000.00	7,000.00	42,000.00
36	017103	MANHOLE (RCFC&WCDS MH 252)	EA	7	6,400.00	44,800.00	8,200.00	57,400.00
37	000003	JUNCTION STRUCTURE (RCFC&WCDS JS 227)	EA	11	2,200.00	24,200.00	2,600.00	28,600.00
38	840656	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,000	0.25	3,500.00	0.25	3,500.00
39	840515	THERMOPLASTIC PAVEMENT MARKING	SQFT	1,400	3.40	4,760.00	3.25	4,550.00
40	850102	PAVEMENT MARKER (REFLECTIVE)	EA	700	3.15	2,205.00	3.00	2,100.00
41	566011	ROADSIDE SIGN - ONE POST	EA	24	300.00	7,200.00	315.00	7,560.00
42	066565	RELOCATE SIGN	EA	16	130.00	2,080.00	135.00	2,160.00
43	861501	MODIFY SIGNAL AND LIGHTING (CLINTON ST AND MILES AVE)	EA	1	92,000.00	92,000.00	75,000.00	75,000.00
44	861501	MODIFY SIGNAL AND LIGHTING (CLINTON ST AND PALMYRA	EA	1	106,000.00	106,000.00	105,000.00	105,000.00
45	000003	SPECIAL SIGN	EA	10	825.00	8,250.00	500.00	5,000.00
46	000003	SPECIAL SIGN (BUSINESS SIGN)	FA	1	10,000.00	10,000.00	10,000.00	10,000.00
47	000003	4" PVC PRIVATE WATER SYSTEM	LS	1	20,000.00	20,000.00	8,000.00	8,000.00
48	000003	CONCRETE WHEEL STOP	EA	18	35.00	630.00	35.00	630.00
49	000003	PIPE SLURRY PLUG	EA	3	1,500.00	4,500.00	800.00	2,400.00
50	860811	DETECTOR LOOP	EA	30	195.00	5,850.00	350.00	10,500.00
51	000003	SLURRY BACKFILL CONCRETE IRRIGATION PIPE (14")	LF	1,435	5.25	7,533.75	15.00	21,525.00
52	000003	ENCROACHMENT PERMIT (CVWD)	FA	1	3,000.00	3,000.00	3,000.00	3,000.00
53	000003	MISCELLANEOUS PRIVATE UTILITY WORK	FA	1	20,000.00	20,000.00	20,000.00	20,000.00
53.A	000003	MISCELLANEOUS DIRECTED WORK	FA	1	50,000.00	50,000.00	50,000.00	50,000.00
<b>SUBTOTAL</b>						<b>3,120,268.00</b>		<b>3,300,388.00</b>
ITEMS 1-53.A								

ALTERNATE BID ITEMS - INDIO WATER AUTHORITY		Match Corporation Riverside, CA 92501			Granite Construction Company Indio, CA 92203			
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
54	152351	RELOCATE HYDRANT	EA	5	3,700.00	18,500.00	4,200.00	21,000.00
55	000003	6" DIP WATER MAIN HORIZONTAL BEND ASSEMBLY	EA	5	3,700.00	18,500.00	950.00	4,750.00
56	152452	ADJUST WATER VALVE COVER	EA	31	850.00	26,350.00	600.00	18,600.00
57	000003	1" WATER SERVICE LATERAL PER IWA STD 700	EA	6	2,100.00	12,600.00	2,500.00	15,000.00
58	000003	RELOCATE BLOW-OFF ASSEMBLY	EA	1	10,000.00	10,000.00	1,900.00	1,900.00
59	000003	BACKFLOW ASSEMBLY PER IWA STD 702	EA	1	3,700.00	3,700.00	3,100.00	3,100.00
<b>SUBTOTAL</b>						<b>89,650.00</b>		<b>64,350.00</b>
ITEMS 54-59								

**Riverside County Transportation Department  
Summary of Bids**

**PROJECT: Clinton Street in the City of Indio and County of Riverside  
Street Improvement Plans**

**Advertised: April 06, 2010 (Agenda Item: 3.76)  
Bids Open: 2 pm Date: Wednesday, April 28, 2010**

**PROJECT NO. B2-03892**

ALTERNATE BID ITEMS - VALLEY SANITARY DISTRICT		Match Corporation Riverside, CA 92501		Granite Construction Company Indio, CA 92203				
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
60	152440	ADJUST MANHOLE TO GRADE	EA	20	850.00	17,000.00	1,200.00	24,000.00
61	000003	8" SDR 35 PVC SEWER PIPE	LF	340	145.00	49,300.00	160.00	54,400.00
62	152400	ADJUST SEWER CLEANOUT TO GRADE	EA	2	850.00	1,700.00	800.00	1,600.00
63	000003	4" SEWER CLEANOUT	EA	2	2,600.00	5,200.00	1,000.00	2,000.00
64	000003	4" SEWER LATERAL WITH CONCRETE ENCASEMENT	LF	56	105.00	5,880.00	100.00	5,600.00
64-A	000003	ADJUST 8" PVC SEWER PIPE	LF	30	160.00	4,800.00	125.00	3,750.00
64-B	000003	REMOVE AND REPLACE 8" SDR 35 PVC 8" x 6" PVC WYE	EA	2	1,600.00	3,200.00	1,500.00	3,000.00
<b>SUBTOTAL</b>						<b>87,080.00</b>		
ITEMS 60-64.B								<b>94,350.00</b>

ALTERNATE BID ITEMS - IMPERIAL IRRIGATION DISTRICT		Match Corporation Riverside, Ca 92501		Granite Construction Company Indio, CA 92203				
ITEM NO.	ITEM CODE	CONTRACT ITEM	UNITS	QUANTITY	BID UNIT PRICE	BID ESTIMATE	BID UNIT PRICE	BID ESTIMATE
65	000003	4" SCHEDULE 40 PVC	LF	30	32.00	960.00	10.00	300.00
66	000003	5" SCHEDULE 40 PVC	LF	290	45.00	13,050.00	12.00	3,480.00
67	000003	SINGLE PHASE TRANSFORMER PAD PER IID STANDARD	EA	1	725.00	725.00	1,100.00	1,100.00
68	000003	MEDIUM HANDHOLE ENCLOSURE (4' x 6.5' x 5') PER IID STANDARD	EA	1	7,400.00	7,400.00	4,500.00	4,500.00
<b>SUBTOTAL</b>						<b>22,135.00</b>		<b>9,380.00</b>
ITEMS 65-68								

<b>PROJECT TOTAL</b>						<b>3,319,133.00</b>		<b>3,468,468.00</b>
ITEMS 1-68								



## CONTRACTOR'S PROPOSAL

TO: COUNTY OF RIVERSIDE

DATE: 4/28/2010

hereafter called "County":

BIDDER: Cooley Construction Inc  
(hereafter called "Contractor")

THE UNDERSIGNED, Contractor, having carefully examined the site and the Contract Documents for the construction of Clinton Street in the City of Indio and County of Riverside - Street Improvement Plans, Project No. B2-03892 hereby proposes to construct the work in accordance with the Contract Documents, including Addenda Nos. 1 for the amount stated in this Proposal.

By submitting this Proposal, Contractor agrees with County:

1. That unless withdrawn in person by Contractor or some person authorized in writing by Contractor not by telephone or telegram before the time specified in the Notice Inviting Bids for the public opening of bids, this Proposal constitutes an irrevocable offer for 90 calendar days after that date.
2. County has the right to reject any or all Proposals and to waive any irregularities or informalities contained in a Proposal.
3. To execute the Agreement and deliver the Faithful Performance Bond, Payment Bond and Insurance Certificate with endorsements, which comply with the requirements set forth in the Instructions to Bidders and General Conditions, within ten (10) working days of the date of the Notice of Acceptance of Proposal and Intent to Award as issued by the County of Riverside.
4. That the contract shall be awarded upon a resolution or minute order to that effect duly adopted by the governing body of County; and that execution of the Contract Documents shall constitute a written memorial thereof.
5. To submit to County such information as County may require to determine whether a particular Proposal is the lowest responsible bid submitted.

6. That the accompanying certified or cashier's check or Bid Bond is in an amount not less than 10% of the total bid submitted and constitutes a guarantee that if awarded the contract, Contractor will execute the Agreement and deliver the required bonds within ten (10) days after notice of award. If Contractor fails to execute and deliver said documents, the check or bond is to be charged with the costs of the resultant damages to County, including but not limited to publication costs, the difference in money between the amount bid and the amount in excess of the bid which it costs County to do or cause to be done the work involved, lease and rental costs, additional salaries and overhead, increased interest and costs of funding the project, attorney expense, additional engineering and architectural expense and cost of maintaining or constructing alternate facilities occasioned by the failure to execute and deliver said documents.
7. By signing this proposal the Contractor certifies that the representations made therein are made under penalty of perjury.

Cooley Construction, Inc  
Lic. 348033  
P.O. Box 401810  
Hesperia, CA 92340-1810

**CLINTON STREET**  
**IN THE CITY OF INDIO AND COUNTY OF RIVERSIDE** Cooley Construction, Inc  
**STREET IMPROVEMENTS** Lic. 348038  
 PROJECT NO. B2-03892 P.O. Box 401810  
 Hesperia, CA 92340-1810

**PROPOSAL (REVISED)**

ITEM No.	ITEM CODE	ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
1	999990	MOBILIZATION	LS	1	90,000. <sup>00</sup>	90,000. <sup>00</sup>
2	160101	CLEARING AND GRUBBING	LS	1	147,000. <sup>00</sup>	147,000. <sup>00</sup>
3	066102	DUST ABATEMENT	LS	1	7300. <sup>00</sup>	7300. <sup>00</sup>
4	170101	DEVELOP WATER SUPPLY	LS	1	3200. <sup>00</sup>	3200. <sup>00</sup>
5	066105	RESIDENT ENGINEERS OFFICE	LS	1	8400. <sup>00</sup>	8400. <sup>00</sup>
6	074020	WATER POLLUTION CONTROL	LS	1	10600. <sup>00</sup>	10600. <sup>00</sup>
7	190101	ROADWAY EXCAVATION	CY	10,300	15.50	159650. <sup>00</sup>
8	220101	FINISHING ROADWAY	LS	1	13700. <sup>00</sup>	13700. <sup>00</sup>
9	120100	TRAFFIC CONTROL SYSTEMS	LS	1	41000. <sup>00</sup>	41000. <sup>00</sup>
10	153103	COLD PLANE ASPHALT CONCRETE PAVEMENT [0.15' MAXIMUM]	SQYD	1,320	4.20	5544. <sup>00</sup>
11	390130	HOT MIX ASPHALT	TON	3,680	74.00	272,320. <sup>00</sup>
12	013901	ASPHALT RUBBER HOT MIX	TON	2,080	92.00	191,360. <sup>00</sup>
13	260201	CLASS 2 AGGREGATE BASE	CY	5,960	27.70	165,092. <sup>00</sup>
14	731516	MINOR CONCRETE (DRIVEWAY)	SQFT	7,940	4.30	34142. <sup>00</sup>
15	017304	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	3,760	17.40	65424. <sup>00</sup>
16	017310	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207)	EA	17	1280. <sup>00</sup>	21760. <sup>00</sup>
17	017312	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207A)	EA	5	4350. <sup>00</sup>	21750. <sup>00</sup>
18	017317	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	6,500	8.90	57850. <sup>00</sup>
19	731521	MINOR CONCRETE (SIDEWALK)	SQFT	22,700	4.40	99880. <sup>00</sup>
20	017309	MINOR CONCRETE (TYPE "D" CURB) (CRS 204)	LF	15	43. <sup>00</sup>	645. <sup>00</sup>
21	000003	MINOR CONCRETE (TYPE "D-1" CURB) (CRS 203)	LF	20	35. <sup>00</sup>	700. <sup>00</sup>
22	510503	MINOR CONCRETE (STRUCTURE) [CONCRETE BULKHEAD-RCFC&WCD M816] [66" BULKHEAD]	EA	1	1700. <sup>00</sup>	1700. <sup>00</sup>
23	017315	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	4	3140. <sup>00</sup>	12560. <sup>00</sup>
24	017316	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	15	2400. <sup>00</sup>	36000. <sup>00</sup>
25	000003	INSTALL 24" BOX TREE [ACACIA ANEURA MULGA / PINUS ELДАРICA TREES]	EA	8	424. <sup>00</sup>	3392. <sup>00</sup>
26	000003	REMOVE AND REINSTALL STREET LIGHT PER COI STD 202	EA	7	1200. <sup>00</sup>	8400. <sup>00</sup>
27	000003	ADJUST STORM DRAIN MANHOLE TO GRADE	EA	2	1080. <sup>00</sup>	2160. <sup>00</sup>
28	518201	MASONRY BLOCK WALL	SQFT	650	48.40	31460. <sup>00</sup>

**PROPOSAL (REVISED)**

ITEM No.	ITEM CODE	ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
29	833088	TUBULAR HANDRAILING	LF	184	60. <sup>00</sup>	11040. <sup>00</sup>
30	650014	18" REINFORCED CONCRETE PIPE	LF	655	63. <sup>00</sup>	41265. <sup>00</sup>
31	000003	24" REINFORCED CONCRETE PIPE	LF	340	70. <sup>00</sup>	23800. <sup>00</sup>
32	000003	66" REINFORCED CONCRETE PIPE	LF	2,812	198. <sup>00</sup>	556,776. <sup>00</sup>
33	000003	REINFORCED CONCRETE 4'X6' TRANSITION STRUCTURE	EA	1	11600. <sup>00</sup>	11600. <sup>00</sup>
34	017003	CATCH BASIN (CURB INLET) (CRS 300)	EA	23	6600. <sup>00</sup>	151,800. <sup>00</sup>
35	017101	MANHOLE (RCFC&WCDS MH 251)	EA	6	5300. <sup>00</sup>	31800. <sup>00</sup>
36	017103	MANHOLE (RCFC&WCDS MH 252)	EA	7	6500. <sup>00</sup>	45500. <sup>00</sup>
37	000003	JUNCTION STRUCTURE (RCFC&WCDS JS 227)	EA	11	1770. <sup>00</sup>	19470. <sup>00</sup>
38	840656	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,000	0.35	4900. <sup>00</sup>
39	840515	THERMOPLASTIC PAVEMENT MARKING	SQFT	1,400	4.20	5880. <sup>00</sup>
40	850102	PAVEMENT MARKER (REFLECTIVE)	EA	700	2.54	1778. <sup>00</sup>
41	566011	ROADSIDE SIGN - ONE POST	EA	24	237. <sup>00</sup>	5688. <sup>00</sup>
42	066565	RELOCATE SIGN	EA	16	105. <sup>00</sup>	1680. <sup>00</sup>
43	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND MILES AVE]	EA	1	103,000. <sup>00</sup>	103000. <sup>00</sup>
44	861501	MODIFY SIGNAL AND LIGHTING [CLINTON ST AND PALMYRA AVE]	EA	1	110,000. <sup>00</sup>	110,000. <sup>00</sup>
45	000003	SPECIAL SIGN	EA	10	680. <sup>00</sup>	6800. <sup>00</sup>
46	000003	SPECIAL SIGN (BUSINESS SIGN)	FA	1	10,000.00	10,000.00
47	000003	4" PVC PRIVATE WATER SYSTEM	LS	1	7900. <sup>00</sup>	7900. <sup>00</sup>
48	000003	CONCRETE WHEEL STOP	EA	18	52. <sup>00</sup>	936. <sup>00</sup>
49	000003	PIPE SLURRY PLUG	EA	3	950. <sup>00</sup>	2850. <sup>00</sup>
50	860811	DETECTOR LOOP	EA	30	238. <sup>00</sup>	7140. <sup>00</sup>
51	000003	SLURRY BACKFILL CONCRETE IRRIGATION PIPE (14")	LF	1,435	7.40	10619. <sup>00</sup>
52	000003	ENCROACHMENT PERMIT [CVWD]	FA	1	3,000.00	3,000.00
53	000003	MISCELLANEOUS PRIVATE UTILITY WORK	FA	1	20,000.00	20,000.00
53.A	000003	MISCELLANEOUS DIRECTED WORK	FA	1	50,000.00	50,000.00

SUB-TOTAL:  
 ITEMS 1-53.A

TWO MILLION, SEVEN HUNDRED FIFTY-EIGHT THOUSAND,  
 TWO HUNDRED ELEVEN DOLLARS AND NO CENTS

\$2,758,211.<sup>00</sup>

"WORDS"

Cooley Construction, Inc  
 Lic. 348033  
 P.O. Box 401810  
 Hesperia, CA 92340-1810

**PROPOSAL (REVISED)**

ITEM No.	ITEM CODE	ITEM	UNIT	ESTIMATED QUANTITY	ITEM PRICE (IN FIGURES)	TOTAL (IN FIGURES)
----------	-----------	------	------	--------------------	-------------------------	--------------------

**Alternate Bid Items - Indio Water Authority**

54	152351	RELOCATE HYDRANT	EA	5	2440. <sup>00</sup>	12200. <sup>00</sup>
55	000003	6" DIP WATER MAIN HORIZONTAL BEND ASSEMBLY	EA	5	4640. <sup>00</sup>	23200. <sup>00</sup>
56	152452	ADJUST WATER VALVE COVER	EA	31	450. <sup>00</sup>	13950. <sup>00</sup>
57	000003	1" WATER SERVICE LATERAL PER IWA STD 700	EA	6	1700. <sup>00</sup>	10200. <sup>00</sup>
58	000003	RELOCATE BLOW-OFF ASSEMBLY	EA	1	2530. <sup>00</sup>	2530. <sup>00</sup>
59	000003	BACKFLOW ASSEMBLY PER IWA STD 702	EA	1	2320. <sup>00</sup>	2320. <sup>00</sup>

SUB-TOTAL: SIXTY-FOUR THOUSAND, FOUR HUNDRED DOLLARS No CENTS \$64,400.<sup>00</sup>  
 ITEMS 54-59 "WORDS"

**Alternate Bid Items - Valley Sanitary District**

60	152440	ADJUST MANHOLE TO GRADE	EA	20	780. <sup>00</sup>	15600. <sup>00</sup>
61	000003	8" SDR 35 PVC SEWER PIPE	LF	340	155. <sup>00</sup>	52700. <sup>00</sup>
62	152400	ADJUST SEWER CLEANOUT TO GRADE	EA	2	850. <sup>00</sup>	1700. <sup>00</sup>
63	000003	4" SEWER CLEANOUT	EA	2	850. <sup>00</sup>	1700. <sup>00</sup>
64	000003	4" SEWER LATERAL WITH CONCRETE ENCASEMENT	LF	56	74. <sup>00</sup>	4144. <sup>00</sup>
64.A	000003	ADJUST 8" PVC SEWER PIPE	LF	30	84. <sup>00</sup>	2520. <sup>00</sup>
64.B	000003	REMOVE AND REPLACE 8" SDR 35 PVC 8" x 6" PVC WYE	EA	2	5300. <sup>00</sup>	10600. <sup>00</sup>

SUB-TOTAL: EIGHTY-EIGHT THOUSAND, NINE HUNDRED SIXTY-FOUR DOLLARS \$88,964.<sup>00</sup>  
 ITEMS 60-64.B "WORDS" No CENTS

**Alternate Bid Items - Imperial Irrigation District**

65	000003	4" SCHEDULE 40 PVC	LF	30	33. <sup>00</sup>	990. <sup>00</sup>
66	000003	5" SCHEDULE 40 PVC	LF	290	17. <sup>00</sup>	4930. <sup>00</sup>
67	000003	SINGLE PHASE TRANSFORMER PAD PER IID STANDARD	EA	1	1300. <sup>00</sup>	1300. <sup>00</sup>
68	000003	MEDIUM HANDHOLE ENCLOSURE (4' x 6.5' x 5') PER IID STANDARD	EA	1	5800. <sup>00</sup>	5800. <sup>00</sup>

SUB-TOTAL: THIRTEEN THOUSAND, TWENTY DOLLARS AND No CENTS \$13,020.<sup>00</sup>  
 ITEMS 65-68 "WORDS"

PROJECT TOTAL: TWO MILLION, NINE HUNDRED TWENTY-FOUR THOUSAND, FIVE HUNDRED NINETY-FIVE DOLLARS AND No CENTS \$2,924,595.<sup>00</sup>  
 ITEMS 1-68 "WORDS"

Cooley Construction, Inc  
 Lic. 348038  
 P.O. Box 401810  
 Hesperia, CA 92340-1810

**BIDDER DATA:**

Name of Bidder Cooley Construction Inc

Type of Organization Corp

Person(s) Authorized to Sign for Bidder Paul Cooley Jr, Glen Daniels  
Scott Daniels

Address Po Box 401810 Hesperia CA

Phone 760/948-8403

Contractor's License 348038 A  
Type & Number

Expiration Date 2/2011

8. DESIGNATION OF SUBCONTRACTORS: Contractor submits the following complete list of each subcontractor who will perform work or labor or render service in or about the construction in an amount in excess of 1/2 of 1% of the total bid.

<u>ITEM</u>	<u>SUBCONTRACTOR</u>	<u>ADDRESS</u>	<u>LICENSE NO.</u>
<u>SEE ATTACHED</u>			

Percent of work to be performed by sub-contractors: 49%  
(Note: 50% of the work required to be performed by general contractor)

IN WITNESS WHEREOF Contractor executed this Proposal as of the date set forth on Page 1 of this proposal.

Cooley Construction Inc  
[Signature]  
TITLE President  
"Contractor"

**DESIGNATION OF SUBCONTRACTORS:**

ITEM	SUBCONTRACTOR	ADDRESS	LICENSE NO.
14, 15, 16, 17, 18, 19, 20, 21, 23, 24	KOBOLD CONSTRUCTION	CHINO, CA	538329
2 (PORTION)	YOUNG'S LANDCLEARING	THERMAL, CA	632630
27, 56, 60 22, 30, 31, 32, 33 34, 35, 36, 37, 47 49, 51, 54, 55, 57 58, 59, 61, 62, 63 64, 64A, 64B,	JAMES A. SHIRLEY CONSTRUCTION	YUCCA VALLEY, CA	710357
28	BARTHOLOMEY & SONS MASONRY	ONTARIO, CA	434350
38, 39, 40, 41, 42, 45 48	JP STRIPING	BEAUMONT, CA	746266
26, 43, 44, 50, 65 66, 67, 68	SIERRA PACIFIC ELECTRIC	RIVERSIDE, CA	254048

COOLEY CONSTRUCTION INC



TITLE President

**Cooley Construction, Inc**  
 Lic. 348038  
 P.O. Box 401810  
 Hesperia, CA 92340-1810

"Contractor"

**AFFIDAVIT FOR INDIVIDUAL CONTRACTORS**

\_\_\_\_\_ declares as follows:

That he or she is the party making the foregoing proposal or bid; that the bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the bid is genuine and not collusive or sham; that the bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any bidder or anyone else to put in a sham bid, or that anyone shall refrain from bidding; that the bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid price of the bidder or any other bidder, or to fix any overhead, profit, or cost element of the bid price, or of that of any other bidder, or to secure any advantage against the County of Riverside or anyone interested in the proposed contract; that all statements contained in the bid are true; and, further, that the bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay, any fee to any corporation, partnership, company association, organization, bid depository, or to any member or agent thereof to effectuate a collusive or sham bid.

**I declare, under penalty of perjury, that the foregoing is true and correct.**

**Dated this \_\_\_\_\_ (day) of \_\_\_\_\_ (month),  
\_\_\_\_\_ (year) at \_\_\_\_\_, California**

**Signature of affiant: \_\_\_\_\_**

Note: Notarization of signature required



**AFFIDAVIT FOR JOINT VENTURE OR COPARTNERSHIP CONTRACTOR**

\_\_\_\_\_ Declares as follows:

That he or she is a member of the joint venture or copartnership firm designated as \_\_\_\_\_ which is the party making the foregoing proposal or bid; that the bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the bid is genuine and not collusive or sham; that the bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any bidder or anyone else to put in a sham bid, or that anyone shall refrain from bidding; that the bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid price of the bidder or any other bidder, or to fix any overhead, profit, or cost element of the bid price, or of that of any other bidder, or to secure any advantage against the County of Riverside or anyone interested in the proposed contract; that all statements contained in the bid are true; and, further, that the bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay, any fee to any corporation, partnership, company association, organization, bid depository or to any member or agent thereof to effectuate a collusive or sham bid.

That he has been and is duly vested with authority to make and sign instruments for the joint venture or copartnership by \_\_\_\_\_ who constitute the other members of the joint venture or copartnership.

**I declare, under penalty of perjury, that the foregoing is true and correct.**

Dated this \_\_\_\_\_ (day) of \_\_\_\_\_ (month),  
\_\_\_\_\_ (year)  
at \_\_\_\_\_, California

**Signature of affiant:** \_\_\_\_\_

Note: Notarization of signature required

**AFFIDAVIT FOR CORPORATE CONTRACTOR**

Paul R Cooley Jr declares as follows:

That he or she is President of Cooley Construction Inc a corporation which is the party making the foregoing proposal or bid; that the bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the bid is genuine and not collusive or sham; that the bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any bidder or anyone else to put in a sham bid, or that anyone shall refrain from bidding; that the bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid price of the bidder or any other bidder, or to fix any overhead, profit, or cost element of the bid price, or of that of any other bidder, or to secure any advantage against the County of Riverside or anyone interested in the proposed contract; that all statements contained in the bid are true; and, further, that the bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay, any fee to any corporation, partnership, company, association, organization, bid depository, or to any member or agent thereof to effectuate a collusive or sham bid.

**I declare, under penalty of perjury, that the foregoing is true and correct.**

Dated this 27th (day) of April (month),  
2010 (year)  
at Hesperia, California

Signature of affiant: 


Note: Notarization of signature required

Notarial Certificate Attached

State of California  
County of San Bernardino

Subscribed and sworn to (or affirmed) before me on this 27th  
day of April, 2010, by Paul R Cooley Jr.

proved to me on the basis of satisfactory evidence to be the  
person(s) who appeared before me.



(Seal)

Signature

Karen M Shackelford

**BID BOND**

**Recitals:**

1. Cooley Construction, Inc. "Contractor", has submitted his Contractor's Proposal to County of Riverside, "County", for the construction of public work for Clinton Street in accordance with a Notice Inviting Bids of County dated April 6, 2010.  
Bid date: April 28, 2010
2. Fidelity and Deposit Company of Maryland a Maryland corporation, hereafter called "Surety", is the surety of this Bond.

**Agreement:**

We, Contractor as principal and Surety as surety, jointly and severally agree and state as follows:

1. The amount of the obligation of this bond is 10% of the amount of the Contractor's Proposal, including bid alternates, and inures to the benefit of County.
2. This Bond is exonerated by (1) County rejecting said Proposal or, in the alternate, (2) if said Proposal is accepted, Contractor executes the Agreement and furnishes the Bonds as agreed to in its Proposal, otherwise it remains in full force and effect for the recovery of loss, damage and expense of County resulting from failure of Contractor to act as agreed to in its Proposal. Some types of possible loss, damage and expense are specified in the Contractor's Proposal.
3. Surety, for value received, stipulates and agrees that its obligations hereunder shall in no way be impaired or affected by any extension of time within which County may accept the Proposal and waives notice of any such extension.
4. This Bond is binding on our heirs, executors, administrators, successors and assigns.

Dated: April 13, 2010

Fidelity and Deposit Company of Maryland

Cooley Construction, Inc.

By [Signature]  
 Title: Janet C. Rojo, Attorney in Fact  
 "Surety"

By [Signature]  
 Title: President  
 "Contractor"

STATE OF CALIFORNIA }  
 COUNTY OF \_\_\_\_\_ } ss. SURETY'S ACKNOWLEDGEMENT

On \_\_\_\_\_ before me, \_\_\_\_\_ personally appeared, \_\_\_\_\_, known to me, or proved to me on the basis of satisfactory evidence, to be the person whose name is subscribed to the within instrument and acknowledged to me that he/she executed the same in his/her authorized capacities, and that by his/her signature on the instrument the person, or the entity upon behalf of which the person acted, executed the instrument.

WITNESS my hand and official seal.

*Notarial Certificate Attached*

\_\_\_\_\_  
Signature of Notary Public

Notary Public (Seal)

**Note: All signatures must be notarized**

**CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT**

State of California }  
County of San Francisco

On April 13, 2010 before me, Virginia L. Ledford-Black, Notary Public  
Date Here Insert Name and Title of the Officer


personally appeared Janet C. Rojo  
Name(s) of Signer(s)

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature Virginia L. Ledford-Black  
Signature of Notary Public



Place Notary Seal Above

**OPTIONAL**

*Though the information below is not required by law, it may prove valuable to persons relying on the document and could prevent fraudulent removal and reattachment of this form to another document.*

**Description of Attached Document**

Title or Type of Document: \_\_\_\_\_

Document Date: \_\_\_\_\_ Number of Pages: \_\_\_\_\_

Signer(s) Other Than Named Above: \_\_\_\_\_

**Capacity(ies) Claimed by Signer(s)**

Signer's Name: \_\_\_\_\_

- Individual
- Corporate Officer — Title(s): \_\_\_\_\_
- Partner —  Limited  General
- Attorney in Fact
- Trustee
- Guardian or Conservator
- Other: \_\_\_\_\_

**RIGHT THUMBPRINT OF SIGNER**  
Top of thumb here

Signer Is Representing: \_\_\_\_\_

Signer's Name: \_\_\_\_\_

- Individual
- Corporate Officer — Title(s): \_\_\_\_\_
- Partner —  Limited  General
- Attorney in Fact
- Trustee
- Guardian or Conservator
- Other: \_\_\_\_\_

**RIGHT THUMBPRINT OF SIGNER**  
Top of thumb here

Signer Is Representing: \_\_\_\_\_

**Power of Attorney**  
**FIDELITY AND DEPOSIT COMPANY OF MARYLAND**

KNOW ALL MEN BY THESE PRESENTS: That the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, a corporation of the State of Maryland, by THEODORE G. MARTINEZ, Vice President, and ERIC D. BARNES, Assistant Secretary, in pursuance of authority granted by Article VI, Section 2, of the By-Laws of said Company, which are set forth on the reverse side hereof and are hereby certified to be in full force and effect on the date hereof, does hereby nominate, constitute and appoint Susan HECKER, Janet C. ROJO, Betty L. TOLENTINO, M. MOODY, Maureen O'CONNELL, J.M. ALBADA, Brian F. COOPER, Robert P. WRIXON and Virginia L. BLACK, all of San Francisco, California, EACH its true and lawful agent and Attorney-in-Fact to make, execute, seal and deliver for, and on its behalf as surety, and as its act and deed: any and all bonds and undertakings, and the execution of such bonds or undertakings in pursuance of these presents, shall be as binding upon said Company, as fully and amply, to all intents and purposes, as if they had been duly executed and acknowledged by the regularly elected officers of the Company at its office in Baltimore, Md., in their own proper persons. This power of attorney, revokes that issued on behalf of Susan HECKER, Janet C. ROJO, Betty L. TOLENTINO, M. MOODY, Maureen O'CONNELL, J.M. ALBADA, Brian F. COOPER, Robert P. WRIXON, dated July 14, 2008.

The said Assistant Secretary does hereby certify that the extract set forth on the reverse side hereof is a true copy of Article VI, Section 2, of the By-Laws of said Company, and is now in force.

IN WITNESS WHEREOF, the said Vice-President and Assistant Secretary have hereunto subscribed their names and affixed the Corporate Seal of the said FIDELITY AND DEPOSIT COMPANY OF MARYLAND, this 15th day of October, A.D. 2008.

ATTEST:

**FIDELITY AND DEPOSIT COMPANY OF MARYLAND**



*Eric D. Barnes*

*Theodore G. Martinez*

Eric D. Barnes

Assistant Secretary


By:

Theodore G. Martinez

State of Maryland }  
Baltimore County } ss:

On this 15th day of October, A.D. 2008, before the subscriber, a Notary Public of the State of Maryland, duly commissioned and qualified, came THEODORE G. MARTINEZ, Vice President, and ERIC D. BARNES, Assistant Secretary of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, to me personally known to be the individuals and officers described in and who executed the preceding instrument, and they each acknowledged the execution of the same, and being by me duly sworn, severally and each for himself depose and saith, that they are the said officers of the Company aforesaid, and that the seal affixed to the preceding instrument is the Corporate Seal of said Company, and that the said Corporate Seal and their signatures as such officers were duly affixed and subscribed to the said instrument by the authority and direction of the said Corporation.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed my Official Seal the day and year first above written.



*Dennis R. Hayden*

Dennis R. Hayden

Notary Public

My Commission Expires: February 15, 2013

**EXTRACT FROM BY-LAWS OF FIDELITY AND DEPOSIT COMPANY OF MARYLAND**

“Article VI, Section 2. The Chairman of the Board, or the President, or any Executive Vice-President, or any of the Senior Vice-Presidents or Vice-Presidents specially authorized so to do by the Board of Directors or by the Executive Committee, shall have power, by and with the concurrence of the Secretary or any one of the Assistant Secretaries, to appoint Resident Vice-Presidents, Assistant Vice-Presidents and Attorneys-in-Fact as the business of the Company may require, or to authorize any person or persons to execute on behalf of the Company any bonds, undertakings, recognizances, stipulations, policies, contracts, agreements, deeds, and releases and assignments of judgements, decrees, mortgages and instruments in the nature of mortgages,...and to affix the seal of the Company thereto.”

**CERTIFICATE**

I, the undersigned, Assistant Secretary of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, do hereby certify that the foregoing Power of Attorney is still in full force and effect on the date of this certificate; and I do further certify that the Vice-President who executed the said Power of Attorney was one of the additional Vice-Presidents specially authorized by the Board of Directors to appoint any Attorney-in-Fact as provided in Article VI, Section 2, of the By-Laws of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND.

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the 10th day of May, 1990.

RESOLVED: "That the facsimile or mechanically reproduced seal of the company and facsimile or mechanically reproduced signature of any Vice-President, Secretary, or Assistant Secretary of the Company, whether made heretofore or hereafter, wherever appearing upon a certified copy of any power of attorney issued by the Company, shall be valid and binding upon the Company with the same force and effect as though manually affixed."

IN TESTIMONY WHEREOF, I have hereunto subscribed my name and affixed the corporate seal of the said Company,

this 13th day of April, 2010.



*Assistant Secretary*

**ACKNOWLEDGMENT**

State of California  
County of San Bernardino )


On April 27, 2010 before me, Karen M Shackelford, Notary Public  
(insert name and title of the officer)

personally appeared Paul R Cooley Jr.  
who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are  
subscribed to the within instrument and acknowledged to me that he/she/they executed the same in  
his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the  
person(s) or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing  
paragraph is true and correct.

WITNESS my hand and official seal.

Signature Karen M Shackelford (Seal)







# COUNTY OF RIVERSIDE TRANSPORTATION AND LAND MANAGEMENT AGENCY



*Juan C. Perez, P.E., T.E.,  
Director of Transportation*

## Transportation Department

### ADDENDUM NUMBER 1

Dated April 22, 2010

to the  
Specifications and Contract Documents  
for the construction of

Clinton Street  
In The City of Indio and County of Riverside  
Project No B2-030892

**Bids Due: Wednesday, April 28, 2010; 2:00 p.m.**  
14<sup>th</sup> Street Transportation Annex  
3525 14<sup>th</sup> Street; Riverside, CA 92501  
(951) 955-6780

This Addendum is issued pursuant to the instructions to Bidders, Item No. 8, of the Contract Document for the referenced project. This Addendum is issued as a supplement to the plans, specifications and special provisions for the referenced project. Any revisions to the plans and specifications shall become a part of the Contract Documents, and each bidder shall acknowledge receipt thereof on the Contractor's Proposal. Bidders are directed to sign this addendum as acknowledged, and attach the signed addendum to the contractor's submitted proposal.

**Note:** During the advertisement period of this project, this document and attachments (if any) are available upon request at the office of the Transportation Department, and are available as a free download at the Transportation Department's website:  
[www.tlma.co.riverside.ca.us/trans/con\\_bid\\_advertisements.html](http://www.tlma.co.riverside.ca.us/trans/con_bid_advertisements.html)

### MODIFICATIONS / CLARIFICATIONS TO THE PLANS FOR CLINTON STREET

**Item 1:** The following Plan sheet is revised by **Attachment "A"** and made a part hereof:

Delete and replace Sheet 17 of 24 with revised "**MASONRY RETAINING WALL**", **Attachment "A"**

**Item 2:**        **Revision of Construction Note 15.** Refer to plans sheet CONSTRUCTION NOTE INDEX, sheet 2 of 24:

- Delete construction note 15 and replace with "CONSTRUCT MASONRY RETAINING WALL PER CALTRANS STD PLAN B3-11 TYPE 6A WITH 4" CONCRETE PAVING PER SECTION A-A HEREON"

### **MODIFICATIONS / CLARIFICATIONS TO SPECIAL PROVISIONS**

**Item 3:**        **Revised Proposal.** Refer to "Proposal" pages B3 - B5. Proposal (pages B3 - B5) are deleted and replaced with revised "Proposal" attached herewith as **Attachment "B"** pages 1 through 3. The following additional revisions have been made to the Proposal bid schedules:

- a. The following bid item descriptions have been revised:
  - Item 25, "INSTALL 24" BOX TREE [ACACIA ANEURA MULGA / PINUS ELDARICA TREES]
  - Item 37, "JUNCTION STRUCTURE (RFC&WCDS JS 227)"
- b. "Estimated Quantities" are revised from the following bid items:
  - Item 25, "INSTALL 24" BOX TREE" [ACACIA ANEURA MULGA / PINUS ELDARICA TREES]
  - Item 28, "MASONRY BLOCK WALL"
  - Item 61, Alternate Bid Items – Valley Sanitary District, Item 61, "8" SDR 35 PVC SEWER PIPE"
- c. The following bid items have been added:
  - Item 53.A, "MISCELLANEOUS DIRECTED WORK"
  - Item 64.A, Alternate Bid Items – Valley Sanitary District, Item 64.A, "ADJUST 8" PVC SEWER PIPE"
  - Item 64.B, Alternate Bid Items – Valley Sanitary District, Item 64.B, "REMOVE AND REPLACE 8" x 6" SDR 35 PVC WYE"

**Item 4: Revision of Encroachment Permit.** Refer to section "ENCROACHMENT PERMIT" on page 60. The first paragraph is deleted and replaced with the following:

"It shall be the responsibility of the Contractor to obtain an encroachment permit for the work done within the City of Indio Right-Of-Way. The Encroachment Permit from the City is free of charge to the Contractor."

**Item 5: Revision of Minor Concrete (Masonry Block Wall).** Refer to section "MINOR CONCRETE (MASONRY BLOCK WALL)" on page 95. The following paragraph is added after the first paragraph:

"The masonry block shall be split face and tan in color to closely match the existing block wall on the site. The Contractor shall submit a sample of the split face block and obtain the Engineer's approval prior to installation."

Additionally, the last paragraph is deleted and replaced with the following:

"The contract unit bid price paid per square foot for Masonry Block Wall shall include full compensation for furnishing all labor, materials, tools and equipment, and doing all the work involved in the complete structure including the concrete paving (4" thick), structure excavation and backfill, furnishing and placing reinforcement, submittal of block sample for Engineer's approval prior to installation and no additional compensation will be allowed therefor."

**Item 6: Revision of Tubular Handrailing.** Refer to section "TUBULAR HANDRAILING" on page 102. The following paragraph is added after the first paragraph:

"The handrailing shall be painted to match the color of the fencing and railing around the remainder of the site. The Contractor shall provide a color sample to the Engineer for approval prior to initiation of the painting process. Application of paint materials to the handrailing shall conform to Section 59 of the Standard Specifications."

Additionally, the last paragraph is deleted and replaced with the following:

"The contract unit bid price paid per linear foot for Tubular Handrailing shall include full compensation for all labor, materials, tools, equipment, and incidentals, submittal of color sample for Engineer's approval prior to painting, and for doing all the work involved and complete in place on top of the masonry retaining wall as shown on the plans and no additional compensation will be allowed therefor."

**Item 7:**        **Revision of Box Tree.** Refer to section "BOX TREE" on page 102. The first paragraph is deleted and replaced with the following:

"Box trees shall be 24" box trees [Acacia Aneura Mulga (first choice) or Pinus Eldarica trees (second choice)], and shall be located and planted as directed by the Engineer on the Lyndon B. Johnson Elementary School site."

Additionally, the fifth paragraph is deleted and replaced with the following:

"The Contractor shall be responsible for the relocation of the irrigation systems encountered within the planting areas of the trees."

Additionally, the last paragraph is deleted and replaced with the following:

"The contract unit bid price paid per each for Box Tree shall include full compensation for furnishing all labor, tools, materials, equipment, and incidentals, and for doing all the work required and complete in place including the furnishing and installation of the tree support poles, relocation of encountered irrigation systems, restore the planting areas to the original as directed by the Engineer and no additional compensation will be allowed therefor."

**Item 8:**        **Sanitary Sewer.** Refer to section "SANITARY SEWER" on page 107. The following Special Provisions are added hereby:

No adjustment in compensation will be allowed for changes in the total quantity of any of sewer bid items. If the total quantity exceed 125% of the quantity or are less than 75% of the quantity indicated in the Proposal Bid Schedule for sewer construction items, the respective unit prices will not be adjusted pursuant to Section 4-1.03B "Increased or Decreased Quantities" of the Standard Specifications.

All connections between the existing VCP and the new PVC sewer line shall be made with a Fernco Strong Back Repair Coupling or Valley Sanitary approved equal.

All relocated and new sewer cleanout shall be placed at the street right of way line.

At 81-500 Clinton Street Station 11+68 and 44-800 Clinton Street Station 16+32, the Contractor shall locate and replace the existing 8" wye with an 8"x6" SDR 35 PVC Wye. The Contractor shall verify the size of the lateral prior to the start of the removal existing wye. The connections between the existing VCP and the new PVC sewer line shall be made with a Fernco Strong Back Repair Coupling or Valley Sanitary approved equal. All bends, joints, and lateral replacement to make the wye connection shall be considered incidental to the contract unit price paid per each and shall include full compensation for furnishing all labor, materials, tools and equipment and for doing all work involved in excavation,

proper bedding, compaction, placement of the wye, backfill, fittings, proper disposal of the old materials, and no additional compensation will be allowed therefor.

Along Clinton Street between Station 25+92 to 26+72 (Sewer Manhole), the Contractor shall replace 80 linear feet of the damaged 8" VCP with 8" SDR 35 PVC pipe. The connections between the existing VCP and the new PVC sewer line shall be made with a Fernco Strong Back Repair Coupling or Valley Sanitary approved equal. This replacement pipe length shall be laid back at a uniform grade from the upstream to the downstream point of connection. Removal and placement of a new 8" sewer main shall include full compensation for furnishing all labor, materials, tools and equipment and for doing all work involved in excavation, removal and proper disposal of the existing pipe, proper bedding, compaction, placement of the new 8" PVC pipe, backfill, fittings and no additional compensation will be allowed therefor.

Along Clinton Street between approximate Station 36+64 to 36+84, the Contractor shall adjust approximately 20 linear feet of depressed 8" PVC. The Contractor shall salvage the existing PVC pipe, prepare the subgrade to the proper straight line grade from each point of connection, and re-lay the PVC pipe at a uniform grade from the upstream to the downstream. Full compensation for adjustment of the sewer main shall be paid for by the lineal foot and shall include full compensation for furnishing all labor, materials, tools and equipment and for doing all work involved in excavation, salvaging the existing PVC pipe, subgrade preparation, proper bedding, compaction, placement of the 8" PVC pipe, backfill, fittings and no additional compensation will be allowed therefor.

**Item 9:** The following drawing standard is included as **Attachment "C"**, which is made a part hereof:

- CALTRANS, RETAINING WALL TYPE 6, STD PLAN B3-11

**Item 10: Miscellaneous Directed Work.** The following Special Provisions are added hereby:


Miscellaneous Directed Work shall consist of necessary work that is not included in other contract bid items, as determined by the Engineer. Miscellaneous Directed Work shall be performed as directed by the engineer and in accordance with the applicable standards and specifications.

Full compensation for implementing "Miscellaneous Directed Work" shall be made on a force account basis, in accordance with Section 9-1.03 of the Standard Specifications. The total accumulated costs for the Miscellaneous Directed Work shall not exceed the amount specified in the contract bid item, unless otherwise increased by change order.

Addendum No. 1  
Clinton Street In The City Of Indio And County Of Riverside  
Project No. B2-03892  
April 22, 2010  
Page 6 of 8

---


The addendum for Clinton Street in the City of Indio and County of Riverside has been prepared under the direction of the following registered Civil Engineer:

  
BRADLEY J. DONAIS, PE

4/22/10




**Recommended by:**



\_\_\_\_\_  
Cindi A. Wachi, PE  
County Project Manager

**Concurrence:**



\_\_\_\_\_  
Khalid Nasim, PE  
Engineering Division Manager

**Acknowledged:**



\_\_\_\_\_  
(Contractor)

Date: 4/28/10

**ATTACHMENTS**

**A** – Revised “**MASONRY RETAINING WALL**”, Sheet 17 of 24

**B** – Revised Proposal


**C** – CALTRANS, RETAINING WALL TYPE 6 STD PLAN No. B3-11







DATE: 11/10/10  
 DRAWN: J. W. W.  
 CHECKED: J. W. W.

**CONSTRUCTION NOTES**

1. PROJECT IN PLACE
2. CONSTRUCT MASONRY RETAINING WALL FOR CALTRANS IN A 14' WIDE CONCRETE PAVING PER SECTION A-A
3. INSTALL 2" DIA. TREE AS DIRECTED BY THE ENGINEER
4. INSTALL 4" WHEEL STOP PER DETAIL B-1000
5. INSTALL TYPE A WALL, PER SPEC. STD. 100-2



**3\"/>**

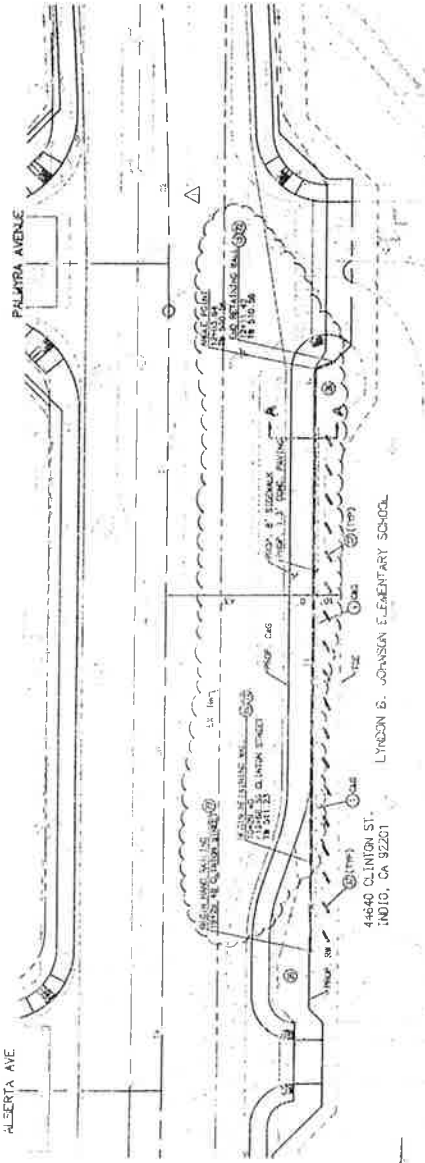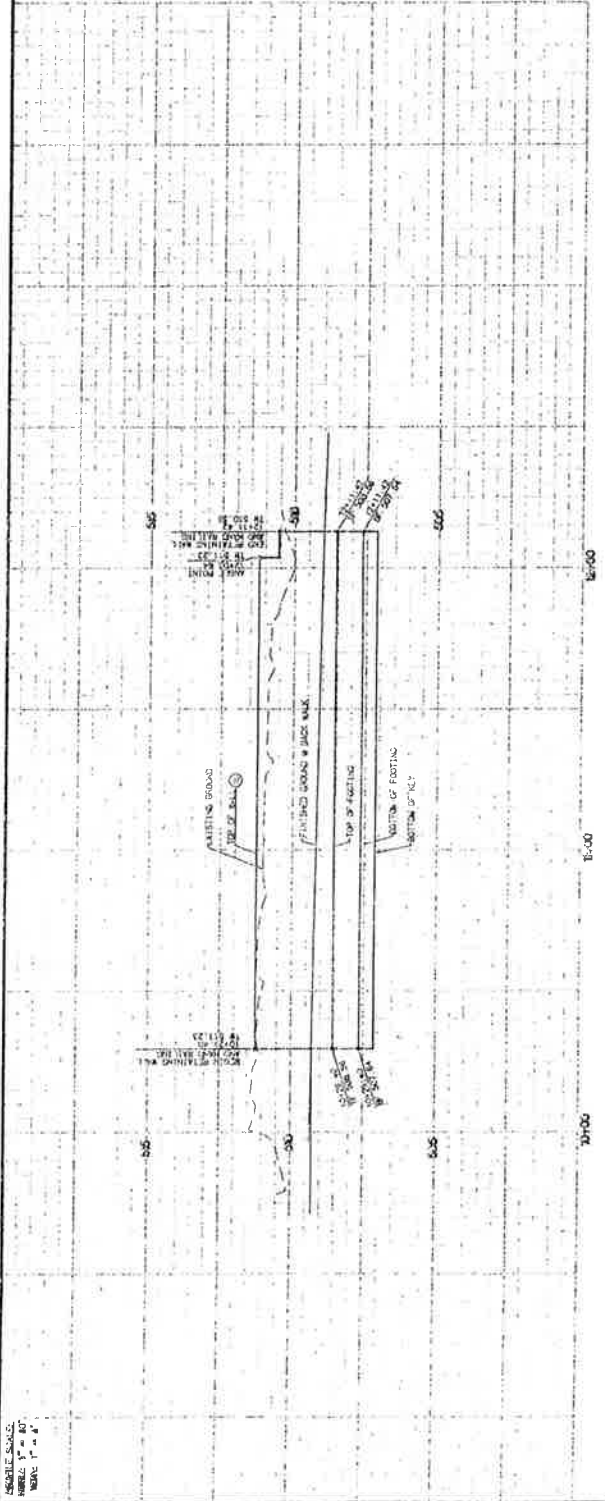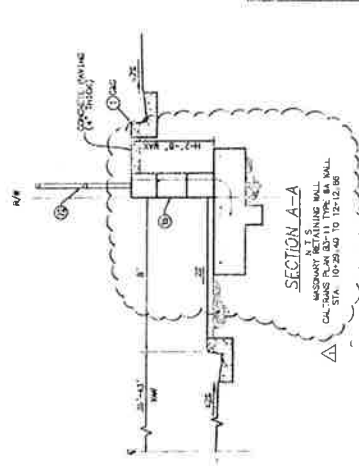

**CLINTON STREET**



<p>44640 CLINTON ST.          10010, CA 92201</p> <p>LYNDEN B. JOHNSON ELEMENTARY SCHOOL</p>	<p>CLINTON STREET          COUNTY OF RIVERSIDE</p>	<p>CLINTON STREET WIDENING PROJECT</p>
<p>DATE: 11/10/10</p> <p>PROJECT: CLINTON STREET WIDENING PROJECT</p>	<p>DESIGNED BY: J. W. W.</p> <p>CHECKED BY: J. W. W.</p>	<p>DATE: 11/10/10</p> <p>PROJECT: CLINTON STREET WIDENING PROJECT</p>
<p>PROJECT: CLINTON STREET WIDENING PROJECT</p>	<p>PROJECT: CLINTON STREET WIDENING PROJECT</p>	<p>PROJECT: CLINTON STREET WIDENING PROJECT</p>
<p>PROJECT: CLINTON STREET WIDENING PROJECT</p>	<p>PROJECT: CLINTON STREET WIDENING PROJECT</p>	<p>PROJECT: CLINTON STREET WIDENING PROJECT</p>



## Company Profile

# FIDELITY AND DEPOSIT COMPANY OF MARYLAND

1400 AMERICAN LANE, 19TH FLOOR TOWER 1  
SCHUAMBURG, IL 60196-1056  
800-382-2150

### Agent for Service of Process

KAREN HARRIS, 2730 GATEWAY OAKS DRIVE SUITE 100 SACRAMENTO, CA 95833

Unable to Locate the Agent for Service of Process?

---

### Reference Information

NAIC #:	39306
NAIC Group #:	<u>0212</u>
California Company ID #:	2479-4
Date authorized in California:	January 01, 1982
License Status:	UNLIMITED-NORMAL
Company Type:	Property & Casualty
State of Domicile:	MARYLAND

---

### Lines of Insurance Authorized to Transact

The company is authorized to transact business within these lines of insurance. For an explanation of any of these terms, please refer to the [glossary](#).

AIRCRAFT  
AUTOMOBILE  
BOILER AND MACHINERY  
BURGLARY  
CREDIT  
FIRE  
LIABILITY  
MARINE  
MISCELLANEOUS  
PLATE GLASS  
SPRINKLER  
SURETY  
TEAM AND VEHICLE  
WORKERS' COMPENSATION

---
